

FIELD REPORT

Project: Serenity Amenity Client: TriPointe Date: 03/03/26
 City: Fuquay Forman: Austin Contractor: Inland
 Temperature: 54 Weather Conditions: Cloudy Number of Trips: 3
 Personnel: Austin G Notified Austin of Inland of results
 1st Trip Arrived: 8:30 am Left: 9:00 am 2nd Trip Arrived: 9:30 am Left: 10:30 am


REMARKS

TME personnel arrived on site as requested by contractor. Austin from Inland was on site. Tech observed contractor pour grout in CMU walls. Tech sampled grout and tested for slump and air %. Tech created grout sampling forms for grout to setup. Tech will return the following day to transport grout to lab for testing once cured. Tech was informed prior to pour, that concrete pour would occur, not grout. Upon truck arrival, tech notified Austin with Inland that grout was to be poured from trucks, not concrete. Due to unexpected change of material, setup of test area took additional time. 3rd trip 11:00-12:30.



Signature: *Austin Gorth*

TME's presence on site is to perform specific services limited to that scheduled by others based on the understanding of our agreement with our client. This report is not an acceptance or approval of site activities. Test results and inspections are representative of our observations only while onsite at that specific time and location and may vary at other locations. The frequency of testing is based on timely scheduling of work by others and properly conveying progress of work in progress. At no time will TME be responsible for Safety considerations for other parties on the site.



CONCRETE FIELD REPORT

Project: Serenity Amenity Client: TriPointe Date: 03/03/26
 City: Fuquay Arrived On-Site: 8:30 am Left Site: 9:00 am
 Temperature: 54 Weather Conditions: Cloudy Number of Trips: 3
 Material(s) Tested: Slab Foundation Wall Masonry Other: _____
 Personnel: Austin G Notified Austin of Inland of results
 Concrete Supplier: Thomas Concrete Specified Strength: 3,000 psi Specified Slump: 9.0 inches
 Concrete Strength on ticket: 3,000 psi

TEST DATA

Truck No.	Batch Time	Plant No.	Ticket No.	Size of Load	Sample	Slump (in)	Air %	Unit Wt. (pcf)	H2O Added (gallons)	Concrete Temp.	No. of Test Samples	Daily Set No.
1,770	11:15	505	667327	5.00	11:45	10.0	1.00		10.00	59	4	1

Daily Set No.	Sample Type	Specified Strength	Detailed Location
1	Grout	3,000 psi	CMU walls at pool
		psi	
		psi	
		psi	
		psi	
		psi	


The above report is the field rendition of the author only and subject to review

FIELD REPORT ATTACHMENTS


Project: **Serenity Amenity**

Client: **TriPointe**

Date: **03/03/26**

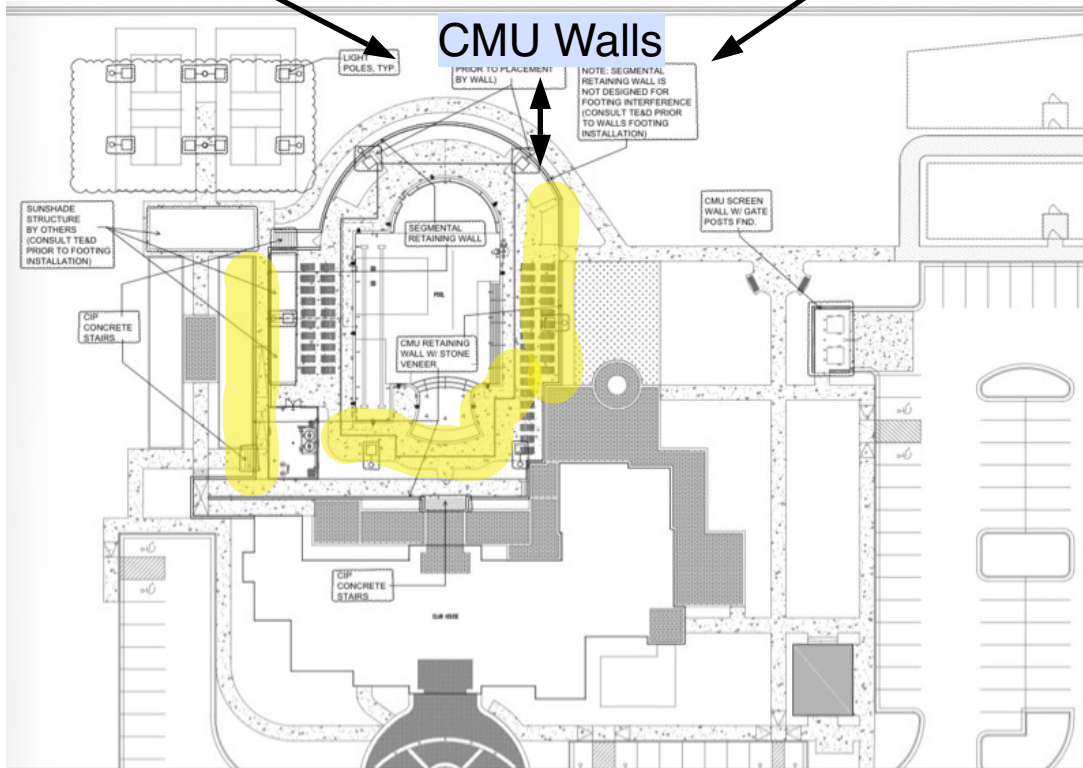


All locations should be considered approximate and were not surveyed.



FIELD REPORT ATTACHMENTS

Project: Serenity Amenity Client: TriPointe Date: 03/03/26

Truck ticket



ISO 9001 Certified
ISO 14001 Certified


GEORGIA 770-431-3300
SOUTH CAROLINA 864-225-1070
RALEIGH 919-832-0451
CHARLOTTE 704-333-0390
COASTAL 912-330-8990

CAUTION
May cause eye or skin injury. Contains Portland cement. Freshly mixed cement, mortar, concrete, or grout may cause skin injury.
TAKE THESE PRECAUTIONS:
1. Avoid all contact with eyes.
2. Wear rubber boots and gloves, and avoid prolonged contact directly with skin or through porous materials.
3. In case of contact with skin or eyes, FLUSH THOROUGHLY WITH WATER.
4. If irritation persists, get medical attention promptly.
5. Keep children away.
6. DO NOT STAND BEHIND TRUCK WHEN BACKING.

In the event of delivery beyond curbside, the company will not assume damages to property. Wrecker/Tow Truck charges are the responsibility of customer when required. Our concrete strength guarantees per ASTM C94 will not be effective unless the field sampling has been done per ASTM C172 and ASTM C31 and unless the laboratory testing fully complies with ASTM C39 and ASTM C1077.
A service charge of 1% per month (12% per year) will be charged on all invoices over 30 days old. Purchases will be responsible for Attorney fees and any other collection costs. Title and risk of loss of the ready mixed concrete passes to the purchaser when loaded into the truck at the plant.

Water Added at Customer Request Gallons: _____	Maximum Allowable Water Gallons: _____	Test Cylinder <input type="checkbox"/> YES <input type="checkbox"/> NO	Received in Good Order By: _____ TIME _____ : _____ A P	*By adding water or any other material to this load of concrete I acknowledge that the specified strength and other properties may be reduced significantly. I assume full responsibility for this reduction.*	
---	---	---	---	--	--

Customer # 452164	P.O. Number/Ordered By	Zone	Job Number	Time Batched	Date	Ticket
PINNACLE MASONRY, INC.					03-03-2026	667327



667327

SERINITY 325 stream side tearace					County	4044	
					WAKE COUNTY		
Quantity This Load	Quantity Ordered	Quantity Delivered	Product Code	Product Description	Unit of Measure	Unit Price	Extended Price
5.00	15.00	15.00	309GT78	3000 ASTM GROUT	cy		
1.00		1.00	8100	PER LOAD ENVIR.	ea		
1.00		1.00	8500	FUEL CHARGE	ea		

THOMAGREEN FIBERTRON

DELIVERY INSTRUCTIONS

PREVIOUS TRUCK 2188

Track # 1770	Plant # 505	Slump 9	Use of Concrete COMMERCIAL	Driver's Name -BUMPASS, TIMOTHY	MAR3 11:15AM
Callout All Est. Plan	Super Plass.				

WRECKER CHARGE
YES NO

MAKE EVERY TRIP A SAFE TRIP

LOAD TOTAL	
SUB TOTAL	
TAX	
TOTAL	

All locations should be considered approximate and were not surveyed.
