

SCANNED
8/16/10
DATE

ADDRESS : 275 COBBLESTONE DR SUBDIV: STONE CROSS
CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
OWNER : CHARNETZKY CUSTOM HOMES PHONE :
PARCEL : 01-0535-14- -0100- -11-
APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)
DIRECTIONS : HWY 210 S TOWARD SPRING LAKE TAKE RIGHT
ON RAY RD TURN RIGHT ON OVERHILLS RD
TURN LEFT INTO STONECROSS LOT 36 JB

STRUCTURE: 000 000 54X52 4BDR
FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 4.00 PROPOSED USE : SFD
SEPTIC - EXISTING? : NEW

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	5/26/10 5/25/10	RD CA	R*BLDG FOOTING / TEMP SVC POLE VRU #: 001932417 T/S: 05/25/2010 04:33 PM RDCONTE ----- CUTOMER ROLLED TO 5/27/10
B101 02	5/27/10 <i>S-27-10</i>	TI <i>AP JV</i>	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 001932789 T/S: 05/25/2010 04:33 PM RDCONTE ----- <i>T-pole passed</i>
----- COMMENTS AND NOTES -----			

ADDRESS : 275 COBBLESTONE DR SUBDIV: STONE CROSS
CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
OWNER : CHARNETZKY CUSTOM HOMES PHONE :
PARCEL : 01-0535-14- -0100- -11-
APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

DIRECTIONS : HWY 210 S TOWARD SPRING LAKE TAKE RIGHT
ON RAY RD TURN RIGHT ON OVERHILLS RD
TURN LEFT INTO STONECROSS LOT 36 JB

STRUCTURE: 000 000 54X52 4BDR
FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 4.00 PROPOSED USE : SFD
SEPTIC - EXISTING? : NEW

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	5/26/10 5/25/10	RD CA	R*BLDG FOOTING / TEMP SVC POLE VRU #: 001932417 T/S: 05/25/2010 04:33 PM RDCONTE ----- CUTOMER ROLLED TO 5/27/10
B101 02	5/27/10 5/27/10	JH AP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 001932789 T/S: 05/25/2010 04:33 PM RDCONTE ----- t-pole passed -----
A814 01	6/01/10	TI	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 001934033 T/S: 05/27/2010 02:25 PM RDCONTE -----
B111 01	6/02/10 6/02/10	JH CA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935196 T/S: 06/01/2010 12:23 PM DJOHNSON ----- TOM SCHNECKSKY ASKING FOR BASEMENT SLAB INSPECTION. T/S: 06/02/2010 08:18 AM DJOHNSON ----- HAD TO CANCEL SLAB INSPECTION PER JIMMY BECAUSE THE WHOLE BASEMENT IS THE COMPLETE HOUSE AND THE CUSTOMER NEEDS A FOUNDATION FIRST BEFORE SLAB.
B103 01	6/04/10 <u>6-4-10</u>	TI <u>DA JH</u>	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001935642 T/S: 06/02/2010 12:34 PM DJOHNSON ----- T/S: 06/03/2010 09:00 AM NTART -----
B111 02	6/04/10 <u>6-4-10</u>	TI <u>DA JW</u>	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935691 T/S: 06/02/2010 12:39 PM VBROWN ----- CUSTOMER CALLED PER KEN. T/S: 06/03/2010 09:00 AM NTART -----

----- COMMENTS AND NOTES -----

VIOLATION NOTICE

DO NOT REMOVE!

Harnett County Inspection Department

108 East Front Street • P.O. Box 65

Lillington, NC 27546

Phone: (910) 893-7525 Ext. 1 • Fax: (910) 893-2793

Job Name: Charnitzky Custom Homes Date: 6-4-10

Address: 275 Cobblestone Dr

Lot No.: 36 Permit No.: 06-50015114

(Check Box for Violation)

- | | | | | | | | |
|-------------------------------------|--|----------------------------------|--|-------------------------------------|---------------------------------------|---------------------------------|--------------------------------------|
| <input type="checkbox"/> Footing | <input checked="" type="checkbox"/> Foundation | <input type="checkbox"/> Bldg. | <input type="checkbox"/> Elec. | <input type="checkbox"/> Plumb. | <input type="checkbox"/> Mech. | <input type="checkbox"/> Insul. | <input type="checkbox"/> Floor Fram. |
| <input type="checkbox"/> Floor Slab | <input type="checkbox"/> MFG. Home | <input type="checkbox"/> Modular | <input type="checkbox"/> Damp/Water Proof. | <input type="checkbox"/> Structural | <input type="checkbox"/> Wall Sheath. | <input type="checkbox"/> Other | |

Violations Found: Foundation wall does not have projection on inside of foundation wall to right of garage. ~~Red ink~~ is marked on plans in red ink

Code Enforcement Official

Signature: James J Hall Date: 6-4-10

It is unlawful for any subcontractor, general contractor, or owner to cover or cause to be covered any part of the work with flooring, sheetrock, earth or other material until the proper inspector had ample time to approve the installation

ADDRESS : 275 COBBLESTONE DR SUBDIV: STONE CROSS
CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
OWNER : CHARNETZKY CUSTOM HOMES PHONE :
PARCEL : 01-0535-14- -0100- -11-
APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

DIRECTIONS : HWY 210 S TOWARD SPRING LAKE TAKE RIGHT
ON RAY RD TURN RIGHT ON OVERHILLS RD
TURN LEFT INTO STONECROSS LOT 36 CB

STRUCTURE: 000 000 54X52 4BDR

FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 4.00 PROPOSED USE : SFD
SEPTIC - EXISTING? : NEW

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	5/26/10 5/25/10	RD CA	R*BLDG FOOTING / TEMP SVC POLE VRU #: 001932417 T/S: 05/25/2010 04:33 PM RDCONTE CUTOMER ROLLED TO 5/27/10
B101 02	5/27/10 5/27/10	JH AP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 001932789 T/S: 05/25/2010 04:33 PM RDCONTE t-pole passed
A814 01	6/01/10	TI	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 001934033 T/S: 05/27/2010 02:25 PM RDCONTE
B111 01	6/02/10 6/02/10	JH CA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935196 T/S: 06/01/2010 12:23 PM DJOHNSON TOM SCHNECKSKY ASKING FOR BASEMENT SLAB INSPECTION. T/S: 06/02/2010 08:18 AM DJOHNSON HAD TO CANCEL SLAB INSPECTION PER JIMMY BECAUSE THE WHOLE BASEMENT IS THE COMPLETE HOUSE AND THE CUSTOMER NEEDS A FOUNDATION FIRST BEFORE SLAB.
B103 01	6/04/10 6/04/10	JH DA	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001935642 T/S: 06/02/2010 12:34 PM DJOHNSON T/S: 06/03/2010 09:00 AM NTART Foundation wall does not have projection on inside of foundation wall to right of garage, Area is marked in red ink on plans.
B111 02	6/04/10 6/04/10	JH DA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935691 T/S: 06/02/2010 12:39 PM VBROWN CUSTOMER CALLED PER KEN. T/S: 06/03/2010 09:00 AM NTART Foundation wall does not have projection on inside of foundation wall to right of garage, Area is marked in red ink on plans.
B103 02	6/14/10 <u>6/14/10</u>	TI <u>AP DR</u>	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001939909 T/S: 06/11/2010 10:38 AM VBROWN

COMMENTS AND NOTES

ADDRESS : 279 COBBLESTONE DR SUBDIV: STONE CROSS
CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
OWNER : CHARNETZKY CUSTOM HOMES PHONE :
PARCEL : 01-0535-14- -0100- -11-
APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

DIRECTIONS : HWY 210 S TOWARD SPRING LAKE TAKE RIGHT
ON RAY RD TURN RIGHT ON OVERHILLS RD
TURN LEFT INTO STONECROSS LOT 36 JB

STRUCTURE: 000 000 54X52 4BDR

FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 4.00 PROPOSED USE : SFD
SEPTIC - EXISTING? : NEW WATER SUPPLY : UNKNOWN

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	5/26/10 5/25/10	RD CA	R*BLDG FOOTING / TEMP SVC POLE VRU #: 001932417 T/S: 05/25/2010 04:33 PM RDCONTE ----- CUTOMER ROLLED TO 5/27/10
B101 02	5/27/10 5/27/10	JH AP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 001932789 T/S: 05/25/2010 04:33 PM RDCONTE ----- t-pole passed -----
A814 01	6/01/10 6/14/10	TW AP	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 001934033 T/S: 05/27/2010 02:25 PM RDCONTE ----- 279 COBBLESTONE DR LOT 36R SPRING LAKE 28390 T/S: 06/14/2010 11:17 AM TWARD -----
B111 01	6/02/10 6/02/10	JH CA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935196 T/S: 06/01/2010 12:23 PM DJOHNSON ----- TOM SCHNECKSKY ASKING FOR BASEMENT SLAB INSPECTION. T/S: 06/02/2010 08:18 AM DJOHNSON ----- HAD TO CANCEL SLAB INSPECTION PER JIMMY BECAUSE THE WHOLE BASEMENT IS THE COMPLETE HOUSE AND THE CUSTOMER NEEDS A FOUNDATION FIRST BEFORE SLAB.
B103 01	6/04/10 6/04/10	JH DA	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001935642 T/S: 06/02/2010 12:34 PM DJOHNSON ----- T/S: 06/03/2010 09:00 AM NTART ----- Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in rel inkon plans.
B111 02	6/04/10 6/04/10	JH DA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935691 T/S: 06/02/2010 12:39 PM VBROWN ----- CUSTOMER CALLED PER KEN. T/S: 06/03/2010 09:00 AM NTART ----- Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in rel inkon plans.
B103 02	6/14/10 6/14/10	DT AP	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001939909 T/S: 06/11/2010 10:38 AM VBROWN -----
B105 01	6/14/10 <u>6/14/10</u>	TI <u>AP</u>	R*OPEN FLOOR TIME: 17:00 VRU #: 001940733 T/S: 06/14/2010 11:31 AM VBROWN -----

----- COMMENTS AND NOTES -----

ADDRESS : 279 COBBLESTONE DR SUBDIV: STONE CROSS
CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
OWNER : CHARNETZKY CUSTOM HOMES PHONE :
PARCEL : 01-0535-14- -0100- -11-
APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

DIRECTIONS : HWY 210 S TOWARD SPRING LAKE TAKE RIGHT
ON RAY RD TURN RIGHT ON OVERHILLS RD
TURN LEFT INTO STONECROSS LOT 36 JB

STRUCTURE: 000 000 54X52 4BDR

FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 4.00 PROPOSED USE : SFD
SEPTIC - EXISTING? : NEW WATER SUPPLY : UNKNOWN

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	5/26/10 5/25/10	RD CA	R*BLDG FOOTING / TEMP SVC POLE VRU #: 001932417 T/S: 05/25/2010 04:33 PM RDCONTE CUTOMER ROLLED TO 5/27/10
B101 02	5/27/10 5/27/10	JH AP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 001932789 T/S: 05/25/2010 04:33 PM RDCONTE t-pole passed
A814 01	6/01/10 6/14/10	TW AP	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 001934033 T/S: 05/27/2010 02:25 PM RDCONTE 279 COBBLESTONE DR LOT 36R SPRING LAKE 28390 T/S: 06/14/2010 11:17 AM TWARD
B111 01	6/02/10 6/02/10	JH CA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935196 T/S: 06/01/2010 12:23 PM DJOHNSON TOM SCHNECKSKY ASKING FOR BASEMENT SLAB INSPECTION. T/S: 06/02/2010 08:18 AM DJOHNSON HAD TO CANCEL SLAB INSPECTION PER JIMMY BECAUSE THE WHOLE BASEMENT IS THE COMPLETE HOUSE AND THE CUSTOMER NEEDS A FOUNDATION FIRST BEFORE SLAB.
B103 01	6/04/10 6/04/10	JH DA	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001935642 T/S: 06/02/2010 12:34 PM DJOHNSON T/S: 06/03/2010 09:00 AM NTART Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in red inkon plans.
B111 02	6/04/10 6/04/10	JH DA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935691 T/S: 06/02/2010 12:39 PM VBROWN CUSTOMER CALLED PER KEN. T/S: 06/03/2010 09:00 AM NTART Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in red inkon plans.
B103 02	6/14/10 6/14/10	DT AP	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001939909 T/S: 06/11/2010 10:38 AM VBROWN
B105 01	6/14/10 6/14/10	DT AP	R*OPEN FLOOR TIME: 17:00 VRU #: 001940733 T/S: 06/14/2010 11:31 AM VBROWN
B113 01	6/30/10 <u>6-30-10</u>	TI <u>APJD</u>	R*BLDG WATER/DAMP PROOFING TIME: 17:00 VRU #: 001948264 T/S: 06/30/2010 09:00 AM VBROWN

ADDRESS : 279 COBBLESTONE DR SUBDIV: STONE CROSS
CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
OWNER : CHARNETZKY CUSTOM HOMES PHONE :
PARCEL : 01-0535-14- -0100- -11-
APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
R427 01	6/30/10 6/30/10	VC CA	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001947303 T/S: 06/29/2010 12:39 PM VBROWN ----- T/S: 06/30/2010 08:56 AM VBROWN ----- CUSTOMER CAN INSP WAS NOT READY WILL DO 4 TRADE ROUGH IN FOR 7-1-10. PUTTING ON WATER PROOFING FOR 6-30-10.

----- COMMENTS AND NOTES -----

ADDRESS : 279 COBBLESTONE DR SUBDIV: STONE CROSS
CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
OWNER : CHARNETZKY CUSTOM HOMES PHONE :
PARCEL : 01-0535-14- -0100- -11-
APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

DIRECTIONS : HWY 210 S TOWARD SPRING LAKE TAKE RIGHT
ON RAY RD TURN RIGHT ON OVERHILLS RD
TURN LEFT INTO STONECROSS LOT 36 JB

STRUCTURE: 000 000 54X52 4BDR

FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 4.00 PROPOSED USE : SFD
SEPTIC - EXISTING? : NEW WATER SUPPLY : UNKNOWN

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	5/26/10 5/25/10	RD CA	R*BLDG FOOTING / TEMP SVC POLE VRU #: 001932417 T/S: 05/25/2010 04:33 PM RDCONTE ----- CUTOMER ROLLED TO 5/27/10
B101 02	5/27/10 5/27/10	JH AP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 001932789 T/S: 05/25/2010 04:33 PM RDCONTE ----- t-pole passed -----
A814 01	6/01/10 6/14/10	TW AP	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 001934033 T/S: 05/27/2010 02:25 PM RDCONTE ----- 279 COBBLESTONE DR LOT 36R SPRING LAKE 28390 T/S: 06/14/2010 11:17 AM TWARD -----
B111 01	6/02/10 6/02/10	JH CA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935196 T/S: 06/01/2010 12:23 PM DJOHNSON ----- TOM SCHNECKSKY ASKING FOR BASEMENT SLAB INSPECTION. T/S: 06/02/2010 08:18 AM DJOHNSON ----- HAD TO CANCEL SLAB INSPECTION PER JIMMY BECAUSE THE WHOLE BASEMENT IS THE COMPLETE HOUSE AND THE CUSTOMER NEEDS A FOUNDATION FIRST BEFORE SLAB.
B103 01	6/04/10 6/04/10	JH DA	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001935642 T/S: 06/02/2010 12:34 PM DJOHNSON ----- T/S: 06/03/2010 09:00 AM NTART ----- Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in red inkon plans.
B111 02	6/04/10 6/04/10	JH DA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935691 T/S: 06/02/2010 12:39 PM VBROWN ----- CUSTOMER CALLED PER KEN. T/S: 06/03/2010 09:00 AM NTART ----- Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in red inkon plans.
B103 02	6/14/10 6/14/10	DT AP	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001939909 T/S: 06/11/2010 10:38 AM VBROWN -----
B105 01	6/14/10 6/14/10	DT AP	R*OPEN FLOOR TIME: 17:00 VRU #: 001940733 T/S: 06/14/2010 11:31 AM VBROWN -----
B113 01	6/30/10 6/30/10	JH AP	R*BLDG WATER/DAMP PROOFING TIME: 17:00 VRU #: 001948264 T/S: 06/30/2010 09:00 AM VBROWN -----

CONTINUED ONTO NEXT PAGE

ADDRESS : 279 COBBLESTONE DR SUBDIV: STONE CROSS
 CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
 OWNER : CHARNETZKY CUSTOM HOMES PHONE :
 PARCEL : 01-0535-14- -0100- -11-
 APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
			water proofing inspection
R427 01	6/30/10	VC	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001947303
	6/30/10	CA	T/S: 06/29/2010 12:39 PM VBROWN ----- T/S: 06/30/2010 08:56 AM VBROWN ----- CUSTOMER CAN INSP WAS NOT READY WILL DO 4 TRADE ROUGH IN FOR 7-1-10. PUTTING ON WATER PROOFING FOR 6-30-10.
R427 02	7/01/10 <u>7-1-10</u>	TI <i>DA JH</i>	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001948356 T/S: 06/30/2010 08:59 AM VBROWN ----- <i>Do not insulate</i>
			COMMENTS AND NOTES

VIOLATION NOTICE

DO NOT REMOVE!

Harnett County Inspection Department

108 East Front Street • P.O. Box 65

Lillington, NC 27546

Phone: (910) 893-7525 Ext. 1 • Fax: (910) 893-2793

Job Name: Charnetzky Homes LLC Date: 7-1-10

Address: 279 Cobblestone Dr

Lot No.: 36B Permit No.: 06-50015114

(Check Box for Violation)

- | | | | | | | | |
|-------------------------------------|-------------------------------------|---|--|-------------------------------------|---------------------------------------|---------------------------------|--------------------------------------|
| <input type="checkbox"/> Footing | <input type="checkbox"/> Foundation | <input checked="" type="checkbox"/> Bldg. | <input type="checkbox"/> Elec. | <input type="checkbox"/> Plumb. | <input type="checkbox"/> Mech. | <input type="checkbox"/> Insul. | <input type="checkbox"/> Floor Fram. |
| <input type="checkbox"/> Floor Slab | <input type="checkbox"/> MFG. Home | <input type="checkbox"/> Modular | <input type="checkbox"/> Damp/Water Proof. | <input type="checkbox"/> Structural | <input type="checkbox"/> Wall Sheath. | <input type="checkbox"/> Other | |

Violations Found: ① Nail all holes on anchor straps & need paper work on & stance for straps
② Need paper work for LVLs in garage and in kitchen roots.
③ Missing 2 studs in kitchen under beam @ stairs
④ missing collar ties on rafters
⑤ 4' Header on double windows in basement need 2 feet studs on each side
⑥ Fire Caution main electrical with a tap plate in basement.

Code Enforcement Official

Signature: James T. Hill Date: 7-1-10

It is unlawful for any subcontractor, general contractor, or owner to cover or cause to be covered any part of the work with flooring, sheetrock, earth or other material until the proper inspector had ample time to approve the installation

WHITE COPY - CONTRACTOR/OWNER

YELLOW COPY - INSPECTORS

ADDRESS : 279 COBBLESTONE DR SUBDIV: STONE CROSS
CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
OWNER : CHARNETZKY CUSTOM HOMES PHONE :
PARCEL : 01-0535-14- -0100- -11-
APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

DIRECTIONS : HWY 210 S TOWARD SPRING LAKE TAKE RIGHT
ON RAY RD TURN RIGHT ON OVERHILLS RD
TURN LEFT INTO STONECROSS LOT 36 JB

STRUCTURE: 000 000 54X52 4BDR

FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 4.00 PROPOSED USE : SFD
SEPTIC - EXISTING? : NEW WATER SUPPLY : UNKNOWN

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	5/26/10 5/25/10	RD CA	R*BLDG FOOTING / TEMP SVC POLE VRU #: 001932417 T/S: 05/25/2010 04:33 PM RDCONTE ----- CUTOMER ROLLED TO 5/27/10
B101 02	5/27/10 5/27/10	JH AP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 001932789 T/S: 05/25/2010 04:33 PM RDCONTE ----- t-pole passed -----
A814 01	6/01/10 6/14/10	TW AP	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 001934033 T/S: 05/27/2010 02:25 PM RDCONTE ----- 279 COBBLESTONE DR LOT 36R SPRING LAKE 28390 T/S: 06/14/2010 11:17 AM TWARD -----
B111 01	6/02/10 6/02/10	JH CA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935196 T/S: 06/01/2010 12:23 PM DJOHNSON ----- TOM SCHNECKSKY ASKING FOR BASEMENT SLAB INSPECTION. T/S: 06/02/2010 08:18 AM DJOHNSON ----- HAD TO CANCEL SLAB INSPECTION PER JIMMY BECAUSE THE WHOLE BASEMENT IS THE COMPLETE HOUSE AND THE CUSTOMER NEEDS A FOUNDATION FIRST BEFORE SLAB.
B103 01	6/04/10 6/04/10	JH DA	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001935642 T/S: 06/02/2010 12:34 PM DJOHNSON ----- T/S: 06/03/2010 09:00 AM NTART ----- Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in red inkon plans.
B111 02	6/04/10 6/04/10	JH DA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935691 T/S: 06/02/2010 12:39 PM VBROWN ----- CUSTOMER CALLED PER KEN. T/S: 06/03/2010 09:00 AM NTART ----- Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in red inkon plans.
B103 02	6/14/10 6/14/10	DT AP	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001939909 T/S: 06/11/2010 10:38 AM VBROWN -----
B105 01	6/14/10 6/14/10	DT AP	R*OPEN FLOOR TIME: 17:00 VRU #: 001940733 T/S: 06/14/2010 11:31 AM VBROWN -----
B113 01	6/30/10 6/30/10	JH AP	R*BLDG WATER/DAMP PROOFING TIME: 17:00 VRU #: 001948264 T/S: 06/30/2010 09:00 AM VBROWN -----

----- CONTINUED CNTO NEXT PAGE -----

ADDRESS : 279 COBBLESTONE DR SUBDIV: STONE CROSS
 CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
 OWNER : CHARNETZKY CUSTOM HOMES PHONE :
 PARCEL : 01-0535-14- -0100- -11-
 APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
			water proofing inspection
H824 01	6/30/10	OT	ENVIR. OPERATIONS PERMIT TIME: 17:00 VRU #: 001948885
	6/30/10	AP	T/S: 07/01/2010 08:45 AM SZIMMER
			T/S: 07/01/2010 08:46 AM SZIMMER
R427 01	6/30/10	VC	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001947803
	6/30/10	CA	T/S: 06/29/2010 12:39 PM VBROWN
			T/S: 06/30/2010 08:56 AM VBROWN
			CUSTOMER CAN INSP WAS NOT READY WILL DO 4 TRADE ROUGH IN FOR 7-1-10. PUTTING ON WATER PROOFING FOR 6-30-10.
R427 02	7/01/10	JH	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001948856
	7/01/10	DA	T/S: 06/30/2010 08:59 AM VBROWN
			1) Nail all holes on anchor straps & need paper work on distance for straps.
			2) Need paper work for LVLs in garage & kitchen nook.
			3) Missing 2 studs in kitchen under beam @ stairs.
			4) Missing collar ties on rafters.
			5) 4' headers on double windows in basement need 2 jack studson each side.
			6) Fire caulk electrical wire @ panel in basement @ top plate
I129 01	7/02/10	TI	R*INSULATION INSPECTION TIME: 17:00 VRU #: 001949128
	<u>7-2-10</u>	<u>APJH</u>	T/S: 07/01/2010 01:20 PM RDCONTE
			OK TO INSULATE PER INSPECTOR
R427 03	7/02/10	TI	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001949098
	<u>7-2-10</u>	<u>APJH</u>	T/S: 07/01/2010 01:20 PM RDCONTE

----- COMMENTS AND NOTES -----



FOUNDATION ANCHORS - FA3 & ST SERIES

Concrete & Masonry

FA3 - For installation into concrete slabs. The FA3 features a split flange for nailing to both mudsill and stud for greater framing versatility.


ST1-TZ - For installation into concrete slab or poured stemwalls. The ST1-TZ features a prebent base flange to assure proper anchoring into concrete. For concrete/masonry installations, refer to the **FA & ST Foundation Anchors Technical Bulletin**.

ST2-TZ - For installation into concrete slab, poured stemwalls or concrete/masonry. The ST2-TZ features a prebent base flange to assure proper anchoring into concrete. **Do not use in red clay brick.**

- Materials:** See chart
Finish: G90 galvanizing
Options: FA3 is available in Triple Zinc.
 To order, add TZ to end of stock number, as in **FA3-TZ**.
Codes: NER 530, FL822

Installation:


- Use all specified fasteners. See Product Notes, page 10.
- Use a minimum of two anchors per mudsill. An anchor should always be within 12" of the end of each mudsill section. Follow spacing guidelines in chart.
- Do not rely on these anchors to secure concrete sections together between cold joints.
- For FA3 insert into wet concrete (minimum strength of 2,000 psi). Place mudsill after concrete cures. Secure flanges to sill (and stud, if applicable), bending flanges as needed to achieve a tight fit. Fasten as directed in chart.
- For ST1-TZ and ST2-TZ spread sill flanges to mudsill width prior to insertion into wet concrete (minimum strength of 2,000 psi). Alternate installation is possible by inserting unbent flanges through 3/4" center hole predrilled in mudsill. Foundation anchors may also be attached to mudsill and then inserted into wet concrete. When installing ST2-TZ into concrete block, fill cells with grout with a minimum strength of 2,000 psi. Concrete block edges may need to be beveled to facilitate installation.
- For additional installation details and information on mudsill anchors refer to **ST Foundation Anchors Technical Bulletin**.
- ST2-TZ in masonry construction shall be installed in the core of the block and grouted with concrete grout designed for that purpose. In no case, shall they be installed in a mortar joint.




Typical ST1-TZ installation in concrete



Alternate ST1-TZ installation with 3/4" center hole



Alternate ST2-TZ installation with 3/4" center hole in mudsill




DO NOT install ST1-TZ and ST2-TZ without pre-bending sill flanges in "Y" configuration



ST1-TZ


Spread sill flanges to sill width prior to insertion into wet concrete




ST2-TZ

Plate Size	USP Stock No.	Ref. No.	Steel Gauge	Fastener Schedule ¹				Min. Embed. (E) ² (Inches)	Max. Spacing ³ (Feet)	Allowable Loads (Lbs.) ¹				Code Ref.
				Mudsill Top		Mudsill Side				DF-L / SP				
				Qty	Nail	Qty	Nail			F1	F2	F3	Uplift	
2 x 4 - 6	ST1-TZ	MAB15Z	18	4	8d x 1-1/2	4	8d x 1-1/2	8-1/2	5-1/2	585	745	745	825	L8, F16
	ST2-TZ	MAB23Z	18	4	8d x 1-1/2	4	8d x 1-1/2	16-1/2	5-1/2	585	745	745	825	


- 1) Allowable loads have been increased 60% for wind or seismic loads; no further increase shall be permitted.
- 2) 10d x 1-1/2 nails are 9 gauge (0.148" diameter) by 1-1/2" long. 8d x 1-1/2 nails are 11 gauge (0.131" diameter) by 1-1/2" long.
- 3) Anchor spacing and design loads assume treated Douglas Fir-Larch with Fc perpendicular @ 825 psi; rap:acc code prescribed 1/2" anchor bolt with standard washer, spaced 6 ft. on center.
- 4) If installed in the alternate configuration, the ST1-TZ shall be embedded 11" and ST2-TZ 16".
- 5) For ST1-TZ or ST2-TZ: Maximum spacing is 3 feet when using a 2 x 6 mudsill unless an alternate installation is used.

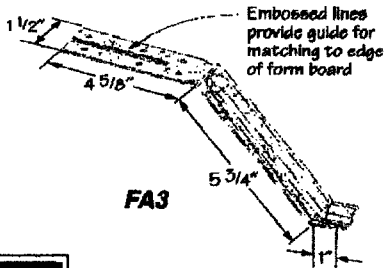


FA3



Alternate FA3 installation



Typical FA3 installation in concrete



Typical FA3 installation to mudsill and stud


continued on next page

© Copyright 2009 USP Structural Connectors

Project : **BEAM 2.FBD**
 Mark # : **Charnetzky Builders**
 Usage : **Beam (Roof)**
 Max Defl : **LL = L/240 TL = L/180**

36-R Stoncross - Appl #
Kitchen/Nook

Spacing (in.) : **0.0**
 Slope : **0/12**



LOADS

Project Design Loads : Roof: Live=30 psf, Dead=15 psf;

#	Shape	Live+Dead Ld(T)		Live Ld(L)		LDF	Location*		Additional Info
		@Start	@End	@Start	@End		Span#	Starts	
1	Uniform(plf)	383		255		115%	0	0' 0"	roof
	Uniform(plf)	9		0		0	0	13' 6"	Self Weight

*Dimensions measured from left end when span# is 0, otherwise, from left end of the specified span.

SUPPORTS(lbs)

	1	2	
Max R'n	2644	2644	
Max 115%	1723	1723	
Min R'n	921	921	
Min 115%	1723	1723	
DL R'n	921	921	
Min Brg(In.)	1.50	1.50	[Based on bearing stress below]
Brg Str(psi)	565	565	

DESIGN

	Value	Span	X	Group	Allow	LDF	Ratio	
V(lbs)	2285	1	12' 7"	31	7075	115%	0.32	
M(ft-lbs)	8925	1	6' 9"	31	14278	115%	0.63	
LtRn(lbs)	2644	0	0' 0"	31	6921		0.38	See Note #
RtRn(lbs)	2644	0	13' 6"	31	6921		0.38	See Note #
LLDefl(in.)	0.43	1	6' 9"	31	0.68		L/373	
TLDefl(in.)	0.67	1	6' 9"	31	0.90		L/243	

USE: **GPLAM 2.0E 1.75x 9.25" 2 Piles**
GP LAM tm Georgia-Pacific Wood Products, LLC

Grade, Depth selected by user


NOTES :

1. Designed in accordance with National Design Specifications for Wood Construction and applicable Approvals or Research Reports.
2. Provide full depth lateral support at all bearing locations. Allowable positive moment is calculated based on top edge with continuous lateral support.
3. Loads have been input by the user and have not been verified by Georgia-Pacific Wood Products LLC.
4. This reaction is based on the combination of loads & duration factors that produces the highest stress ratio and may be less than maximum reaction. Therefore, when reaction values are required, use Max R'n from 'Supports' section above.
5. Bearing length (Min Brg(In.)) based on allowable stress of support material (Brg Str(psi)); support material capacity shall be verified (by others).
6. Roof Usage: Install with minimum 1/4:12 slope for adequate drainage.
7. When required by the building code, a registered design professional or building official should verify the input loads and product application.
8. For beams with loads applied equally to both plies, either top or side loaded, nail plies together with 2 rows of 16d nails @ 12" o/c (one row 2" from top, one row 2" from bottom).
9. For beams with loads not applied equally to all plies, refer to Fastening Recommendations for Side-Loaded, Multiple-Piece Members in the GP Engineered Lumber Residential Floor & Roof Systems Product Guide.
10. Max/Min reactions are based on the applicable load combinations outlined in the notes. Summation of max/min reactions for various DOL may not match total max/min reaction.
11. Analysis valid for dry-use only (less than 16% moisture content).
12. Company, product or brand names referenced are trademarks or registered trademarks of their respective owners.
13. Load Combinations: 10= D, 20= D + 100%, 30= D + 115%, 40= D + 125%, 50= D + 133%, 60= D + 0.75(100%+115%), 70= D + 0.75*(100%+ 25%), 80= D + 0.75(100%+115%+133%), 90= D + 0.75(100%+125%+133%), 100= 0.6D + 133%, 110= D + Commercial Ld (100%), 120= D + 0.75(100%+133%)
14. Group = Load Combination Number + Load Pattern number. (For simple span, Load pattern = 1 for LL, 0 for DL).

Project : **BEAM 2.FBD**
 Mark # : **Charnetzky Builders1**
 Usage : **Beam (Roof)**
 Max Defl : **LL = L/240 TL = L/180**

36-R Stoncross - Appl #
Garage

Spacing (in.) : **0.0**
 Slope : **0/12**



LOADS Project Design Loads : Roof: Live=30 psf, Dead=15 psf;

#	Shape	Live+Dead Ld(T)		Live Ld(L)		LDF	Span#	Location*		Additional Info
		@Start	@End	@Start	@End			Starts	Ends	
1	Uniform(plf)	383		255		115% 0		0' 0"	18' 5"	roof
2	Uniform(plf)	425		283		115% 0		0' 0"	18' 5"	floor
3	Uniform(plf)	80		0		100% 0		0' 0"	18' 5"	wall
4	Uniform(plf)	113		75		115% 0		0' 0"	18' 5"	shed roof
	Uniform(plf)	23		0		0	0	0	18' 5"	Self Weight

*Dimensions measured from left end when span# is 0, otherwise, from left end of the specified span.

SUPPORTS(lbs)

	1	2	
Max R'n	9426	9426	
Max 115%	5654	5654	
Min R'n	3772	3772	
Min 115%	5654	5654	
DL R'n	3772	3772	
Min Brg(in.)	4.77	4.77	[Based on bearing stress below]
Brg Str(psi)	565	565	

DESIGN

	Value	Span	X	Group	Allow	LDF	Ratio	
V(lbs)	7134	1	16' 2"	31	18257	115%	0.39	
M(ft-lbs)	43399	1	9' 3"	31	85608	115%	0.51	
LtRn(lbs)	9426	0	0' 0"	31	11865		0.79	See Note #
RtRn(lbs)	9426	0	18' 5"	31	11865		0.79	See Note #
LLDefl(in.)	0.24	1	9' 3"	31	0.92		L/936	
TLDefl(in.)	0.39	1	9' 3"	31	1.23		L/562	

USE: **GPLAM 2.0E 1.75x23.88" 2 Piles**
GP LAM tm Georgia-Pacific Wood Products, LLC

Grade, Depth, Piles selected by user

NOTES :

1. Designed in accordance with National Design Specifications for Wood Construction and applicable Approvals or Research Reports.
2. Provide full depth lateral support at all bearing locations. Allowable positive moment is calculated based on top edge with continuous lateral support.
3. Loads have been input by the user and have not been verified by Georgia-Pacific Wood Products LLC.
4. This reaction is based on the combination of loads & duration factors that produces the highest stress ratio and may be less than maximum reaction. Therefore, when reaction values are required, use Max R'n from 'Supports' section above.
5. Bearing length (Min Brg(in.)) based on allowable stress of support material (Brg Str(psi)); support material capacity shall be verified (by others).
6. Roof Usage: Install with minimum 1/4:12 slope for adequate drainage.
7. When required by the building code, a registered design professional or building official should verify the input loads and product application.
8. For beams with loads applied equally to both plies, either top or side loaded, nail plies together with 3 rows of 16d nails @ 12" o/c (one row 2" from top, one row at mid-depth, one row 2" from bottom).
9. For beams with loads not applied equally to all plies, refer to Fastening Recommendations for Side-Loaded, Multiple-Piece Members in the GP Engineered Lumber Residential Floor & Roof Systems Product Guide.
10. Max/Min reactions are based on the applicable load combinations outlined in the notes. Summation of max/min reactions for various DOL may not match total max/min reaction.
11. Analysis valid for dry-use only (less than 16% moisture content).
12. Company, product or brand names referenced are trademarks or registered trademarks of their respective owners.
13. Load Combinations: 10= D, 20= D + 100%, 30= D + 115%, 40= D + 125%, 50= D + 133%, 60= D + 0.75(100%+115%), 70= D + 0.75(100%+ 25%), 80= D + 0.75(100%+115%+133%), 90= D + 0.75(100%+125%+133%), 100= 0.6D + 133%, 110= D + Commercial Ld (100%), 120= D + 0.75(100%+133%)
14. Group = Load Combination Number + Load Pattern number. (For simple span, Load pattern = 1 for LL, 0 for DL).

ADDRESS . . : 279 COBBLESTONE DR SUBDIV: STONE CROSS
CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
OWNER . . . : CHARNETZKY CUSTOM HOMES PHONE :
PARCEL . . . : 01-0535-14- -0100- -11-
APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

DIRECTIONS : HWY 210 S TOWARD SPRING LAKE TAKE RIGHT
ON RAY RD TURN RIGHT ON OVERHILLS RD
TURN LEFT INTO STONECROSS LOT 36 JB

STRUCTURE: 000 000 54X52 4BDR

FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 4.00 PROPOSED USE : SFD
SEPTIC - EXISTING? : NEW WATER SUPPLY : UNKNOWN

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	5/26/10 5/25/10	RD CA	R*BLDG FOOTING / TEMP SVC POLE VRU #: 001932417 T/S: 05/25/2010 04:33 PM RDCONTE ----- CUTOMER ROLLED TO 5/27/10
B101 02	5/27/10 5/27/10	JH AP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 001932789 T/S: 05/25/2010 04:33 PM RDCONTE ----- t-pole passed -----
A814 01	6/01/10 6/14/10	TW AP	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 001934033 T/S: 05/27/2010 02:25 PM RDCONTE ----- 279 COBBLESTONE DR LOT 36R SPRING LAKE 28390 T/S: 06/14/2010 11:17 AM TWARD -----
B111 01	6/02/10 6/02/10	JH CA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935196 T/S: 06/01/2010 12:23 PM DJOHNSON ----- TOM SCHNECKSKY ASKING FOR BASEMENT SLAB INSPECTION. T/S: 06/02/2010 08:18 AM DJOHNSON ----- HAD TO CANCEL SLAB INSPECTION PER JIMMY BECAUSE THE WHOLE BASEMENT IS THE COMPLETE HOUSE AND THE CUSTOMER NEEDS A FOUNDATION FIRST BEFORE SLAB.
B103 01	6/04/10 6/04/10	JH DA	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001935642 T/S: 06/02/2010 12:34 PM DJOHNSON ----- T/S: 06/03/2010 09:00 AM NTART ----- Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in red inkon plans.
B111 02	6/04/10 6/04/10	JH DA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935691 T/S: 06/02/2010 12:39 PM VBROWN ----- CUSTOMER CALLED PER KEN. T/S: 06/03/2010 09:00 AM NTART ----- Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in red inkon plans.
B103 02	6/14/10 6/14/10	DT AP	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001939909 T/S: 06/11/2010 10:38 AM VBROWN -----
B105 01	6/14/10 6/14/10	DT AP	R*OPEN FLOOR TIME: 17:00 VRU #: 001940733 T/S: 06/14/2010 11:31 AM VBROWN -----
B113 01	6/30/10 6/30/10	JH AP	R*BLDG WATER/DAMP PROOFING TIME: 17:00 VRU #: 001948264 T/S: 06/30/2010 09:00 AM VBROWN -----

----- CONTINUED ONTO NEXT PAGE -----

 ADDRESS : 279 COBBLESTONE DR SUBDIV: STONE CROSS
 CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
 OWNER : CHARNETZKY CUSTOM HOMES PHONE :
 PARCEL : 01-0535-14- -0100- -11-
 APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
			water proofing inspection
H824 01	6/30/10	OT	ENVIR. OPERATIONS PERMIT TIME: 17:00 VRU #: 00194885
	6/30/10	AP	T/S: 07/01/2010 08:45 AM SZIMMER
			T/S: 07/01/2010 08:46 AM SZIMMER
R427 01	6/30/10	VC	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001947803
	6/30/10	CA	T/S: 06/29/2010 12:39 PM VBROWN
			T/S: 06/30/2010 08:56 AM VBROWN
			CUSTOMER CAN INSP WAS NOT READY WILL DO 4 TRADE ROUGH IN FOR 7-1-10. PUTTING ON WATER PROOFING FOR 6-30-10.
R427 02	7/01/10	JH	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001948856
	7/01/10	DA	T/S: 06/30/2010 08:59 AM VBROWN
			1)Nail all holes on anchor straps & need paper work on distance for straps.
			2)Need paper wrk for LVLs in garage & kitchen nook.
			3)Missing 2 studs in kitchen under beam @ stairs.
			4)Missing collar ties on rafters.
			5)4' headers on double windows in basement need 2 jack studson each side.
			6)Fire caulk electrical wire @ panel in basement @ top plate
I129 01	7/02/10	JH	R*INSULATION INSPECTION TIME: 17:00 VRU #: 001949122
	7/02/10	AP	T/S: 07/01/2010 01:20 PM RDCONTE
			OK TO INSULATE PER INSPECTOR
R427 03	7/02/10	JH	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001949098
	7/02/10	AP	T/S: 07/01/2010 01:20 PM RDCONTE
R431 01	8/04/10	TI	FOUR TRADE FINAL >2500 VRU #: 001963438
	8-4-10	DA JH	

----- COMMENTS AND NOTES -----

VIOLATION NOTICE

DO NOT REMOVE!

Harnett County Inspection Department

108 East Front Street • P.O. Box 65

Lillington, NC 27546

Phone: (910) 893-7525 Ext. 1 • Fax: (910) 893-2793

Job Name: Charitablety instn Homes Date: 8-4-10

Address: 779 Cobblestone Dr

Lot No.: 36 Permit No.: 06-50015114

(Check Box for Violation)

- | | | | | | | | |
|-------------------------------------|-------------------------------------|---|--|--|---|---------------------------------|--------------------------------------|
| <input type="checkbox"/> Footing | <input type="checkbox"/> Foundation | <input checked="" type="checkbox"/> Bldg. | <input checked="" type="checkbox"/> Elec. | <input checked="" type="checkbox"/> Plumb. | <input checked="" type="checkbox"/> Mech. | <input type="checkbox"/> Insul. | <input type="checkbox"/> Floor Fram. |
| <input type="checkbox"/> Floor Slab | <input type="checkbox"/> MFG. Home | <input type="checkbox"/> Modular | <input type="checkbox"/> Damp/Water Proof. | <input type="checkbox"/> Structural | <input type="checkbox"/> Wall Sheath. | <input type="checkbox"/> Other | |

Violations Found: ① No House numbers ② Service cable from meter to panel in basement needs to be 4 wires and protected. ③ No earth tone installed. ④ need 24" walkway to attic in attic from top of stairs for attic access. ⑤ need weather strip around door to basement around door space ⑥ Missing ground bar at meter for cable & phone ⑦ 3" cover on sewer line in back of house.

Code Enforcement Official
Signature: James T. Bell Date: 8-4-10

It is unlawful for any subcontractor, general contractor, or owner to cover or cause to be covered any part of the work with flooring, sheetrock, earth or other material until the proper inspector had ample time to approve the installation

ADDRESS : 279 COBBLESTONE DR SUBDIV: STONE CROSS
CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
OWNER : CHARNETZKY CUSTOM HOMES PHONE :
PARCEL : 01-0535-14- -0100- -11-
APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

DIRECTIONS : HWY 210 S TOWARD SPRING LAKE TAKE RIGHT
ON RAY RD TURN RIGHT ON OVERHILLS RD
TURN LEFT INTO STONECROSS LOT 36 JB

STRUCTURE: 000 000 54X52 4BDR

FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 4.00 PROPOSED USE : SFD
SEPTIC - EXISTING? : NEW WATER SUPPLY : UNKNOWN

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	5/26/10 5/25/10	RD CA	R*BLDG FOOTING / TEMP SVC POLE VRU #: 001932417 T/S: 05/25/2010 04:33 PM RDCONTE CUTOMER ROLLED TO 5/27/10
B101 02	5/27/10 5/27/10	JH AP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 001932789 T/S: 05/25/2010 04:33 PM RDCONTE t-pole passed
A814 01	6/01/10 6/14/10	TW AP	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 001934033 T/S: 05/27/2010 02:25 PM RDCONTE 279 COBBLESTONE DR LOT 36R SPRING LAKE 28390 T/S: 06/14/2010 11:17 AM TWARD
B111 01	6/02/10 6/02/10	JH CA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935196 T/S: 06/01/2010 12:23 PM DJOHNSON TOM SCHNECKSKY ASKING FOR BASEMENT SLAB INSPECTION. T/S: 06/02/2010 08:18 AM DJOHNSON HAD TO CANCEL SLAB INSPECTION PER JIMMY BECAUSE THE WHOLE BASEMENT IS THE COMPLETE HOUSE AND THE CUSTOMER NEEDS A FOUNDATION FIRST BEFORE SLAB.
B103 01	6/04/10 6/04/10	JH DA	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001935642 T/S: 06/02/2010 12:34 PM DJOHNSON T/S: 06/03/2010 09:00 AM NTART Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in rel inikon plans.
B111 02	6/04/10 6/04/10	JH DA	R*BLDG SLAB INSP TIME: 17:00 VRU #: 001935691 T/S: 06/02/2010 12:39 PM VBROWN CUSTOMER CALLED PER KEN. T/S: 06/03/2010 09:00 AM NTART Foundation wall does not have projection on inside of foundation wallto right of garage, Area is marked in rel inikon plans.
B103 02	6/14/10 6/14/10	DT AP	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 001939909 T/S: 06/11/2010 10:38 AM VBROWN
B105 01	6/14/10 6/14/10	DT AP	R*OPEN FLOOR TIME: 17:00 VRU #: 001940733 T/S: 06/14/2010 11:31 AM VBROWN
B113 01	6/30/10 6/30/10	JH AP	R*BLDG WATER/DAMP PROOFING TIME: 17:00 VRU #: 001943264 T/S: 06/30/2010 09:00 AM VBROWN

CONTINUED ONTO NEXT PAGE

ADDRESS : 279 COBBLESTONE DR SUBDIV: STONE CROSS
 CONTRACTOR : CHARNETZKY CUSTOM HOMES LLC PHONE : (252) 478-4045
 OWNER : CHARNETZKY CUSTOM HOMES PHONE :
 PARCEL : 01-0535-14- -0100- -11-
 APPL NUMBER: 06-50015114 CP NEW RESIDENTIAL (SFD)

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
H824 01	6/30/10 6/30/10	OT AP	water proofing inspection ENVIR. OPERATIONS PERMIT TIME: 17:00 VRU #: 001948885 T/S: 07/01/2010 08:45 AM SZIMMER T/S: 07/01/2010 08:46 AM SZIMMER
R427 01	6/30/10 6/30/10	VC CA	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001947803 T/S: 06/29/2010 12:39 PM VBROWN T/S: 06/30/2010 08:56 AM VBROWN CUSTOMER CAN INSP WAS NOT READY WILL DO 4 TRADE ROUGH IN FOR 7-1-10. PUTTING ON WATER PROOFING FOR 6-30-10.
R427 02	7/01/10 7/01/10	JH DA	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001948856 T/S: 06/30/2010 08:59 AM VBROWN 1)Nail all holes on anchor straps & need paper work on distance for straps. 2)Need paper work for LVLs in garage & kitchen nook. 3)Missing 2 studs in kitchen under beam @ stairs. 4)Missing collar ties on rafters. 5)4' headers on double windows in basement need 2 jack studson each side. 6)Fire caulk electrical wire @ panel in basement @ top plate
I129 01	7/02/10 7/02/10	JH AP	R*INSULATION INSPECTION TIME: 17:00 VRU #: 001949122 T/S: 07/01/2010 01:20 PM RDCONTE OK TO INSULATE PER INSPECTOR
R427 03	7/02/10 7/02/10	JH AP	FOUR TRADE ROUGH IN >2500 TIME: 17:00 VRU #: 001949098 T/S: 07/01/2010 01:20 PM RDCONTE
R431 01	8/04/10 8/04/10	JH DA	FOUR TRADE FINAL >2500 VRU #: 001963438 No house numbers on house. Service cable from meter to inside panel needs to be 4 wires & protected. No bath fans installed in house. Need 24" walkway to AHU in attic @ top of ladder for attic access. Need weather strip around door to basement, uncondition space. Missing ground bar for cable & phone @ meter. Need 3" of cover on sewer liene in back yard.
R431 02	8/06/10 <u>8-6-10</u>	TI <u>APJH</u>	FOUR TRADE FINAL >2500 TIME: 17:00 VRU #: 001965482 T/S: 08/05/2010 01:09 PM RDCONTE

----- COMMENTS AND NOTES -----

County of Harnett
Building Inspections Department
Planning Services

Certificate of Compliance: ___ Occupancy:

Certificate issued pursuant to the requirements of North Carolina General Statute 153A-363 and Harnett County Zoning Ordinances. This certifies at the time of issuance, this structure was in compliance with the various ordinances of the County of Harnett and the North Carolina State Building Codes. For the following:

Use Classification: S/O

Permit Numbers

Name: Charneyky Custom Homes LLC

Building: _____

Electrical: _____

Address: 279 Cobblestone Dr

Insulation: _____

Plumbing: _____

Mechanical: _____

MFG Home: _____

Date: 8-6-10

Building Official: _____

James T. Hall

06-50015/14
