

ADDRESS : 144 GWENDOLYN WAY  
 TENANT, NBR: ENVIOR CONF# 014791  
 CONTRACTOR : CUMBERLAND HOMES INC  
 OWNER : NELSON THOMAS W & LORRAINE B  
 PARCEL : 08-0652- -0089- -10-  
 APPL NUMBER: 16-50038101 CP NEW RESIDENTIAL (SFD)  
 DIRECTIONS : T/S: 02/29/2016 10:06 AM JBROCK ----  
 BALLARD WOODS #178

SUBDIV: BALLARDS WOODS PH 4A  
 PHONE : (910) 892-4345  
 PHONE :

STRUCTURE: 000 000 41X54 3BDR SLAB W/ GARAGE

FLOOD ZONE : FLOOD ZONE X  
 # BEDROOMS : 3000000.00  
 SEPTIC - EXISTING? : NEW TANK

PROPOSED USE : SFD  
 WATER SUPPLY : COUNTY

PERMIT: CPSF 00 CP \* SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	4/11/16	BS	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 002800944
	4/11/16	AP	T/S: April 11, 2016 10:21 AM BSUTTON Tpole missing cover screws and has an open breaker space.
A814 01	4/26/16	SB	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 002807691
	4/26/16	AP	144 GWENDOLYN WAY FUQUAY VARINA 27526 T/S: 04/26/2016 10:11 AM SBENNETT
B103 01	4/26/16	BS	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 002807675
	4/26/16	AP	T/S: 04/25/2016 01:56 PM DJOHNSON inspect tsp if it has not been and if it is there. T/S: April 26, 2016 08:51 AM BSUTTON Called in Tpole
P309 01	5/10/16	BS	R*PLUMB UNDER SLAB TIME: 17:00 VRU #: 002813855
	5/10/16	AP	T/S: 05/09/2016 01:02 PM JFORBES T/S: May 10, 2016 11:50 AM BSUTTON
B111 01	5/13/16	BS	R*BLDG SLAB INSP/TEMP SVC POLE TIME: 17:00 VRU #: 002815918
	5/13/16	DA	T/S: 05/12/2016 09:54 AM DJOHNSON T/S: May 13, 2016 09:07 AM BSUTTON Need soil compaction test results per 506.2.1 for fill in excess of 24 inches
B111 02	5/17/16	TI	R*BLDG SLAB INSP/TEMP SVC POLE TIME: 17:00 VRU #: 002817070
	<u>5/17/16</u>	<u>APBY</u>	T/S: 05/16/2016 09:37 AM LBENNETT

COMMENTS AND NOTES

# Enoch Engineers, P.A.

Materials & Tests Division  
1403 NC Highway 50 South  
Benson, NC 27504  
919-894-7765

# Report

Client: MILLENNIUM HOMES  
Project: BALLARD WOODS S/D  
Location: 144 GWENDOLYN DR.  
Lot #: 178

Technician: BH  
Date: 5.16.16  
Contractor: JO DENNIS NORRIS


### Services Performed:

- Nuclear Density Test
- Concrete Tests
- Asphalt Tests
- Site Inspection
- Foundation Inspection
- Structural Inspection
- Proof-roll

- Steel Inspection
- Sub-Grade Inspection
- H.U.D. Inspection
- LUGG Footing Inspection
- Footing Inspection
- Other: \_\_\_\_\_

Remarks: PERFORMED NOT ON PAD AT LOT NOTED ABOVE USING  
A TARGET DENSITY OF 115 PCF. SOILS CONFIRMED A COMPACTION  
≥ 95%. LUGG FOOTING CONFIRMED A MINIMUM ALLOWABLE  
BEARING CAPACITY OF 2000 LBS/FT<sup>2</sup>.

NTS.

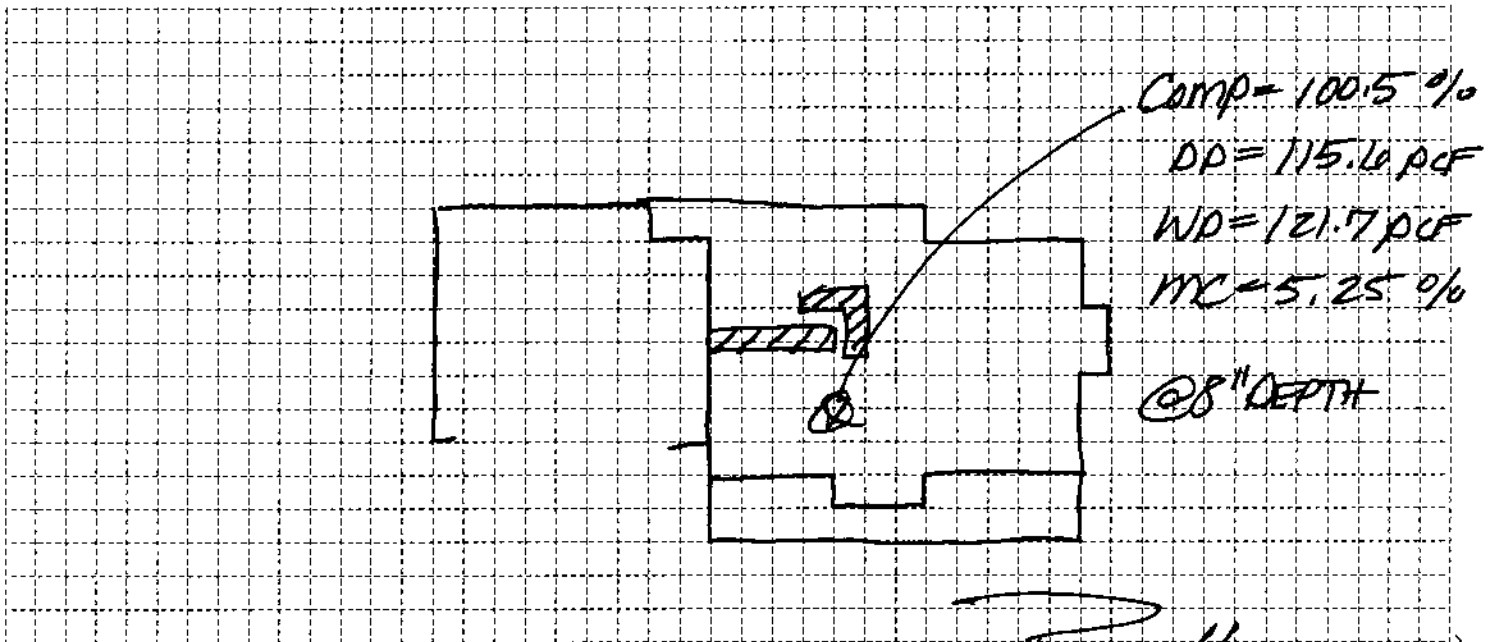

Technician: BH
