

-----  
ADDRESS . : 857 MANN RD SUBDIV:  
CONTRACTOR : STAND SURE CUSTOM HOMES INC PHONE : (910) 890-6870  
OWNER . . : INGRAM BILLY S & ROBERT L PHONE :  
PARCEL . . : 07-1509- - -0062- -15-  
APPL NUMBER: 16-50039663 CP NEW RESIDENTIAL (SFD)  
DIRECTIONS : 421 TOWARDS ERWIN/ L@ RED HILL CHURCH/  
LE@ CANE MILL/ R@ MANN RD/ LOT AT END  
OF DIRT RD ON LEFT  
-----

STRUCTURE: 000 000 70X70 3BDR MONO W/ GARAGE& DECK  
FLOOD ZONE . . . . : FLOOD ZONE X  
PROPOSED USE . . . . : SFD WATER SUPPLY . . . . . : NEW WELL  
-----

PERMIT: CPSF 00 CP \* SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	1/18/17 1/18/17	DT AP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 002921310 T/S: 01/17/2017 01:46 PM LBENNETT ----- T/S: 01/18/2017 01:53 PM DETAYLOR -----
B103 01	1/27/17 1/27/17	DT DA	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 002925030 T/S: 01/26/2017 12:51 PM DJOHNSON ----- TSP INSPECTION NEEDED ALSO. T/S: 01/27/2017 12:50 PM DETAYLOR ----- Need slab insulation/res-check Need engineering for wall with more than 48 inches of unbalanced fill
A814 01	1/31/17 1/31/17	SB AP	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 002926830 857 MANN RD COATS 27521 T/S: 01/31/2017 03:31 PM SBENNETT -----
B103 02	1/31/17 1/31/17	DT AP	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 002926822 T/S: 01/30/2017 02:56 PM LBENNETT ----- T/S: 01/31/2017 01:48 PM DETAYLOR -----
P309 01	2/07/17 2/07/17	KS AP	R*PLUMB UNDER SLAB TIME: 17:00 VRU #: 002930097 T/S: 02/06/2017 01:23 PM JBROCK ----- if pole has not been check - please make sure t-pole has been check, there is no way for me to tell if it has been looked at or not T/S: 02/07/2017 02:57 PM KSLATTUM -----
B111 01	2/10/17 <u>2/10/17</u>	TI <u>APDT</u>	R*BLDG SLAB INSP/TEMP SVC POLE TIME: 17:00 VRU #: 002931798 T/S: 02/09/2017 01:29 PM JBROCK -----

----- COMMENTS AND NOTES -----

# Enoch Engineers, P.A.

Materials & Tests Division  
1403 NC Highway 50 South  
Benson, NC 27504  
919-894-7765

## Report

Client: KC Concrete  
Project: \_\_\_\_\_  
Location: 857 Mann rd., Coats  
Lot #: \_\_\_\_\_


Technician: BP  
Date: 2-2-17  
Contractor: c/o Michael Williams

Services Performed:

- Nuclear Density Test
- Concrete Tests
- Asphalt Tests
- Site Inspection
- Foundation Inspection
- Structural Inspection
- Proof-roll

- Steel Inspection
- Sub-Grade Inspection
- H.U.D. Inspection
- LUGG Footing Inspection
- Footing Inspection
- Other: \_\_\_\_\_

Remarks: Performed NDT on pad at site noted above  
using a target density of 100 pcf. Soils confirmed  
a compaction  $\geq$  95%.

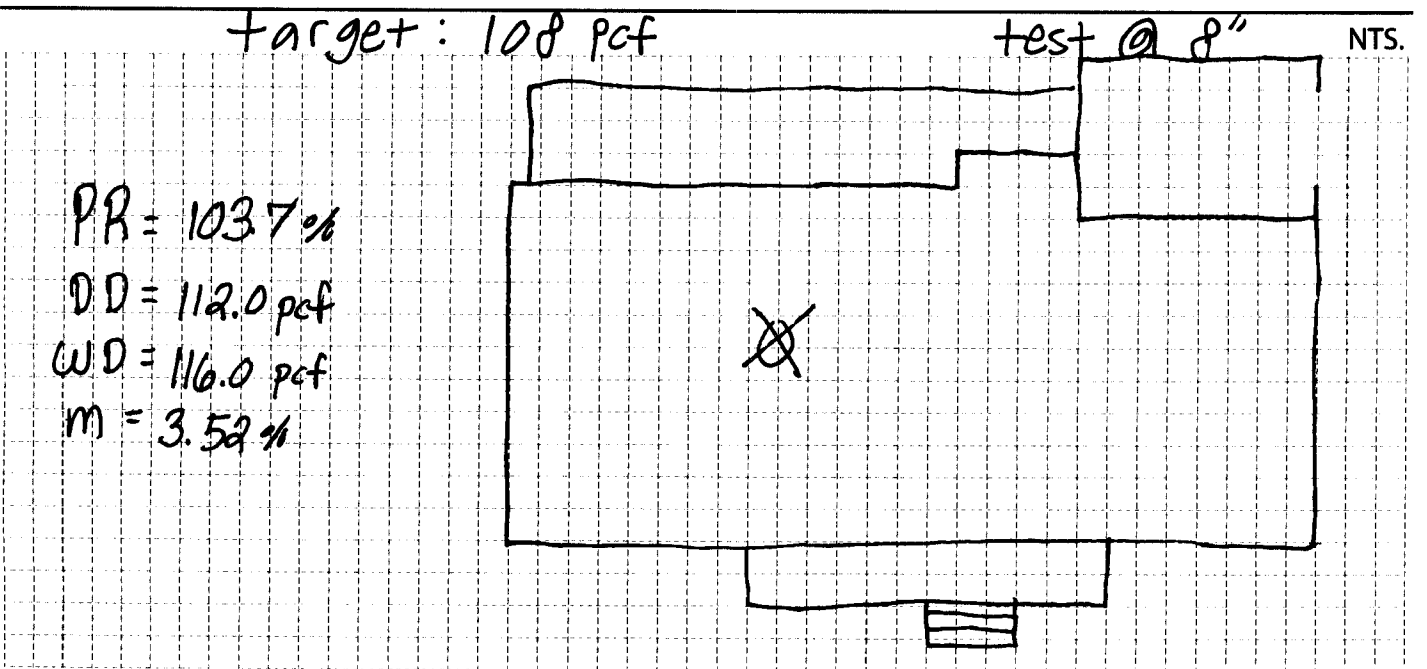

Technician: Breton Parker
