



**ECS Southeast, LLP**

6151 Raeford Road, Suite A  
Fayetteville, NC 28304  
9104013288  
9103230539

**LETTER OF TRANSMITTAL**


September 9, 2022  
Ben Stout Construction  
PO Box 53798  
Fayetteville, NC 28305  
ATTN: Robert Ivey

RE: **Lot 2 808 Cypress Rd.**  
ECS Job # **33:6171**  
  
Permits:  
Location: **808 Cypress Rd**  
**Cameron, NC 28326**

Field Reports       For your use       As requested

CC:

ENCL: Field Report # 2      9/8/2022      Foundation Soils Bearing



**SEP 09 2022**

Jack Cowsert, P.E.  
Office Manager

Charles A. Pearson  
CMT Senior Project Coordinator

*Disclaimer*

1. This report (and any attachments) shall not be reproduced except in full without prior written approval of ECS.
2. The information in this report relates only to the activities performed on the report date.
3. Where appropriate, this report includes statements as to compliance with applicable project drawings, and specifications for the activities, performed on this report date.
4. Incomplete or non-conforming work will be reported for future resolution.
5. The results of samples and/or specimens obtained or prepared for subsequent laboratory testing will be presented in separate reports/documents.



ECS Southeast, LLP  
 6151 Raeford Road, Suite A  
 Fayetteville, NC 28304  
 (910) 401-3288 [Phone]  
 (910) 323-0539 [Fax]

## FIELD REPORT

Project **Lot 2 808 Cypress Rd.**  
 Location **Cameron, NC**  
 Client **Ben Stout Construction**  
 Contractor **Ben Stout Construction**

Project No. **33:6171**  
 Report No. **2**  
 Day & Date **Thursday 9/8/2022**  
 Weather **75 °/ Cloudy**  
 On-Site Time **0.75**  
 Lab Time **0.00**  
 Travel Time\* **0.00**  
 Total **0.75**  
 Re Obs Time **0.00**

Remarks **Foundation Soils Bearing**

Trip Charges*	Tolls/Parking*	Mileage*	Time of Arrival	Departure
Chargeable Items			<b>10:45A</b>	<b>11:30A</b>

\* Travel time and mileage will be billed in accordance with the contract.


**Summary of Services Performed (field test data, locations, elevations & depths are estimates) & Individuals Contacted.**

ECS arrived on site, as requested, to check the bearing capacity of soils via hand auger/DCP method for foundation footings. Please see the attached sketch for approximate test locations.

A hand auger was used to advance the boreholes to different depths noted on the boring logs. Dynamic Cone Penetrometer (DCP) testing was performed in the hand auger boreholes by a 1.5 inch diameter cone driven into the soil by a 15 pound ring weight with a free fall of 20 inches. The number of blows required to drive the cone into the soil a distance of 1.75 inches is termed the DCP Value and is indicated for each test on the attached DCP data sheet.

A total of 3 hand auger/DCP evaluations were performed to a depth of approximately 3 feet below the current soil sub grade elevation. Test data indicates that the in-place materials, at the locations and elevations tested, did appear to be suitable to support a design bearing capacity 2,000 psf.

ECS will return upon request to provide additional services.

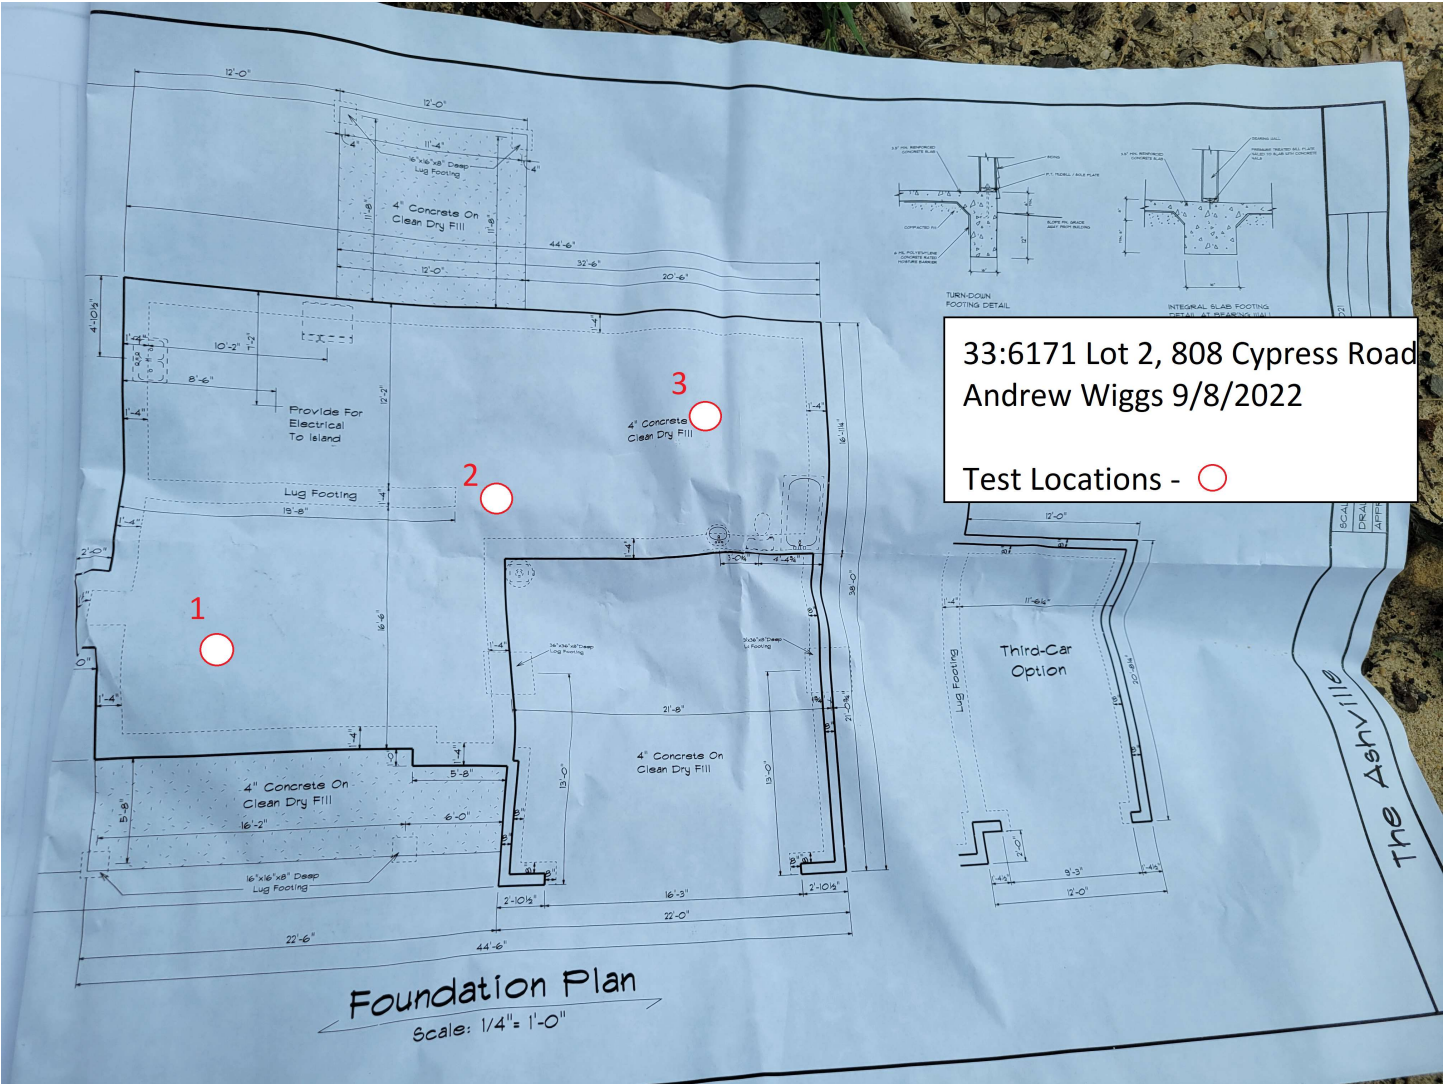

33:6171 Lot 2, 808 Cypress Road  
 Andrew Wiggs 9/8/2022

Test Locations - ○

Foundation Plan  
 Scale: 1/4" = 1'-0"



## Report of Spread Footing - Foundation Observations

Project: Lot 2 808 Cypress Rd.  
 Location: 808 Cypress Rd  
 Cameron - Moore - NC - 28326  
 Contractor: Ben Stout Construction

Project No.: 33:6171  
 Day/Date: 9/8/2022

Footing Number	Location	Size (W x H x L)		Footing Bottom Elevation		Description of Steel Placed	Description of Subgrade Material	Required Blow Counts	Design Bearing Pressure
		Design	Actual	Design **	Depth of Undercut (in)			# of Blows / Increment	
1	southwest corner of stem wall backfill	x x	x x	N/A	N/A		(0/-1/-2/-3)tan sand	6 (0)5,6,7(-1)6,7,8(-2) 12,16,20(-3)19,13,14	2000
1	center of stem wall backfill near lug footing	x x	x x	N/A	N/A		(0/-1/-2/-3)tan sand	6 (0)6,8,9(-1)16,17,17(-2) 10,10,10(-3)17,13,14	2000
1	northeast corner of stem wall backfill	x x	x x	N/A	N/A		(0/-1)tan sand(-2)brown clayey sand(-3)red and yellow clayey sand	6 (0)7,9,10(-1)13,17,17(-2)9,7,4(-3)25+	2000

\*\* SGE: Subgrade Elevation to be determined by surveyor.

By: Andrew Wiggs  
 \_\_\_\_\_  
 \_\_\_\_\_  
 ECS Southeast, LLP

WO: 68731
