



**ECS Southeast, LLP**

6151 Raeford Road, Suite A  
Fayetteville, NC 28304  
9104013288  
9103230539

**LETTER OF TRANSMITTAL**


October 14, 2022  
W.S. Wellons Realty  
PO Box 766  
Spring Lake, NC 28390  
ATTN: Accounts Payable

RE: **Wellons Realty Lot 114**  
ECS Job # **33:6204-D**  
  
Permits:  
Location: **80 Black Oak Place**  
**Spring Lake, NC 28390**

Field Reports       For your use       As requested

CC: W.S. Wellons Realty - Jason Wellons

ENCL: Field Report # 1      10/11/2022



Jack Cowser, P.E.  
Office Manager

Ryan H. Parrish  
CMT Group Supervisor

*Disclaimer*

1. This report (and any attachments) shall not be reproduced except in full without prior written approval of ECS.
2. The information in this report relates only to the activities performed on the report date.
3. Where appropriate, this report includes statements as to compliance with applicable project drawings, and specifications for the activities, performed on this report date.
4. Incomplete or non-conforming work will be reported for future resolution.
5. The results of samples and/or specimens obtained or prepared for subsequent laboratory testing will be presented in separate reports/documents.



ECS Southeast, LLP  
 6151 Raeford Road, Suite A  
 Fayetteville, NC 28304  
 (910) 401-3288 [Phone]  
 (910) 323-0539 [Fax]

## FIELD REPORT

Project **Wellons Realty Lot 114**  
 Location **Spring Lake, NC**  
 Client **W.S. Wellons Realty**  
 Contractor **None Listed**

Project No. **33:6204-D**  
 Report No. **1**  
 Day & Date **Tuesday 10/11/2022**  
 Weather **74 °/ Sunny**  
 On-Site Time **1.00**  
 Lab Time **0.00**  
 Travel Time\* **0.00**  
 Total **1.00**  
 Re Obs Time **0.00**

Remarks

Trip Charges*	Tolls/Parking*	Mileage*	Time of Arrival	Departure
Chargeable Items			<b>11:15A</b>	<b>12:15P</b>

\* Travel time and mileage will be billed in accordance with the contract.


**Summary of Services Performed (field test data, locations, elevations & depths are estimates) & Individuals Contacted.**

The undersigned arrived on site, as requested, to check the bearing for soils at Lot 114. Please see the attached sketch for details.

The footings were not excavated at the time of our site visit. The house corners were staked by others.

To evaluate the bearing grade soils, hand auger borings were performed to approximately 18 inches below the existing pad grade (approximate bearing grade elevation) and Dynamic Cone Penetrometer (DCP) testing was performed per ASTM STP-399 at 12 inch intervals to depths noted on the attached report.

A total of four hand auger borings with DCP tests were performed at four corners of the house. The test results indicated the presence of suitable soils at the areas and elevations tested that will support a foundation designed for a net allowable bearing pressure of 2,000 pounds per square foot.

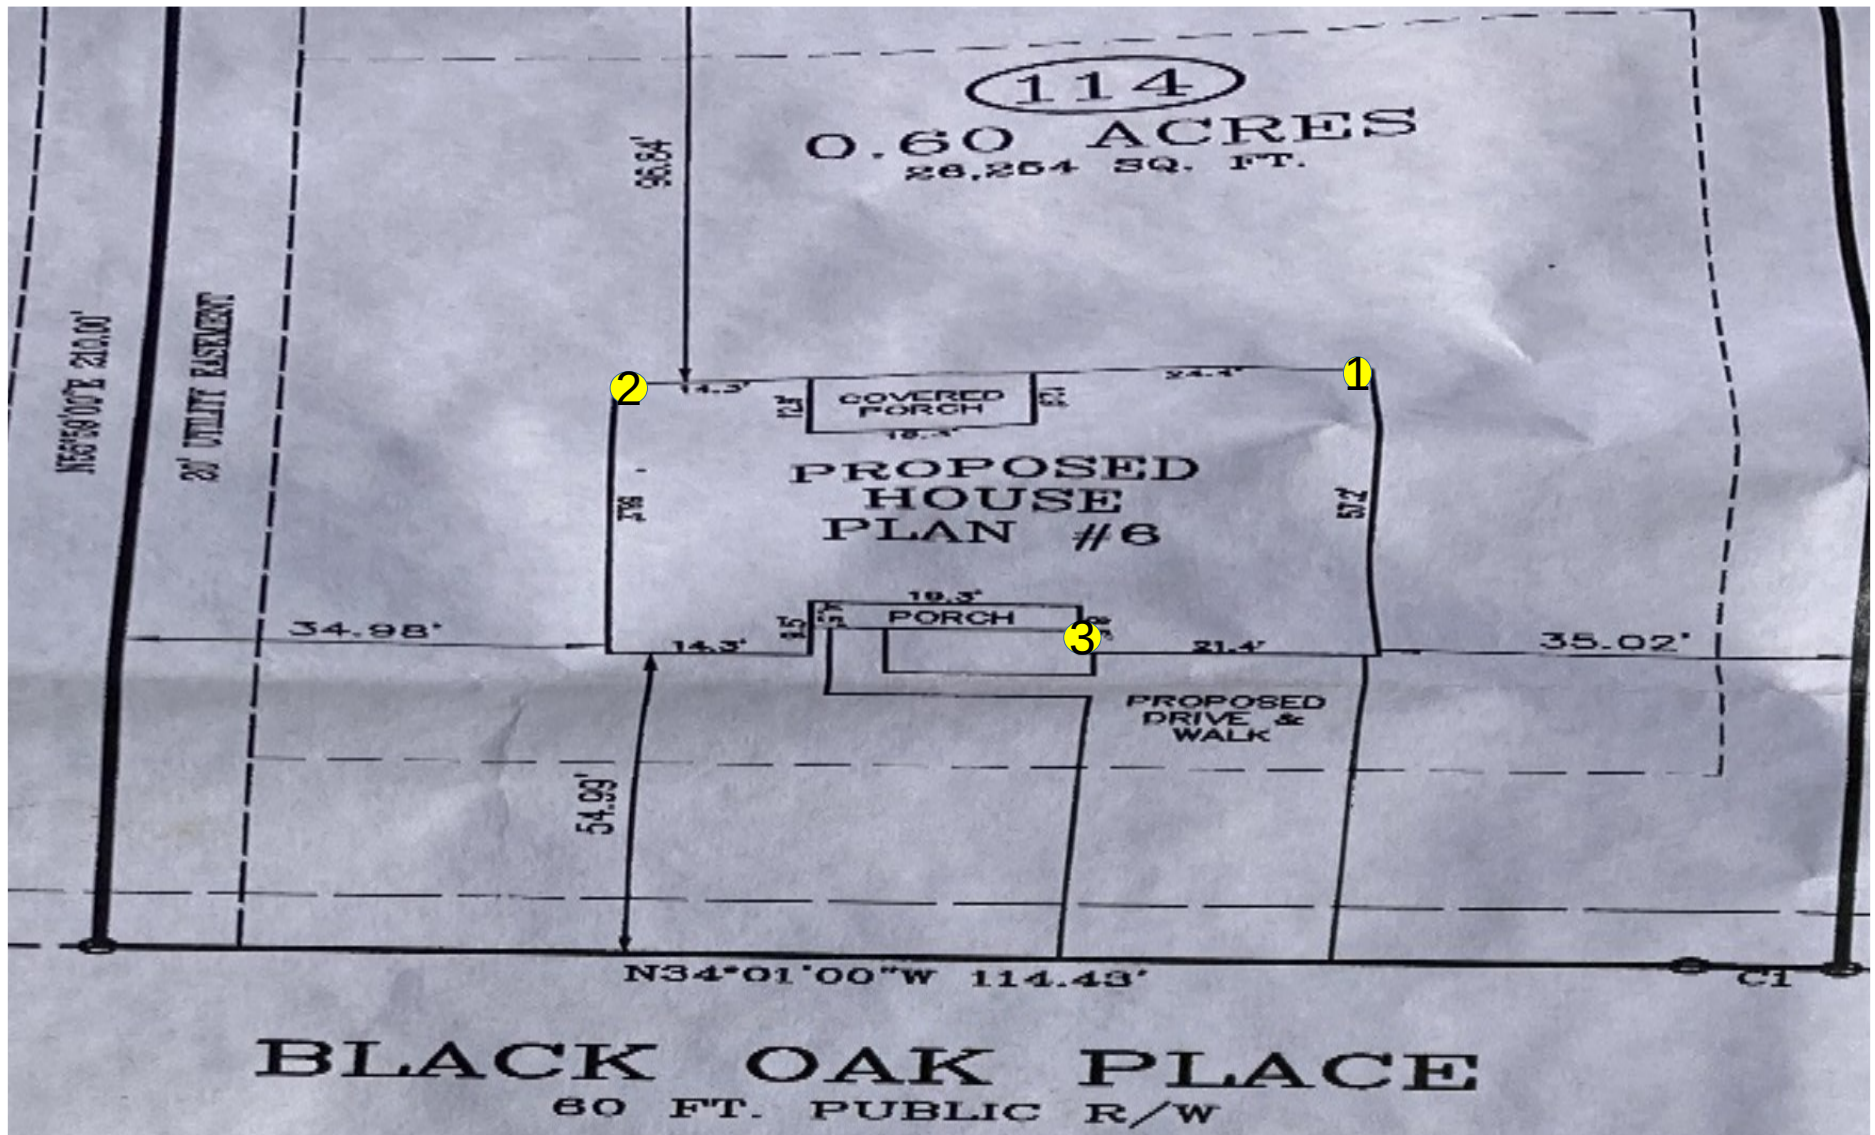

Todd T. Davis  
 10/11/2022  
 Lot 114  
 P# 6204-D  
 WO# 69197

**Key**  
 DCP / Hand Auger Test Locations --- #





Todd T. Davis  
10/11/2022  
Lot 114  
P# 6204-D  
WO# 69197

Key

View of Lot 114





## Report of Spread Footing - Foundation Observations

Project: Wellons Realty Lot 114  
 Location: 80 Black Oak Place  
 Spring Lake - Cumberland - NC - 28390  
 Contractor: None Listed

Project No.: 33:6204-D  
 Day/Date: 10/11/2022

Footing Number	Location	Size (W x H x L)		Footing Bottom Elevation		Description of Steel Placed	Description of Subgrade Material	Required Blow Counts	Design Bearing Pressure
		Design	Actual	Design **	Depth of Undercut (in)			# of Blows / Increment	
1	See Attached Drawing	x x	x x	N/A	N/A		(0) Tan-Orange Silty Sand (1) Brown Silty Sand (2-3) Tan Silty Sand	6	2000
								(0) 4,6,7 (1) 6.7.8 (2) 7,9,9 (3) 8,10,11	
2	See Attached Drawing	x x	x x	N/A	N/A		(0) Tan-Orange Silty Sand (1) Brown Silty Sand (2-3) Tan Silty Sand	6	2000
								(0) 6,8,9 (1) 7,10,11 (2) 7,7,8 (3) 9,10,12	
3	See Attached Drawing	x x	x x	N/A	N/A		(0-3) Tan-Orange Silty Sand	6	2000
								(0) 6,8,9 (1) 7,10,11 (2) 7,7,8 (3) 9,10,12	

\*\* SGE: Subgrade Elevation to be determined by surveyor.

By: Todd Davis \_\_\_\_\_

\_\_\_\_\_  
 ECS Southeast, LLP



## Report of Spread Footing - Foundation Observations

Project: Wellons Realty Lot 114  
Location: 80 Black Oak Place  
Spring Lake - Cumberland - NC - 28390  
Contractor: None Listed

Project No.: 33:6204-D  
Day/Date: 10/11/2022

WO: 69197
