

ECS Southeast, LLP

6151 Raeford Road, Suite A Fayetteville, NC 28304 9104013288 9103230539

LETTER OF TRANSMITTAL

April 18, 2023

Precision Custom Homes

Raeford, NC 28376

ATTN: Shaun Gardner

RE: **Liberty Meadows Lot 18**

ECS Job # 33:6442-A

Permits:

X

Location: 124 Edes Ct

Cameron, NC 28326

Field Reports

For your use

X As requested

CC: Precision Custom Homes - Allen Peterson Precision Custom Homes - Lauren Ceruti

ENCL: Field Report # 1 4/13/2023

APR 18 2023

Jack Cowsert, P.E. Office Manager

Aaron Kyle Adair Team Leader

Disclaimer

^{1.} This report (and any attachments) shall not be reproduced except in full without prior written approval of ECS.

^{2.} The information in this report relates only to the activities performed on the report date.

^{3.} Where appropriate, this report includes statements as to compliance with applicable project drawings, and specifications for the activities, performed on this report date.

^{4.} Incomplete or non-conforming work will be reported for future resolution.

^{5.} The results of samples and/or specimens obtained or prepared for subsequent laboratory testing will be presented in separate reports/documents.



ECS Southeast, LLP 6151 Raeford Road, Suite A Fayetteville, NC 28304 (910) 401-3288 [Phone] (910) 323-0539 [Fax]

Project Liberty Meadows Lot 18

Location Cameron, NC

Client Precision Custom Homes

Contractor Precision Custom Homes

FIELD REPORT

Project No. 33:6442-A

Report No. 1

Day & Date Thursday 4/13/2023

Weather 80 °/ Sunny

On-Site Time 1.50

Lab Time 0.00

Travel Time* 0.00

Total 1.50

Re Obs Time 0.00

Remarks

Trip Charges* Tolls/Parking* Mileage* Time of Arrival Departure

Chargeable Items 4:00P 5:30P

Summary of Services Performed (field test data, locations, elevations & depths are estimates) & Individuals Contacted.


ECS arrived on site, as requested, to check the bearing capacity of soils via hand auger/DCP method for monolithic slab area prior to receiving concrete. Please see the attached sketch and data sheet for details.

A total of 4 hand auger/DCP evaluations were performed to a depth of approximately 3 feet below the current footing sub grade elevation. Test results indicated that the materials in place, at the locations and elevations tested, did appear to be suitable to support the design bearing capacity 2,000 psf.

ECS will return upon request.

By Todd Davis

^{*} Travel time and mileage will be billed in accordance with the contract.

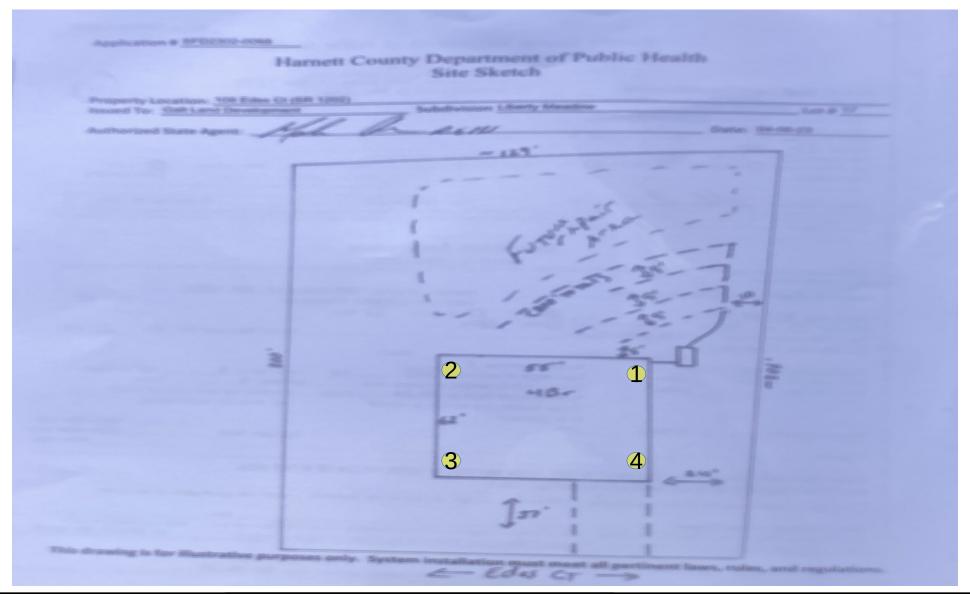

Todd T. Davis 04/13/2023 Liberty Meadows Lot 17

Proj #: 6442-A W/O # 71714

Key (NTS)

Hand Auger / DCP
Test Locations --- #



Transmittal Dags 2/6



Todd T. Davis 04/13/2023 Liberty Meadows Lot 18

Proj #: 6442-A W/O # 71714

Key (NTS)
View of Residential Lot Area





Report of Spread Footing - Foundation Observations

Project: Liberty Meadows Lot 18 Project No.: 33:6442-A 124 Edes Ct Location: Day/Date: 4/13/2023

Contractor: Cameron - Moore - NC - 28326

Precision Custom Homes

Footing Number	Location	Size (W x H x L)		Footing Bottom Elevation				Required Blow Counts	
		Design	Actual	Design **	Depth of Undercut (in)	Description of Steel Placed	Description of Subgrade Material	# of Blows / Increment	Design Bearing Pressure
1	See Attached Drawing	x x	x x	N/A	N/A		(0)Tan-Red Silty Sand (1) Gray Silty Sand (2) Yellowish-Tan Silty Sand (3) Tan-Orange Clayey Sand	(0) 8,10,11 (1) 7,9,9 (2) 9,10,10 (3) 11,12,15	
2	See Attached Drawing	x x	хх	N/A	N/A		(0)Tan-Red Silty Sand (1) Gray Silty Sand (2) Yellowish-Tan Silty Sand (3) Tan-Orange Clayey Sand	(0) 7,10,10 (1) 7,8,9 (2) 9,10,12 (3) 11,12,12	
3	See Attached Drawing	хх	x x	N/A	N/A		(0)Tan-Red Silty Sand (1) Gray Silty Sand (2) Yellowish-Tan Silty Sand (3) Tan-Orange Clayey Sand	(0) 9,10,11 (1) 8,12,13 (2) 9,10,11 (3) 11,15,17	
4	See Attached Drawing	x x	x x	N/A	N/A		(0)Tan-Red Silty Sand (1) Gray Silty Sand (2) Yellowish-Tan Silty Sand (3) Tan-Orange Clayey Sand	6 (0) 6,8,9 (1) 8,10,13 (2) 9,10,13 (3) 11,14,15	

^{**} SGE: Subgrade Elevation to be determined by surveyor.

NC Registered Firm # F-1078



Report of Spread Footing - Foundation Observations

Project:	Liberty Meadows Lot 18	Project No.:	33:6442-A	
Location:	124 Edes Ct	Day/Date:	4/13/2023	
	Cameron - Moore - NC - 28326			

Contractor: Precision Custom Homes

Зу:	Todd Davis
	ECS Southeast, LLP

WO: 71715
