



**ECS Southeast, LLP**

6151 Raeford Road, Suite A  
Fayetteville, NC 28304  
9104013288  
9103230539

**LETTER OF TRANSMITTAL**

July 13, 2023  
W.S. Wellons Realty  
PO Box 766  
Spring Lake, NC 28390  
ATTN: Chandler Jones

RE: **Lot 539 OHC**  
ECS Job # **33:6230-DA**  
  
Permits:  
Location: **272 Caldwell St**  
**Spring Lake, NC 28390**


Field Reports       For your use       As requested

CC:

ENCL: Field Report # 3      7/12/2023      Recommendations

Jack Cowsert, P.E.  
Office Manager

Aaron Kyle Adair  
Team Leader



**Disclaimer**

1. This report (and any attachments) shall not be reproduced except in full without prior written approval of ECS.
2. The information in this report relates only to the activities performed on the report date.
3. Where appropriate, this report includes statements as to compliance with applicable project drawings, and specifications for the activities, performed on this report date.
4. Incomplete or non-conforming work will be reported for future resolution.
5. The results of samples and/or specimens obtained or prepared for subsequent laboratory testing will be presented in separate reports/documents.



ECS Southeast, LLP  
 6151 Raeford Road, Suite A  
 Fayetteville, NC 28304  
 (910) 401-3288 [Phone]  
 (910) 323-0539 [Fax]

## FIELD REPORT

Project **Lot 539 OHC**  
 Location **Spring Lake, NC**  
 Client **W.S. Wellons Realty**  
 Contractor **W.S. Wellons Realty**

Project No. **33:6230-a**  
 Report No. **3**  
 Day & Date **Wednesday 7/12/2023**  
 Weather **79 °/ Sunny**  
 On-Site Time **1.00**  
 Lab Time **0.00**  
 Travel Time\* **0.00**  
 Total **1.00**  
 Re Obs Time **0.00**

Remarks **Recommendations**

Trip Charges*	Tolls/Parking*	Mileage*	Time of Arrival	Departure
Chargeable Items			<b>8:00A</b>	<b>9:00A</b>

\* Travel time and mileage will be billed in accordance with the contract.

<b>Summary of Services Performed (field test data, locations, elevations &amp; depths are estimates) &amp; Individuals Contacted.</b>
---

ECS arrived on site, as requested, to observe a portion of the garage footing that had ground water seepage. Upon arrival, ECS probed the footing throughout to determine the stability of the soils in place. Due to the soils being saturated, ECS spoke with Chandler Jones w/ Wellons Realty. ECS provide the recommendation of undercutting the soft and saturated soils down to 3 feet below the current footing subgrade. Once undercut, ECS recommended backfilling the footing with 57 stone and wrapping the stone with an engineering non-woven fabric. Please see the attached photos for the documented repairs.

ECS will return, as requested, for additional services.

# Attachments



Figure 1



Figure 2

# Attachments



Figure 3

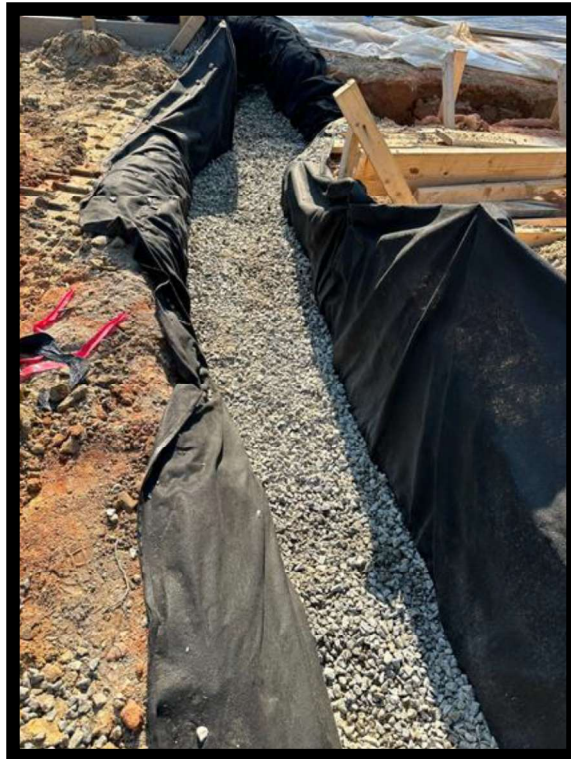


Figure 4

# Attachments



Figure 5
