

County of Harnett
Building Inspections Department
Planning Services

SCANNED

DATE

Certificate of Compliance: _____ Occupancy:

Certificate issued pursuant to the requirements of North Carolina General Statute 153A-363 and Harnett County Zoning Ordinances. This certifies at the time of issuance, this structure was in compliance with the various ordinances of the County of Harnett and the North Carolina State Building Codes. For the following:

Use Classification: SFD

Permit Numbers

Name: William T. Mary Prough

Building: 11-5-26245

Address: 5908 River Road

Electrical: 11-5-26245

Ferguson Virginia NC 27526

Insulation: 11-5-26245


Plumbing: 11-5-26245

Mechanical: 11-5-26245

MFG Home: _____

Date: 8-15-2011

Building Official: Brad Gittler

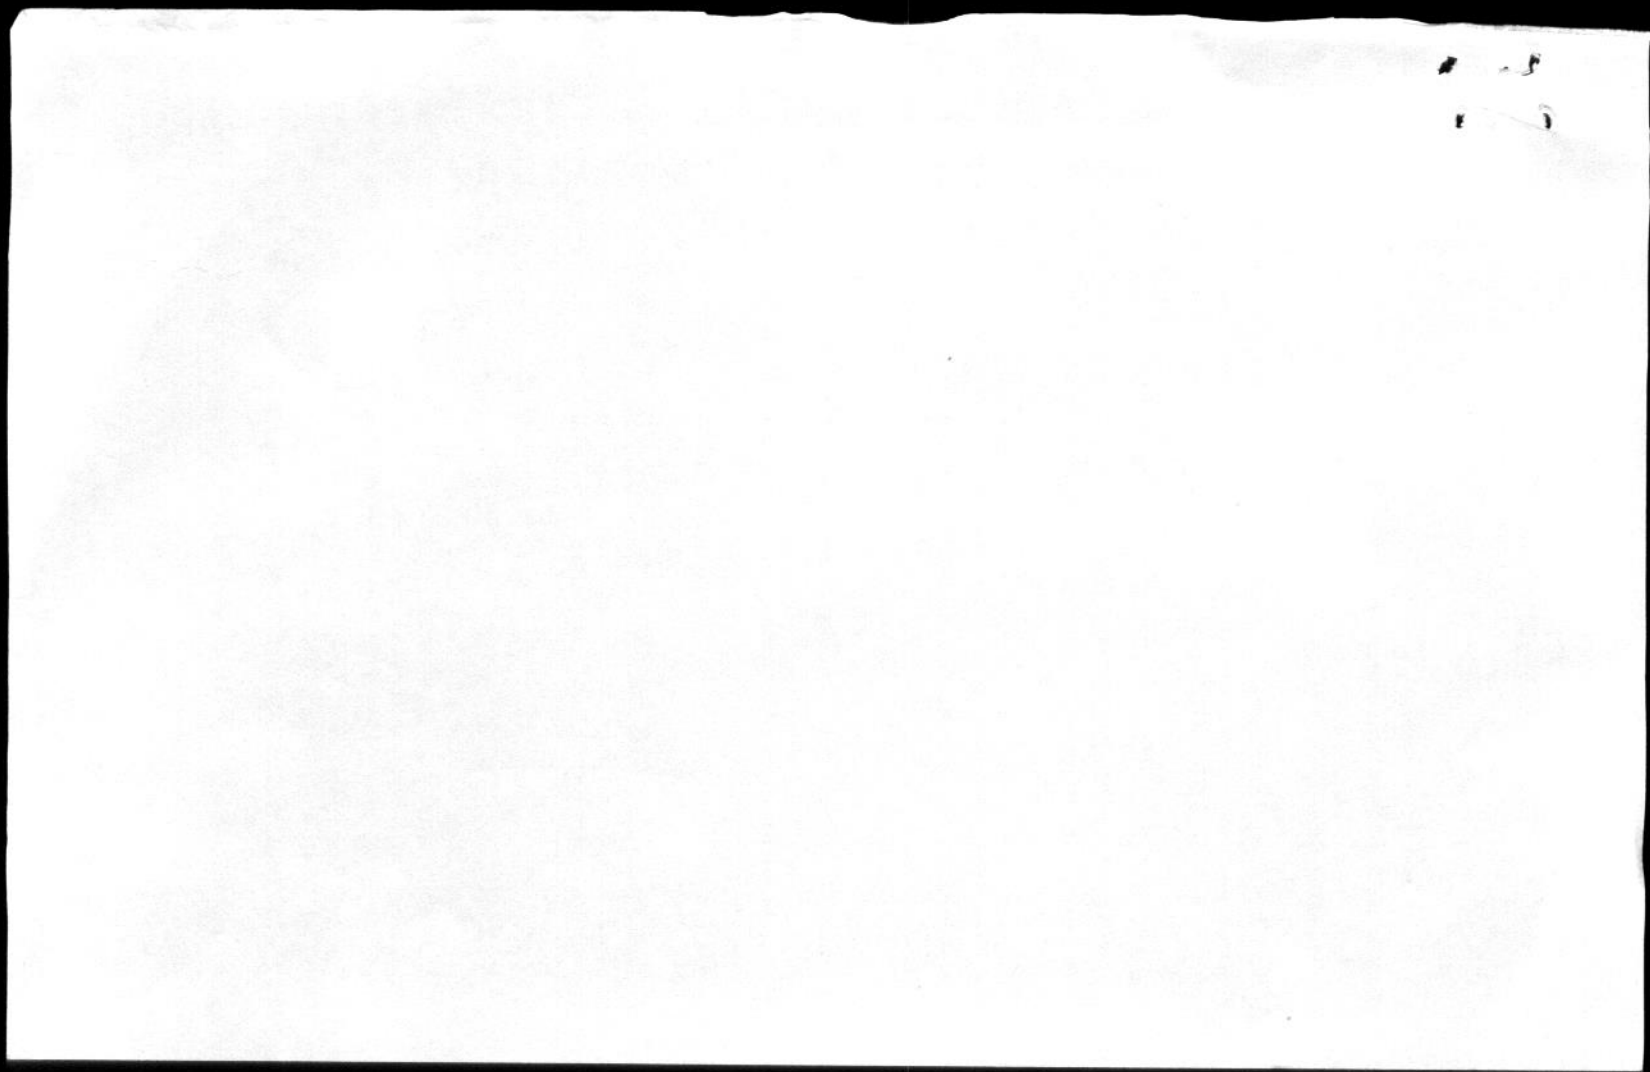

ADDRESS : 5908 RIVER RD SUBDIV:
CONTRACTOR : SCHUMACHER HOMES OF NC, INC PHONE : (330) 478-4505
OWNER : PROUGH WILLIAM T & MARY C PHONE : (480) 543-8174
PARCEL : 05-0624- - -0029- -02-
APPL NUMBER: 11-50026245 CP NEW RESIDENTIAL (SFD)
DIRECTIONS : T/S: 03/15/2011 10:34 AM VBROWN ----
PROPERTY IS NEAR 5908 RIVER RD 27546.
401N, LEFT ON CHRISTIAN LIGHT RD, LEFT
ON RIVER RD, APPROX 1MI TO 5908 RIVER
RD, DOWN PRIVATE DRIVE.

STRUCTURE: 000 000 50X30 3BDR 3BATH SFD W GAR, CRAWL&BASMENT

FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 3.00 PROPOSED USE : SFD
SEPTIC - EXISTING? : NEW TANK WATER SUPPLY : COUNTY

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	5/04/11 5/04/11	RD CA	R*BLDG FOOTING / TEMP SVC POLE VRU #: 002075240 WOULD LIKE THIS AROUND 12:00. T/S: 05/04/2011 10:05 AM RDCONTE ----- ROLLED TO 5/5/11
B101 02	5/05/11 5/05/11	KS DP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 002075943 T/S: 05/04/2011 10:06 AM RDCONTE ----- T/S: 05/05/2011 01:11 PM NTART ----- T/S: 05/05/2011 01:12 PM NTART -----
B101 03	5/06/11 5/06/11	BS AP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 002077212 T/S: 05/05/2011 02:48 PM NTART ----- T/S: May 06, 2011 11:34 AM BSUTTON -----
B103 01	5/11/11 5/11/11	BS AP	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 002078764 WILL BE FOR THE BASEMENT WALL. ART ----- T/S: 05/10/2011 12:49 PM NTART ----- T/S: May 11, 2011 02:44 PM BSUTTON -----
B103 02	5/20/11 5/20/11	BS AE	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 002083319 T/S: 05/19/2011 12:21 PM RDCONTE ----- THIS IS FOR THE CRAWL SPACE PORTION. BASEMENT HAS ALREADY BEEN INSPECTED. 1. Need information on bond beams in foundation. Ok to waterproof.
P309 01	5/23/11 5/23/11	BS AP	R*PLUMB UNDER SLAB TIME: 17:00 VRU #: 002083913 T/S: 05/20/2011 01:10 PM NTART ----- T/S: May 23, 2011 10:57 AM BSUTTON -----
A814 01	5/24/11 5/26/11	TW AP	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 002084408 T/S: 05/23/2011 11:45 AM VBROWN ----- 5908 RIVER RD # ON HOME & BY DRIVE FUQUAY VARINA 27526 T/S: 05/26/2011 11:45 AM TWARD -----
B113 01	5/24/11 5/24/11	BS AP	R*BLDG WATER/DAMP PROOFING TIME: 17:00 VRU #: 002084416 FOR PARTIAL BASEMENT AND DAMP PROOFING ON THE CRAWL.----- T/S: May 24, 2011 10:59 AM BSUTTON -----
B111 01	5/26/11 5/26/11	BS AP	R*BLDG SLAB INSP/TEMP SVC POLE TIME: 17:00 VRU #: 002085447 T/S: 05/25/2011 09:58 AM RDCONTE ----- BASEMENT SLAB INSPECTION T/S: May 26, 2011 10:02 AM BSUTTON -----

CONTINUED ONTO NEXT PAGE

ADDRESS : 5908 RIVER RD SUBDIV:
 CONTRACTOR : SCHUMACHER HOMES OF NC, INC PHONE : (330) 478-4505
 OWNER : PROUGH WILLIAM T & MARY C PHONE : (480) 543-8174
 PARCEL : 05-0624- - -0029- -02-
 APPL NUMBER: 11-50026245 CP NEW RESIDENTIAL (SFD)

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B105 01	6/06/11 6/06/11	KS AP	R*OPEN FLOOR TIME: 17:00 VRU #: 002088771 T/S: 06/02/2011 01:00 PM RDCONTE ----- T/S: 06/02/2011 02:30 PM NTART -----
R425 01	6/20/11 6/20/11	BS DA	FOUR TRADE ROUGH IN TIME: 17:00 VRU #: 002096824 T/S: 06/17/2011 01:19 PM JBROCK ----- 1. Finish roofing and all flashings. 2. Finish chimney through roof and leave exposed for inspection 3. Firecaulk wire for basement smoke detector and 3 inch drain in washroom. 4. Need hurricane ties on front wall of house, trusses are cantilevered. OK TO SIDE/Insulate walls. Will recheck all at insulation
I129 01	6/28/11 6/28/11	BS AP	R*INSULATION INSPECTION TIME: 17:00 VRU #: 002100329 T/S: 06/24/2011 02:52 PM RDCONTE ----- T/S: June 28, 2011 02:47 PM BSUTTON -----
R425 02	6/28/11 6/28/11	BS AP	FOUR TRADE ROUGH IN TIME: 17:00 VRU #: 002100311 T/S: 06/24/2011 02:52 PM RDCONTE ----- T/S: June 28, 2011 02:47 PM BSUTTON -----
H824 01	7/25/11 7/25/11	JM AP	ENVIR. OPERATIONS PERMIT TIME: 17:00 VRU #: 002114502 T/S: 07/26/2011 10:37 AM SZIMMER ----- T/S: 07/26/2011 10:38 AM SZIMMER -----
M305 01	7/27/11 7/27/11	BS CA	R*PLUMB SEWER CONNECTION TIME: 17:00 VRU #: 002114379 CHECK AT FINAL 1 10:12 AM BSUTTON -----
P307 01	8/15/11 <u>8-15-11</u>	TI <u>APBS</u>	R*PLUMB WATER CONNECTION TIME: 17:00 VRU #: 002123107 T/S: 08/12/2011 11:41 AM DJOHNSON -----
R429 01	8/15/11 <u>8/15/11</u>	TI <u>APBS</u>	FOUR TRADE FINAL TIME: 17:00 VRU #: 002123099 T/S: 08/12/2011 11:39 AM DJOHNSON -----

COMMENTS AND NOTES

64996207
