

**COUNTY OF HARNETT**  
**Building Inspections Department**  
**Planning Services**

**Certificate of Compliance:** \_\_\_\_\_ **Occupancy:** X

Certificate issued pursuant to the requirements of North Carolina General Statute 153A-363 and Harnett County Zoning Ordinances. This certifies at the time of issuance, this structure was in compliance with the various ordinances of the County of Harnett and the North Carolina State Building Codes. For the following:

Use Classification: Residential

Name: Stanci Builders Inc

Address: 188 Gunner Ct  
Broadway, NC 27505

Date: 11-26-13

Building Official: \_\_\_\_\_

**Permit Numbers**

Building: \_\_\_\_\_


Electrical: \_\_\_\_\_


Insulation: \_\_\_\_\_

Plumbing: \_\_\_\_\_

Mechanical: 12-50029294

MFG Home: \_\_\_\_\_



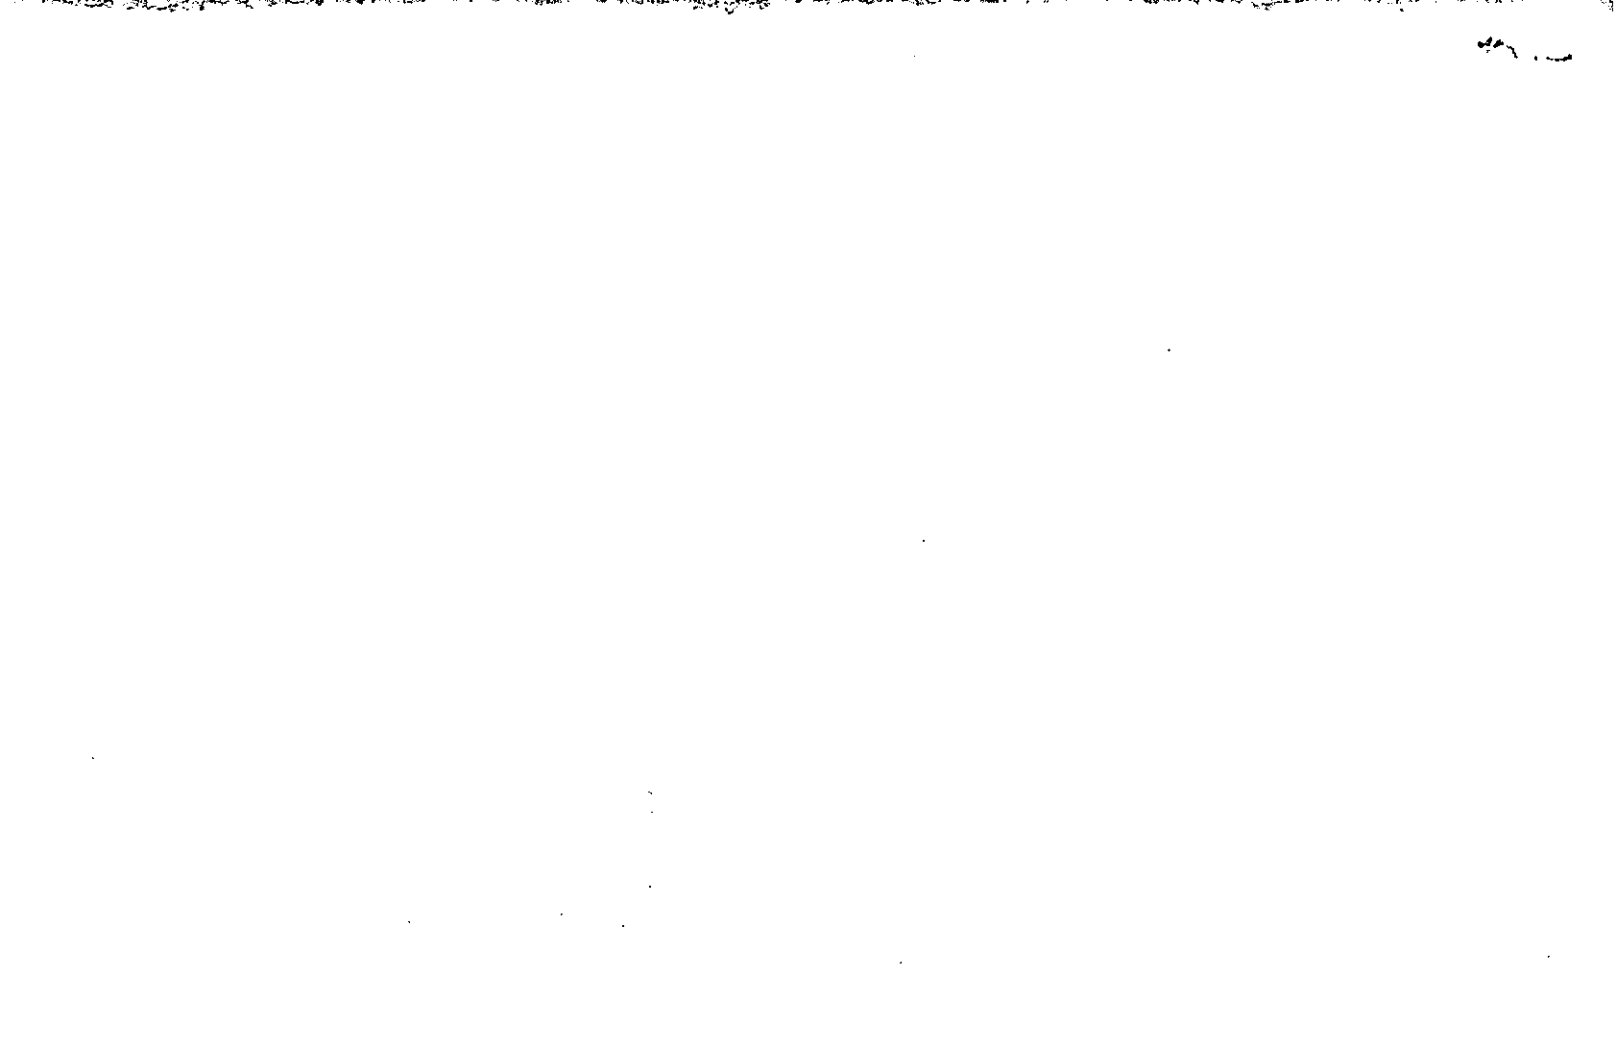

ADDRESS : 188 GUNNER CT SUBDIV: PATTONS POINT PH 2 73LOTS  
CONTRACTOR : STANCIL BUILDERS INC. PHONE : (919) 639-2073  
OWNER : STANCIL BUILDERS INC PHONE :  
PARCEL : 03-9597- - -0225- -27-  
APPL NUMBER: 12-50029294 CP NEW RESIDENTIAL (SFD)  
DIRECTIONS : T/S: 07/04/2012 04:21 PM VBROWN ----  
188 GUNNER COURT BROADWAY 27505 PATTONS  
POINT #147.

STRUCTURE: 000 000 52X35 3BDR 2BATH SFD W GAR DECK CRAWL

FLOOD ZONE : FLOOD ZONE X  
# BEDROOMS : 3.00 PROPOSED USE : SFD  
SEPTIC - EXISTING? : NEW TANK WATER SUPPLY : COUNTY

PERMIT: CPSF 00 CP \* SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	3/20/13	FS	R*BLDG FOOTING / TEMP SVC POLE VRU #: 002353544
	3/20/13	AP	T/S: 03/20/2013 02:17 PM FSPIVEY
B103 01	4/10/13	MR	R*BLDG FOUND & TEMP SVC POLE VRU #: 002363695
	4/10/13	AP	T/S: 04/10/2013 01:04 PM MREARIC
B105 01	5/13/13	JH	R*OPEN FLOOR VRU #: 002380943
	5/13/13	AP	
A814 01	6/28/13	TW	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 002404341
	7/02/13	AP	188 GUNNER CT BROADWAY 27505
			T/S: 07/02/2013 10:36 AM TWARD
R425 01	6/28/13	MR	FOUR TRADE ROUGH IN TIME: 17:00 VRU #: 002404333
	6/28/13	DA	T/S: 06/28/2013 01:14 PM MREARIC
			no water in riser / lvl's that butt together must have a hanger connector / all steps in garage to be the same height except bottom step
R425 02	7/12/13	MR	FOUR TRADE ROUGH IN VRU #: 002409129
	7/12/13	DA	T/S: 07/12/2013 02:56 PM MREARIC
			wire broken at upstairs bedroom wall ok to insulate
I129 01	7/25/13	MR	R*INSULATION INSPECTION VRU #: 002414818
	7/25/13	AP	T/S: 07/25/2013 02:40 PM MREARIC
R425 03	7/25/13	MR	FOUR TRADE ROUGH IN TIME: 17:00 VRU #: 002415511
	7/25/13	AP	T/S: 07/24/2013 02:45 PM DJOHNSON
			MAKE SURE FAILED ROUGH INS ARE SCHEDULED WITH THE INSULATION INSPECTION. IF ROUGH INS ARE NOT THEN THE INSULATION WILL BE CANCELLED.
			T/S: 07/25/2013 02:44 PM MREARIC
H824 01	9/17/13	OT	ENVIR. OPERATIONS PERMIT TIME: 17:00 VRU #: 002445021
	9/17/13	AP	T/S: 09/25/2013 04:36 PM SSTEWARD
			T/S: 09/25/2013 04:37 PM SSTEWARD
R429 01	11/26/13	TI	FOUR TRADE FINAL TIME: 17:00 VRU #: 002470128
	11/26/13	AP DT	T/S: 11/25/2013 12:51 PM DJOHNSON

COMMENTS AND NOTES
