

COUNTY OF HARNETT
Building Inspections Department
Planning Services

Certificate of Compliance: _____ **Occupancy:** _____

Certificate issued pursuant to the requirements of North Carolina General Statute 153A-363 and Harnett County Zoning Ordinances. This certifies at the time of issuance, this structure was in compliance with the various ordinances of the County of Harnett and the North Carolina State Building Codes. For the following:

Use Classification: SFD

Name: Comfort Homes Inc

Address: 99 Saddlebrook Dr
Fuquay Varina NC 27526

Permit Numbers

Building: 14-5-34943

Electrical: 14-5-34943

Insulation: 14-5-34943


Plumbing: 14-5-34943

Mechanical: 14-5-34943

MFG Home: _____

Date: 4-9-15

Building Official: [Signature]

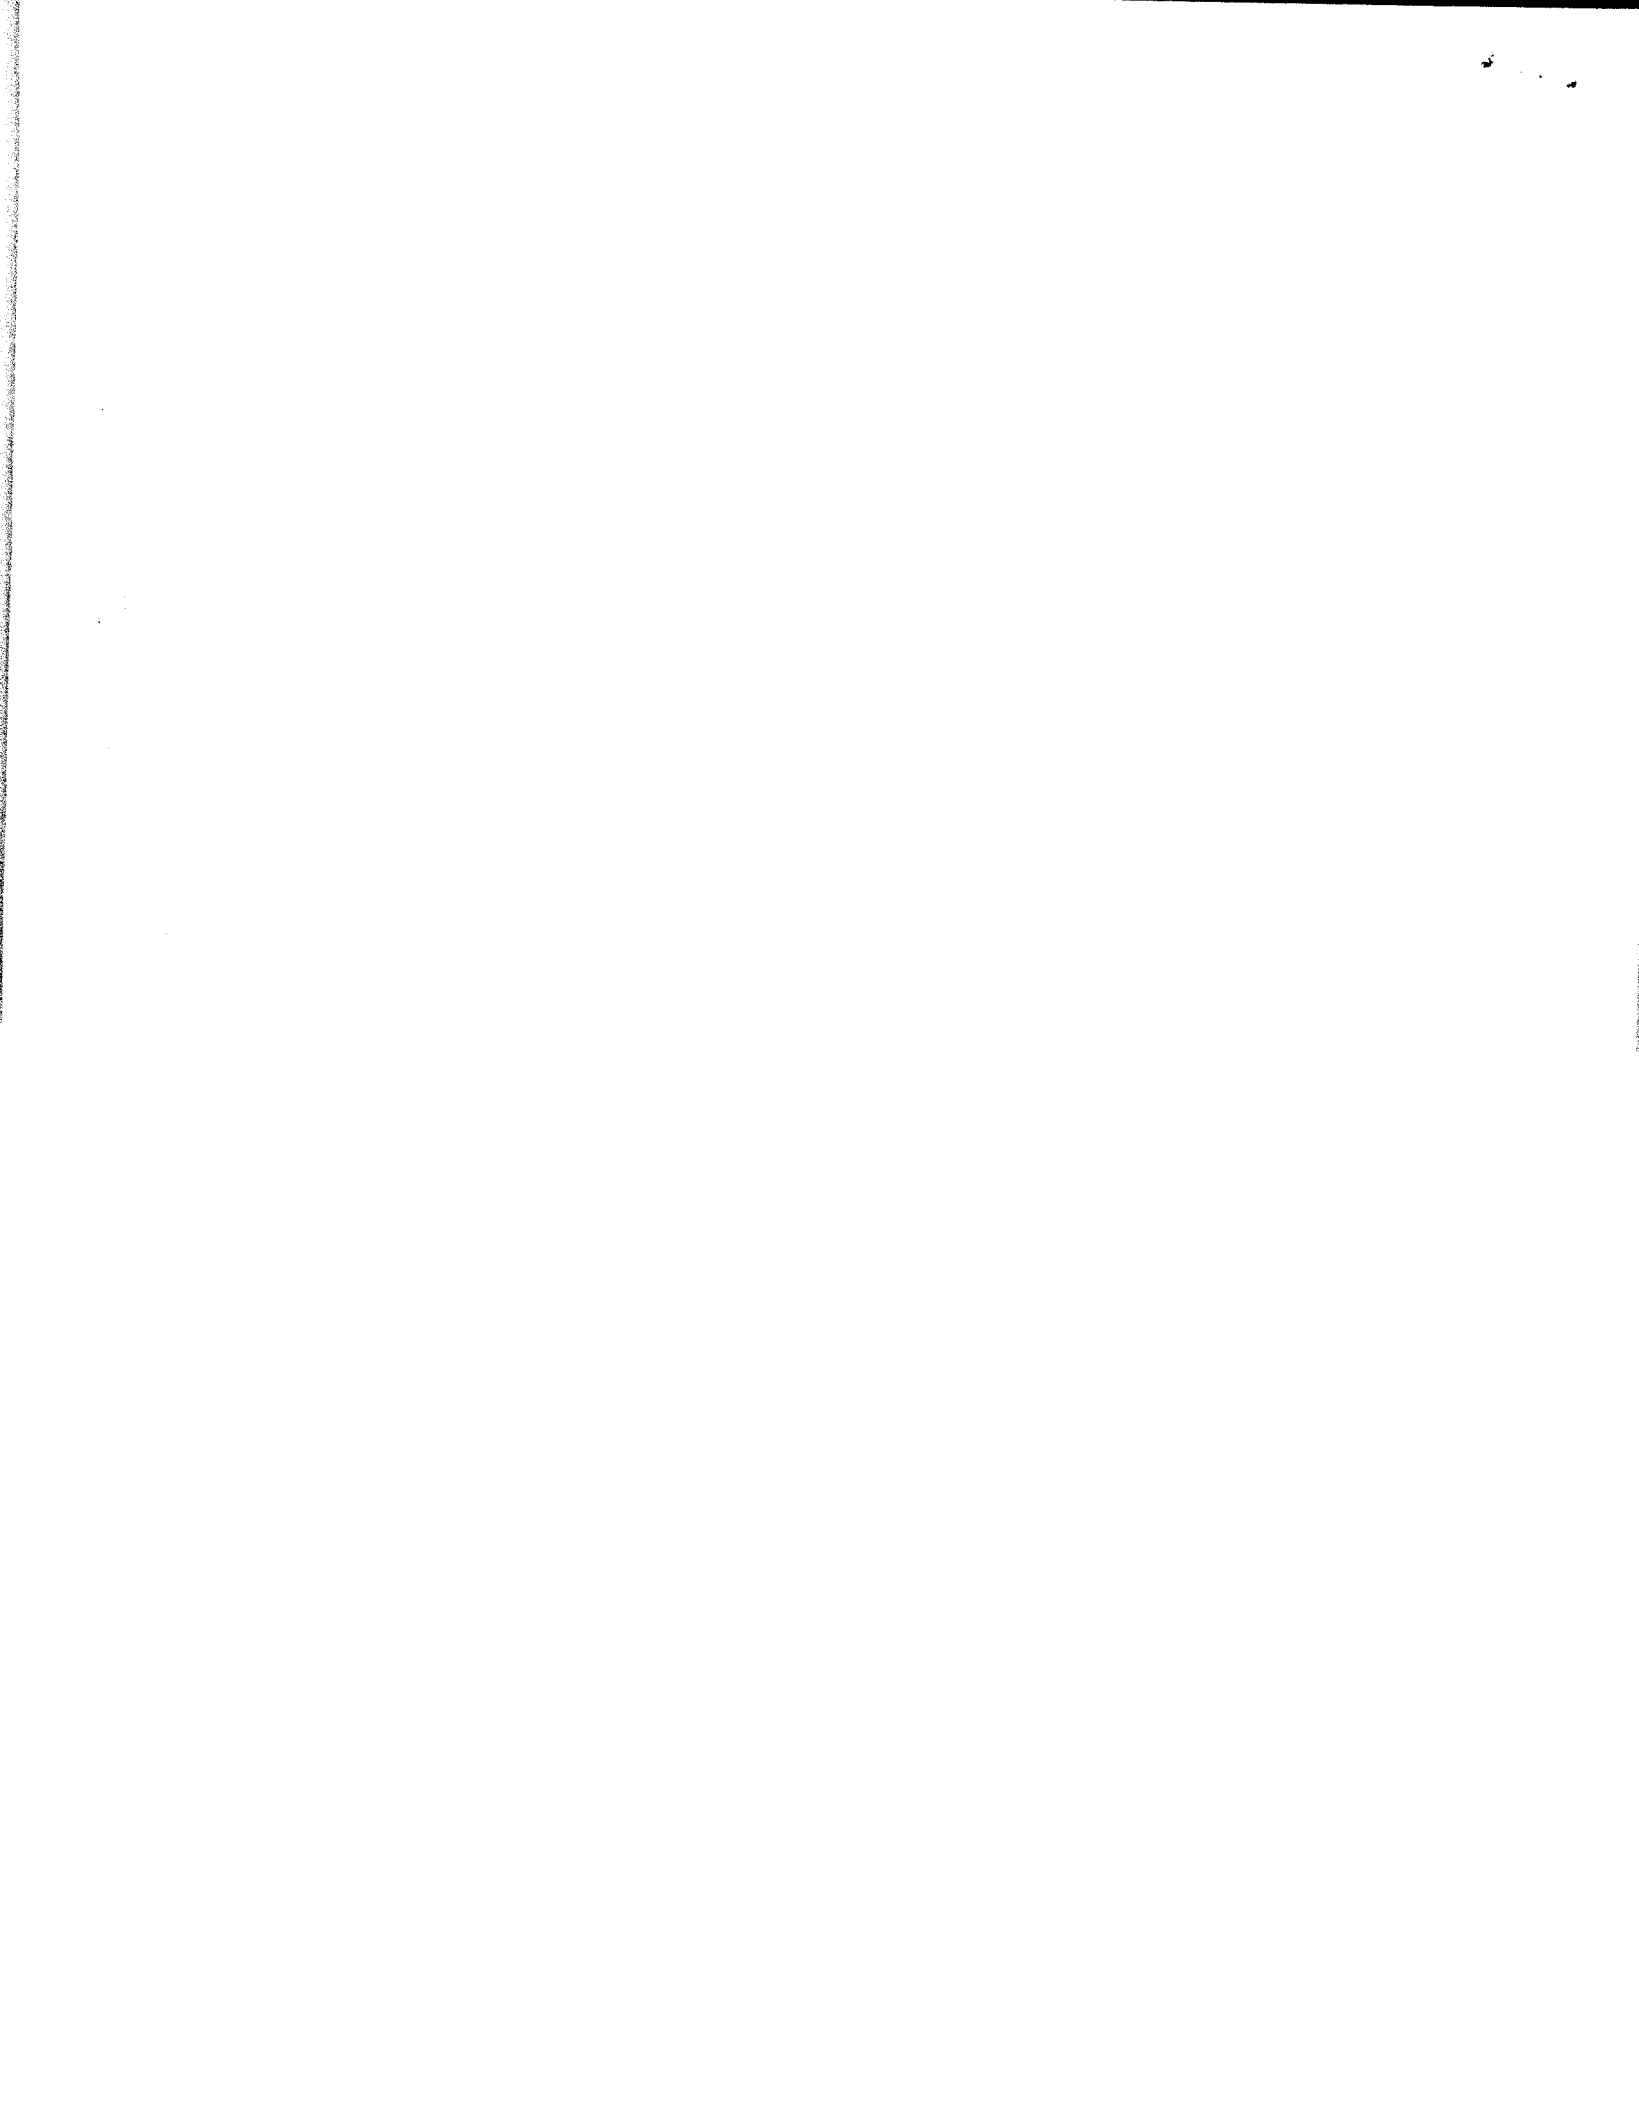


ADDRESS : 99 SADDLEBROOK DR SUBDIV: STETSON 53LOTS
 CONTRACTOR : COMFORT HOMES INC PHONE : (919) 553-3242
 OWNER : FISH BROTHERS INC PHONE :
 PARCEL : 04-0674- - -0046- -40-
 APPL NUMBER: 14-50034943 CP NEW RESIDENTIAL (SFD)
 DIRECTIONS : T/S: 11/17/2014 09:00 AM VBROWN ----
 99 SADDLEBROOK DRIVE FUQ VAR, STETSON
 SUB DIV #99

STRUCTURE: 000 000 70X37 3BDR 2BATH SFD W GAR DECK CRAWL

FLOOD ZONE : FLOOD ZONE X
 # BEDROOMS : 3.00 PROPOSED USE : SFD
 SEPTIC - EXISTING? : NEW TANK WATER SUPPLY : COUNTY

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	12/16/14	DT	R*BLDG FOOTING / TEMP SVC POLE VRU #: 002609332 T/S: 12/16/2014 03:07 PM DETAYLOR -----
A814 01	1/23/15	SB	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 002620102 T/S: 01/22/2015 09:09 AM VBROWN ----- T/S: 01/23/2015 08:40 AM SBENNETT ----- 99 SADDLEBROOK DR FUQUAY VARINA 27526 POST# ON HOME
B103 01	1/23/15	MR	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 002620094 T/S: 01/22/2015 09:09 AM VBROWN ----- T/S: 01/23/2015 01:17 PM MREARIC ----- need premise #
B105 01	2/03/15	DT	R*OPEN FLOOR VRU #: 002623700 T/S: 02/03/2015 03:07 PM DETAYLOR -----
R425 01	2/16/15	BS	FOUR TRADE ROUGH IN TIME: 17:00 VRU #: 002627479 T/S: February 16, 2015 02:47 PM BSUTTON ----- Install missing windows at rear door. Do not cover this area. Ok to insulate.
I129 01	2/20/15	BS	R*INSULATION INSPECTION TIME: 17:00 VRU #: 002628170 T/S: 02/18/2015 01:54 PM LBENNETT ----- T/S: 02/18/2015 02:00 PM VBROWN ----- T/S: 02/19/2015 12:32 PM DJOHNSON ----- T/S: 02/19/2015 12:32 PM DJOHNSON ----- T/S: February 20, 2015 02:54 PM BSUTTON -----
R425 02	2/20/15	BS	FOUR TRADE ROUGH IN TIME: 17:00 VRU #: 002628188 T/S: 02/18/2015 02:01 PM VBROWN ----- T/S: 02/19/2015 12:32 PM DJOHNSON ----- T/S: 02/19/2015 12:32 PM DJOHNSON ----- T/S: February 20, 2015 02:54 PM BSUTTON -----
H824 01	3/04/15	JM	ENVIR. OPERATIONS PERMIT TIME: 17:00 VRU #: 002631406 T/S: 03/05/2015 09:47 AM SSTEWARD ----- T/S: 03/05/2015 09:48 AM SSTEWARD -----
R429 01	4/09/15	TI	FOUR TRADE FINAL TIME: 17:00 VRU #: 002643567 T/S: 04/07/2015 01:30 PM LBENNETT -----

4-9-15


COMMENTS AND NOTES
