

-----

ADDRESS . . : 588 ROBERTS RD SUBDIV:  
 CONTRACTOR : MARKS MOBILE HOME SET-UP PHONE : (919) 499-2768  
 OWNER . . : FRIZZELLE RUSTY KIRT PHONE :  
 PARCEL . . : 03-9586- - -0053- - -  
 APPL NUMBER: 10-50023966 CP MANUFACTURED HOME RA20R/RA20M CRITERIA  
 DIRECTIONS : T/S: 03/12/2010 03:47 PM VBROWN ----  
 DWMH NEAR 588 ROBERTS ROAD SANFORD NC  
 27332. 27W, LEFT ON BUFFALO LAKES RD,  
 RIGHT AT HIGHLAND ELEMENTARY SCHOOL ON  
 ROBERTS RD, APPROX 1/2MI ON RIGHT 588  
 ON MAILBOX AT GATE. CALL CUSTOMER GATE  
 LOCKED CUSTOMER RUSTY FRIZZELLE CELL  
 NUMBER 919 770 0394.

-----

STRUCTURE: 000 000 28X44 3BDR DWMH  
 FLOOD ZONE . . . . : FLOOD ZONE X  
 # BEDROOMS . . . . . : 3.00 MOBILE HOME YEAR . . . . . : .00  
 PROPOSED USE . . . . . : DWMH SEPTIC - EXISTING? . . . . . : NEW SEPTIC  
 WATER SUPPLY . . . . . : COUNTY

PERMIT: CPDW 00 CP MOBILE HOME DOUBLEWIDE

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
H824 01	5/18/10	OT	ENVIR. OPERATIONS PERMIT TIME: 17:00 VRU #: 001929397
	5/18/10	AP	T/S: 05/19/2010 10:39 AM SSTEWARD ----- T/S: 05/19/2010 10:39 AM SSTEWARD -----
T501 01	7/01/10	TI	R*MOBILE HOME FOUND./ M. WALL VRU #: 001948192
	<u>7-1-10</u>	<u>DA-MB</u>	

----- COMMENTS AND NOTES -----

Plumb -OK  
 Eng. Needed  
 For elevated Pies

ADDRESS : 588 ROBERTS RD SUBDIV:  
CONTRACTOR : MARKS MOBILE HOME SET-UP PHONE : (919) 499-2768  
OWNER : FRIZZELLE RUSTY KIRT PHONE :  
PARCEL : 03-9586- - -0053- - -  
APPL NUMBER: 10-50023966 CP MANUFACTURED HOME RA20R/RA20M CRITERIA  
DIRECTIONS : T/S: 03/12/2010 03:47 PM VBROWN ----  
DWMH NEAR 588 ROBERTS ROAD SANFORD NC  
27332. 27W, LEFT ON BUFFALO LAKES RD,  
RIGHT AT HIGHLAND ELEMENTARY SCHOOL ON  
ROBERTS RD, APPROX 1/2MI ON RIGHT 588  
ON MAILBOX AT GATE. CALL CUSTOMER GATE  
LOCKED CUSTOMER RUSTY FRIZZELLE CELL  
NUMBER 919 770 0394.

STRUCTURE: 000 000 28X44 3BDR DWMH  
FLOOD ZONE : FLOOD ZONE X  
# BEDROOMS : 3.00 MOBILE HOME YEAR : .00  
PROPOSED USE : DWMH SEPTIC - EXISTING? : NEW SEPTIC  
WATER SUPPLY : COUNTY

PERMIT: CPDW 00 CP MOBILE HOME DOUBLEWIDE

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
H824 01	5/18/10 5/18/10	OT AP	ENVIR. OPERATIONS PERMIT TIME: 17:00 VRU #: 001929397 T/S: 05/19/2010 10:39 AM SSTEWARD T/S: 05/19/2010 10:39 AM SSTEWARD
T501 01	7/01/10 7/01/10	MR DA	R*MOBILE HOME FOUND./ M. WALL VRU #: 001948192 T/S: 07/01/2010 09:57 AM MREARIC plmb and marriage ok but you need an engineer to ok piers as more than 25% are over 3' from grade.
T501 02	7/06/10	TI AP-MR	T/S: 07/01/2010 12:14 PM MREARIC R*MOBILE HOME FOUND./ M. WALL VRU #: 001949832

COMMENTS AND NOTES

Rec'd letter  
Robt Becken

# RJB, P.E., P.A.

ROBERT J. BRACKEN  
ENGINEER • SURVEYOR

3768 Carbonton Road • Sanford, North Carolina 27330

(919) 774-6074

July 2, 2010

Harnett County Building Inspectors  
P.O. Box 65  
Lillington, NC 27546

REF: Over-Height Ltr.  
Rusty Frizzelle, Res.  
588 Roberts Rd  
Harnett Co, NC

Dear Sir/Madam:

I made an onsite inspection of the double-wide mobile home referenced above. The highest point of the chassis above the existing grade was approximately 58 inches. The existing tie downs and piers are adequate, see attached sketch. It is my opinion that the mobile home is anchored adequately to resist the wind pressures in the area, and meets or exceeds the requirements set forth in the State of N.C. Regulations For Manufactured Homes Edition 2004.

I always suggest that after about six months, when the home has had time to settle, that all of the hold down straps be retightened.

If you have any questions call 919-774-6074.


Sincerely,




Robert J. Bracken, PE

RJB:jeb


Attachment



44'

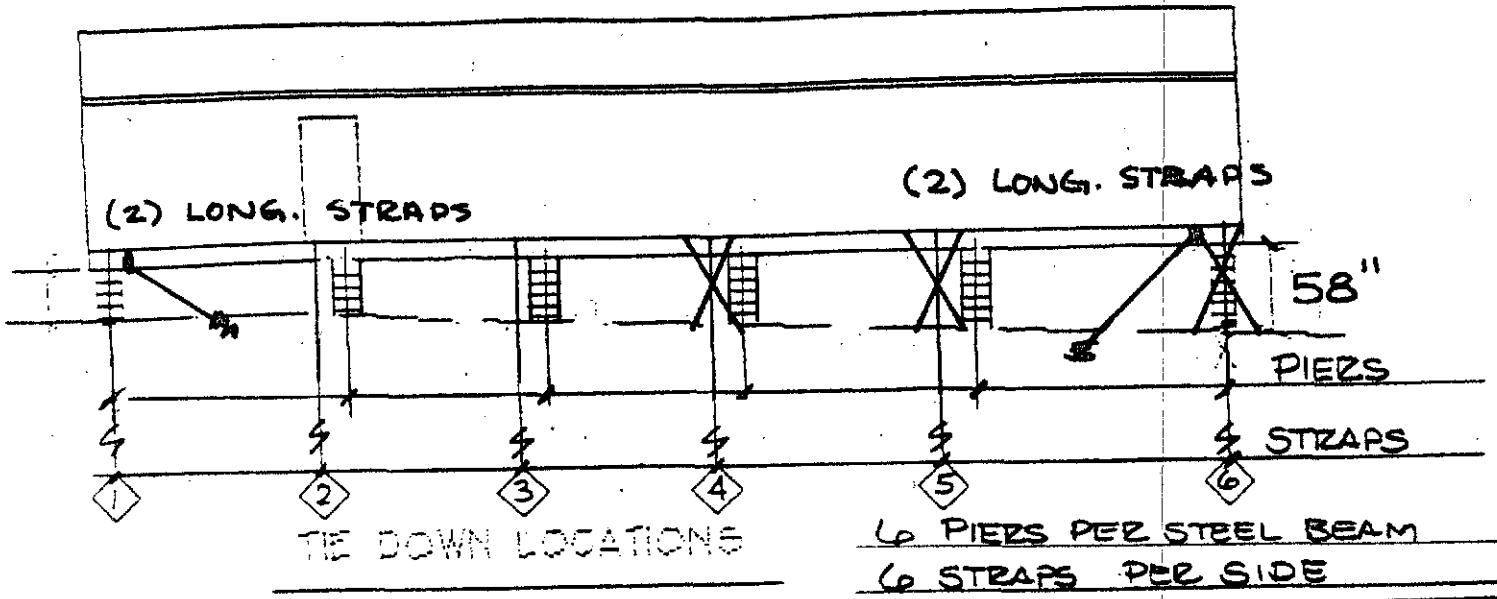


NOTE: CROSS STRAPS  
REQUIRED @ LOCATIONS  
4, 5, & 6

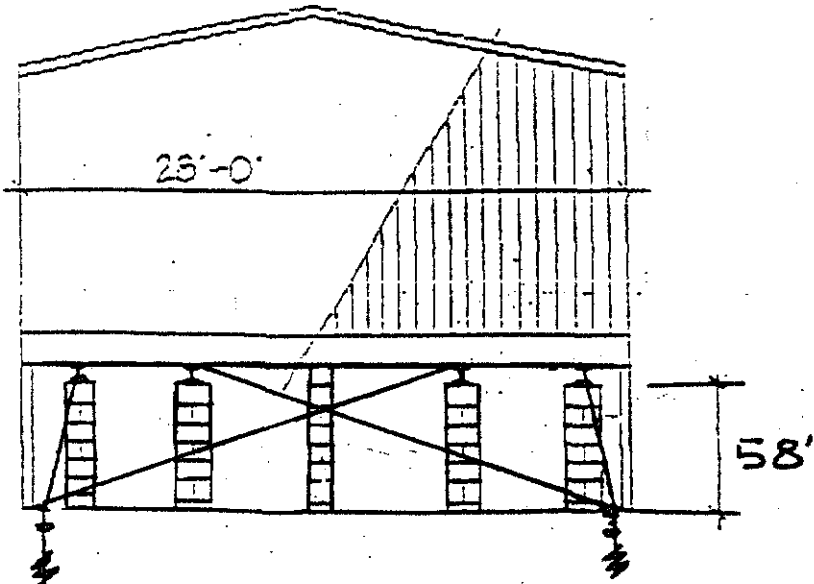

END VIEW SHOWING  
CROSS STRAPS  
16x16 PIERS AT ALL  
LOCATIONS OVER 40" HIGH  
UNDER STEEL "I" BEAM

DOUBLE WIDE M.H  
RUSTY FRIZZELLE RES  
588 ROBERTS RD  
HARNETT CO

NORTH CAROLINA  
DATE: JULY 2, 2010  
SCALE: NONE



**BRACKEN & ASSOCIATES**  
ENGINEERING • SURVEYING  
P. O. BOX 532 • SANFORD NC 27330  
OFF (919) 776-5622 Fax (919) 774-6717

ADDRESS : 588 ROBERTS RD SUBDIV:  
 CONTRACTOR : MARKS MOBILE HOME SET-UP PHONE : (919) 499-2768  
 OWNER : FRIZZELLE RUSTY KIRT PHONE :  
 PARCEL : 03-9586- - -0053- - -  
 APPL NUMBER: 10-50023966 CP MANUFACTURED HOME RA20R/RA20M CRITERIA  
 DIRECTIONS : T/S: 03/12/2010 03:47 PM VBROWN ----  
 DWMH NEAR 588 ROBERTS ROAD SANFORD NC  
 27332. 27W, LEFT ON BUFFALO LAKES RD,  
 RIGHT AT HIGHLAND ELEMENTARY SCHOOL ON  
 ROBERTS RD, APPROX 1/2MI ON RIGHT 588  
 ON MAILBOX AT GATE. CALL CUSTOMER GATE  
 LOCKED CUSTOMER RUSTY FRIZZELLE CELL  
 NUMBER 919 770 0394.

**STRUCTURE: 000 000 28X44 3BDR DWMH**

FLOOD ZONE : FLOOD ZONE X  
 # BEDROOMS : 3.00 MOBILE HOME YEAR : .00  
 PROPOSED USE : DWMH SEPTIC - EXISTING? : NEW SEPTIC  
 WATER SUPPLY : COUNTY

**PERMIT: CPDW 00 CP MOBILE HOME DOUBLEWIDE**

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
H824 01	5/18/10 5/18/10	OT AP	ENVIR. OPERATIONS PERMIT TIME: 17:00 VRU #: 001929397 T/S: 05/19/2010 10:39 AM SSTEWARD T/S: 05/19/2010 10:39 AM SSTEWARD
T501 01	7/01/10 7/01/10	MR DA	R*MOBILE HOME FOUND./ M. WALL VRU #: 001948192 T/S: 07/01/2010 09:57 AM MREARIC plmb and marriage ok but you need an engineer to ok piers as more than 25% are over 3' from grade.
T501 02	7/06/10 7/06/10	MR AP	R*MOBILE HOME FOUND./ M. WALL VRU #: 001949832 T/S: 07/06/2010 12:21 PM MREARIC rec.d letter
A814 01	7/20/10 7/20/10	FB AP	ADDRESS CONFIRMATION VRU #: 001956358 T/S: 07/20/2010 03:54 PM FBURGESS 590 ROBERTS RD SANFORD, NC 27332
Z818 01	10/12/10 <u>10/12/10</u>	TI <u>RB/AP</u>	PZ*ZONING INSPECTION VRU #: 001992348

COMMENTS AND NOTES

ADDRESS : 588 ROBERTS RD SUBDIV:  
 CONTRACTOR : MARKS MOBILE HOME SET-UP PHONE : (919) 499-2768  
 OWNER : FRIZZELLE RUSTY KIRT PHONE :  
 PARCEL : 03-9586- - -0053- - -  
 APPL NUMBER: 10-50023966 CP MANUFACTURED HOME RA20R/RA20M CRITERIA

DIRECTIONS : T/S: 03/12/2010 03:47 PM VBROWN ----  
 DWMH NEAR 588 ROBERTS ROAD SANFORD NC  
 27332. 27W, LEFT ON BUFFALO LAKES RD,  
 RIGHT AT HIGHLAND ELEMENTARY SCHOOL ON  
 ROBERTS RD, APPROX 1/2MI ON RIGHT 588  
 ON MAILBOX AT GATE. CALL CUSTOMER GATE  
 LOCKED CUSTOMER RUSTY FRIZZELLE CELL  
 NUMBER 919 770 0394.

STRUCTURE: 000 000 28X44 3BDR DWMH  
 FLOOD ZONE : FLOOD ZONE X  
 # BEDROOMS : 3.00 MOBILE HOME YEAR : .00  
 PROPOSED USE : DWMH SEPTIC - EXISTING? : NEW SEPTIC  
 WATER SUPPLY : COUNTY

PERMIT: CPDW 00 CP MOBILE HOME DOUBLEWIDE

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
H824 01	5/18/10 5/18/10	OT AP	ENVIR. OPERATIONS PERMIT TIME: 17:00 VRU #: 001929397 T/S: 05/19/2010 10:39 AM SSTEWARD T/S: 05/19/2010 10:39 AM SSTEWARD
T501 01	7/01/10 7/01/10	MR DA	R*MOBILE HOME FOUND./ M. WALL VRU #: 001948192 T/S: 07/01/2010 09:57 AM MREARIC plmb and marriage ok but you need an engineer to ok piers as more than 25% are over 3' from grade.
T501 02	7/06/10 7/06/10	MR AP	R*MOBILE HOME FOUND./ M. WALL VRU #: 001949832 T/S: 07/06/2010 12:21 PM MREARIC rec.d letter
A814 01	7/20/10 7/20/10	FB AP	ADDRESS CONFIRMATION VRU #: 001956358 T/S: 07/20/2010 03:54 PM FBURGESS 590 ROBERTS RD SANFORD, NC 27332
Z818 01	10/12/10 10/12/10	RB AP	PZ*ZONING INSPECTION VRU #: 001992348 T/S: 10/12/2010 02:36 PM NTART
T507 01	10/13/10 10-13-10	TI AP-MR	R*MANUFACTURED HOME FINAL TIME: 17:00 VRU #: 001994128 T/S: 10/13/2010 11:55 AM NTART

COMMENTS AND NOTES

County of Harnett  
Building Inspections Department  
Planning Services

Certificate of Compliance: X Occupancy: X

Certificate issued pursuant to the requirements of North Carolina General Statute 153A-363 and Harnett County Zoning Ordinances. This certifies at the time of issuance, this structure was in compliance with the various ordinances of the County of Harnett and the North Carolina State Building Codes. For the following:

Use Classification: R-3 Manufactured

Permit Numbers

Name: Frizzel

Building: 10-50023966

Electrical: 11

Address: 590 Roberts Rd

Insulation: 11

Plumbing: 11

Mechanical: 11

MFG Home: \_\_\_\_\_

Date: 10-13-10

Building Official: T. Michael Ream
