

HTE 0450010946

16636

OPERATIONS PERMIT

Name: (owner) Regency Homes New Installation Septic Tank
 Property Location: SR# 1141 Repairs Nitrification Line
 Subdivision Highland Forest Lot # 92
 Tax ID # _____ Quadrant # _____
 Contractor: Ted Brown Registration # _____

Basement with Plumbing: Garage:

Water Supply: Well Public Community

Distance From Well: 50 ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system: Conventional Other 25% Reduction SYSTEM Infiltrator Quick U Chamber

Size of tank: Septic Tank: 1000 gallons Pump Tank: _____ gallons


Subsurface Drainage Field No. of ditches 1 exact length of each ditch 150 ft. width of ditches 3 ft. depth of ditches 18.30 in.

French Drain Required: _____ Linear feet 4 25% Red. SYSTEM

Date: 3-30-05

Inspected by: Jo WARS
Environmental Health Specialist

PERMIT NO. 21485

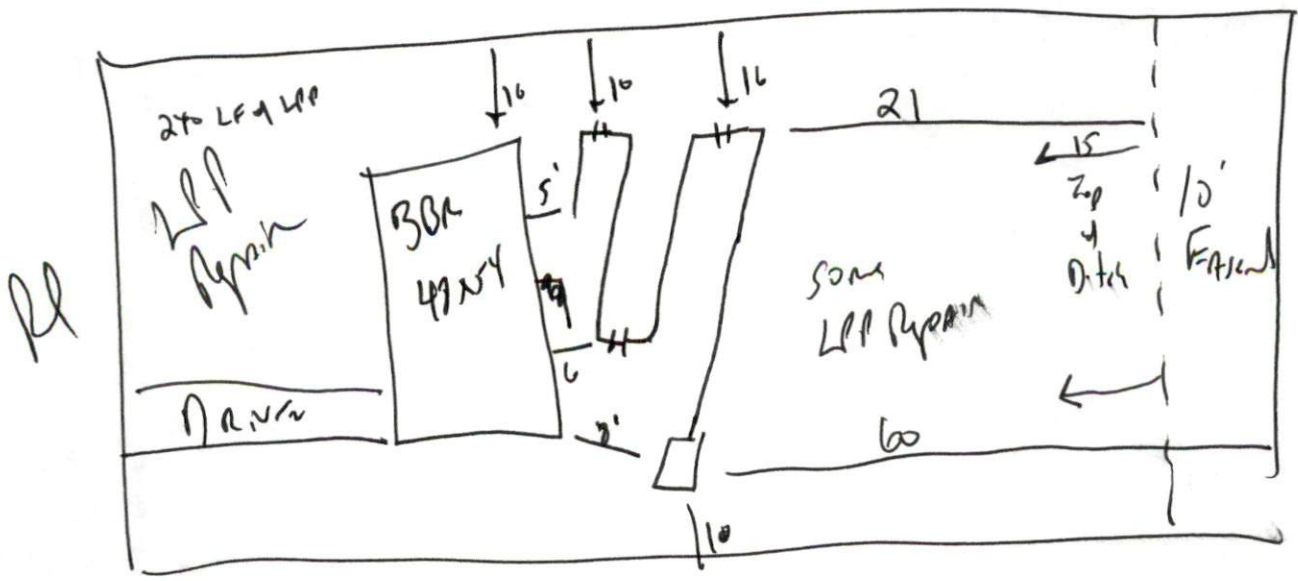

911-1000 570-107
