

Certificate of Completion

Nº 4146

Owner Ed Carrion Address Angier
(MUST BE FILLED IN) (MAILING ADDRESS)

Contractor _____ Address _____
(MAILING ADDRESS)

Location of Premises Benton Place Lot # 34
(SUBDIVISION, STREET OR ROAD NAME OR NUMBER, LOT NO.)
SR1504

Details of Septic Tank System

Kind of Material for Tank: Concrete Other _____

Size of Tank: Capacity 1000 Gallons


Subsurface Drainage Field No. of Ditches 2 Exact Length of each Ditch 100 Width of Ft. Ditches 3 Depth of Ft. Ditches 24 Inches

Square Feet in Absorption Field 600 Surface Drainage Required _____ Linear Ft. _____

Inspected by A. Rance
(SANITARIAN)

Permit No. 4568 Date 25 Apr 90

- Permit called for 3-100' lines
- SL soil was found down to 36"
 - 12" below bottom of trenches
- I can't foresee any problems w/ just 2 lines

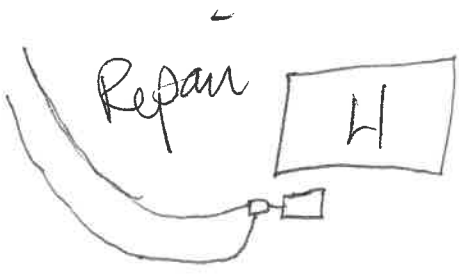

← May 210 SR 6509
