

CERTIFICATE OF COMPLETION / OPERATIONAL PERMIT


Name: (owner) Webb Builders New Installation Septic Tank
 Property Location: SR# Hwy 27 Repairs Nitrification Line
 Subdivision Mine Branch Lot # 92
 Contractor: Ted Brown Registration # 14
 Basement with Plumbing: Garage:
 Water Supply: Well Public Community
 Distance From Well: _____ ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system: Conventional Other _____
 Size of tank: Septic Tank: 1000 gallons Pump Tank: _____ gallons
 Subsurface No. of exact length width of depth of
 Drainage Field ditches 2 of each ditch 75 ft. ditches 3 ft. ditches 18-24 in.
 French Drain: _____ Linear feet

PERMIT NO. 7944 Date: 15 November, 1993
 Inspected by: [Signature]

Environmental Health Specialist

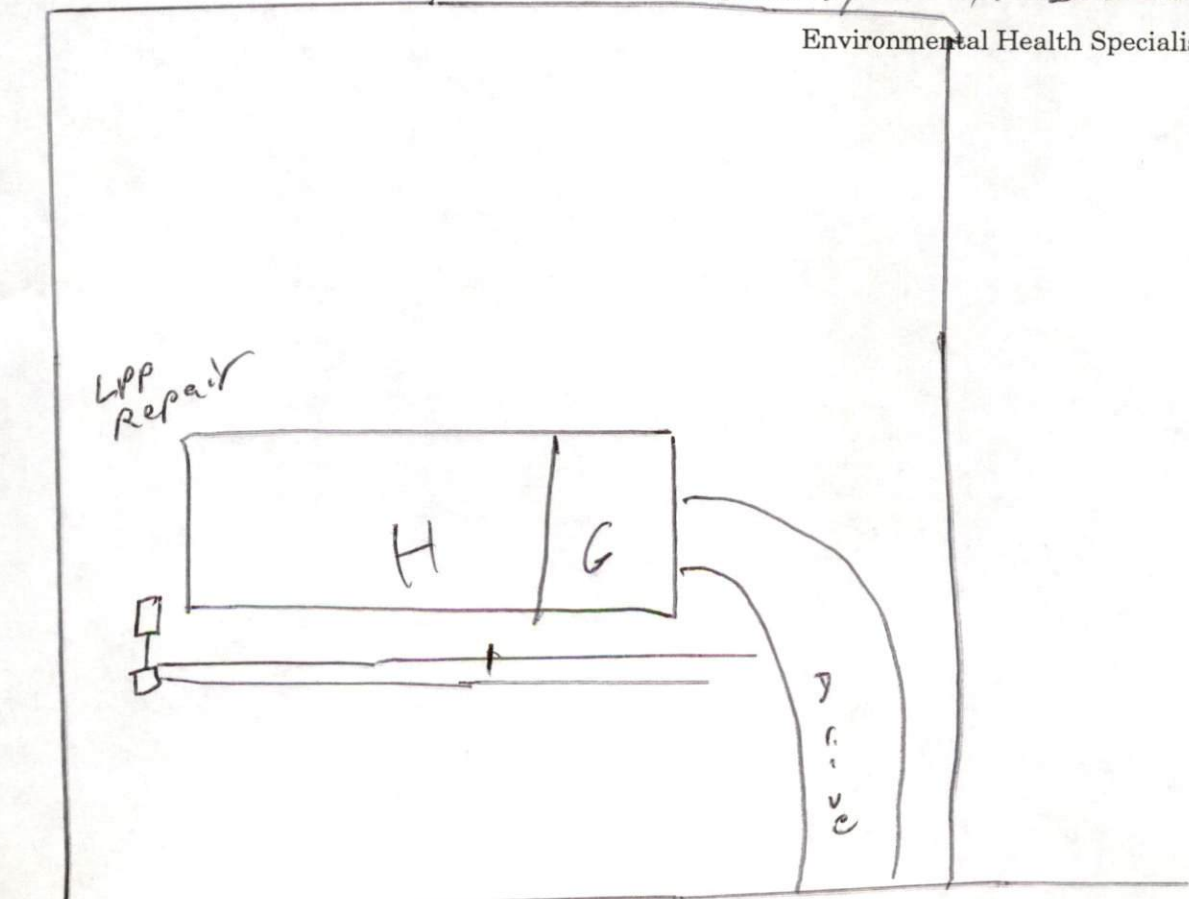

Lakewood Dr. (← to Hwy 27)
