

# CERTIFICATE OF COMPLETION / OPERATIONAL PERMIT

Name: (owner) Weaver Development  New Installation  Septic Tank  
Property Location: SR# HLM 87  Repairs  Nitrification Line  
Subdivision STARWOOD AT OVERHILL Lot # 25  
TAX ID# \_\_\_\_\_ Quadrant # \_\_\_\_\_  
Contractor: M<sup>c</sup>Cartor Registration # \_\_\_\_\_


Basement with Plumbing:  Garage:   
Water Supply:  Well  Public  Community  
Distance From Well: 50' min ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system:  Conventional  Other N/A  
Size of tank: Septic Tank: 1000 gallons Pump Tank: N/A gallons  
Subsurface Drainage Field No. of ditches 2 exact length of each ditch 120' width of ditches 3 ft. depth of ditches 30 in.  
French Drain: \_\_\_\_\_ Linear feet

PERMIT NO. 08848 Date: 11-1-74  
Inspected by: Joe W. A.

Environmental Health Specialist

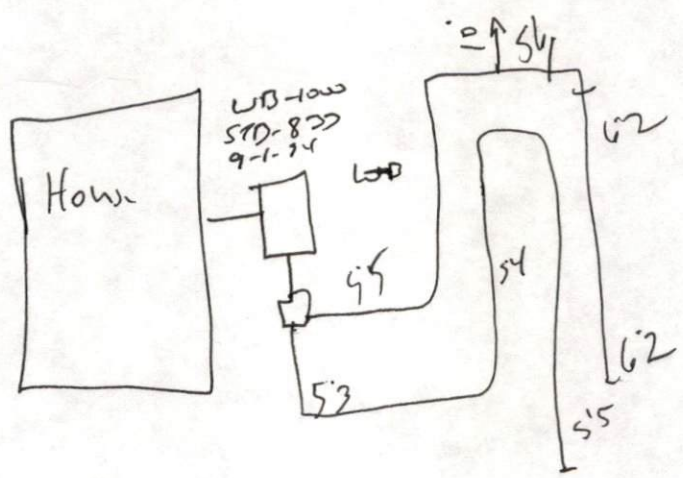

rd
