

# CERTIFICATE OF COMPLETION / OPERATIONAL PERMIT


Deliverence Church

Name: (owner) Chris Mullen/mullen Const.  New Installation  Septic Tank  
 Property Location: SR# 1006 + H<sub>2</sub> 55  Repairs  Nitrification Line  
 Subdivision \_\_\_\_\_ Lot # \_\_\_\_\_  
 Contractor: Southern Handy Registration # 66  
 Basement with Plumbing:  Garage:   
 Water Supply:  Well  Public  Community  
 Distance From Well: 50 ft. +

Following are the specifications for the sewage disposal system on above captioned property.

Type of system:  Conventional  Other \_\_\_\_\_  
 Size of tank: Septic Tank: 1200 gallons Pump Tank: \_\_\_\_\_ gallons  
 Subsurface Drainage Field No. of ditches 1 exact length of each ditch 430 ft. width of ditches 3 ft. depth of ditches 24 in.  
 French Drain: \_\_\_\_\_ Linear feet

PERMIT NO. 7330 Date: 09-13-93  
 Inspected by: John H. Boyd R.E.  
 Environmental Health Specialist

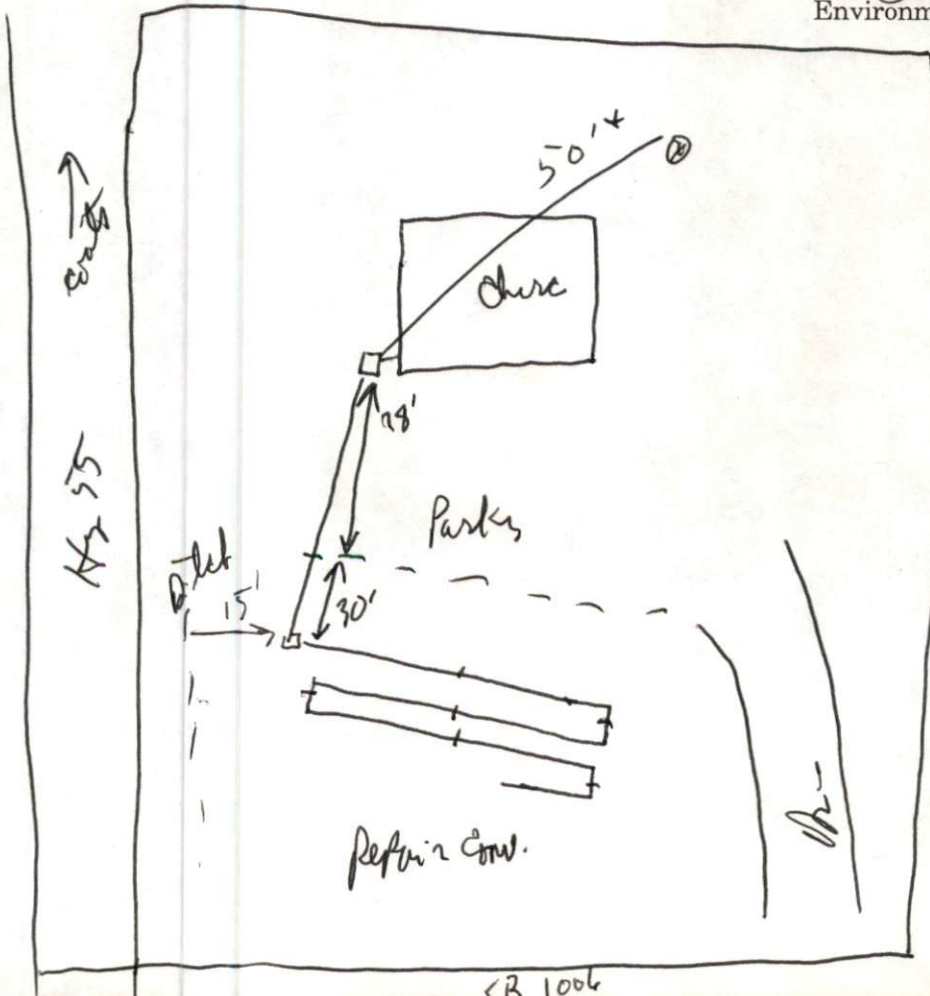

\* Supply Line was kept 30' + under paved area to 78' from Tank, and 30' from Dr-Box  
 \* Paved area is NOT to exceed these setbacks
