

CERTIFICATE OF COMPLETION / OPERATIONAL PERMIT

Name: (owner) Steve Allen ☒ New Installation ☒ Septic Tank
Property Location: SR# 210 ☐ Repairs ☒ Nitrification Line
Subdivision _____ Lot # 2
TAX ID# _____ Quadrant # _____
Contractor: Mike Ray Registration # _____
Basement with Plumbing: ☐ Garage: ☐
Water Supply: ☐ Well ☒ Public ☐ Community
Distance From Well: 50+ ft.

Following are the specifications for the sewage disposal system on above captioned property.


Type of system: ☒ Conventional ☐ Other Pump to cond lines
Size of tank: Septic Tank: 1000 gallons Pump Tank: 1000 gallons
Subsurface No. of exact length width of depth of
Drainage Field ditches 3 of each ditch 135 ft. ditches 3 ft. ditches 18-22 in.
French Drain: _____ Linear feet

PERMIT NO. 09789

Date: 2-23-96

Inspected by: Thomas J. Boyer R.S.

Environmental Health Specialist

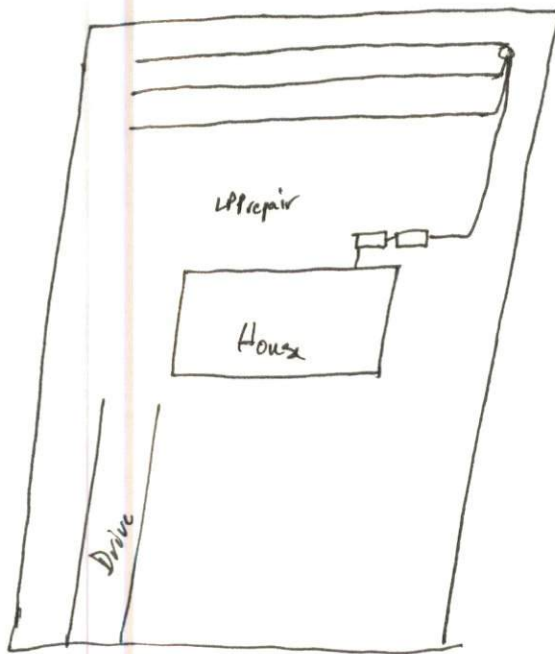

HWY 210
