



**ECS Southeast, LLP**

6151 Raeford Road, Suite A  
Fayetteville, NC 28304  
9104013288  
9103230539

**LETTER OF TRANSMITTAL**


November 6, 2020  
Boddie Noell Enterprises, Inc  
1021 Noell Lane PO Box 1908  
Rocky Mount, NC 27802  
ATTN: Tracy Miller

RE: **Hardee's Cameron**  
ECS Job # **33:5294**  
Permits:  
Location: **2471 NC Hwy 87 South**  
**Cameron, NC 28326**

	<input checked="" type="checkbox"/> Field Reports	<input checked="" type="checkbox"/> For your use	<input checked="" type="checkbox"/> As requested
CC:	Boddie Noell Enterprises, Inc - Reggie Barnacascel Grade-Rite - Marvin Edmundson Harnett County - Donna Johnson	R & L Builders & Sons, LLC - Jose Garcia R & L Builders & Sons, LLC - Ricky Barnhill R & L Builders & Sons, LLC - Stacey Langley	

ENCL: Field Report # 12      11/6/2020

  
\_\_\_\_\_  
Jack Edgar Cowsert, P.E.  
Senior Project Engineer

  
\_\_\_\_\_  
Ryan H. Parrish  
Construction Materials Project Manager

*Disclaimer*

1. This report (and any attachments) shall not be reproduced except in full without prior written approval of ECS.
2. The information in this report relates only to the activities performed on the report date.
3. Where appropriate, this report includes statements as to compliance with applicable project drawings, and specifications for the activities, performed on this report date.
4. Incomplete or non-conforming work will be reported for future resolution.
5. The results of samples and/or specimens obtained or prepared for subsequent laboratory testing will be presented in separate reports/documents.



ECS Southeast, LLP  
6151 Raeford Road, Suite A  
Fayetteville, NC 28304  
(910) 401-3288 [Phone]  
(910) 323-0539 [Fax]

# FIELD REPORT

Project **Hardee's Cameron**  
Location **Cameron, NC**  
Client **Boddie Noell Enterprises, Inc**  
Contractor **Boddie Noell Enterprises, Inc**

Project No. **33:5294**  
Report No. **12**  
Day & Date **Friday 11/6/2020**  
Weather **78 °/ Sunny**  
On-Site Time **2.25**  
Lab Time **0.25**  
Travel Time\* **1.00**  
Total **3.50**  
Re Obs Time **0.00**

Remarks

Trip Charges*	Tolls/Parking*	Mileage* <b>50</b>	Time of Arrival	Departure
Chargeable Items			<b>10:30A</b>	<b>12:45P</b>

\* Travel time and mileage will be billed in accordance with the contract.

**Summary of Services Performed (field test data, locations, elevations & depths are estimates) & Individuals Contacted.**

ECS arrived on site as requested to conduct asphalt coring for the Hardee's drive/parking lot.


Please see the attached sketch sheet for details.

A total of (5) 6" inch cores were collected at randomly selected locations. Asphalt thicknesses ranged from 3.0-6.5 inches.

Cores were returned to the ECS laboratory for specific gravity density testing. A letter will be provided by the ECS Project Manager at the completion of laboratory testing.

- Core,#1= 6.5" thick.
- Core,#2= 4.5" thick.
- Core,#3= 5.0" thick.
- Core,#4= 3.0" thick.
- Core,#5= 4.35" thick.

ECS will return upon request.

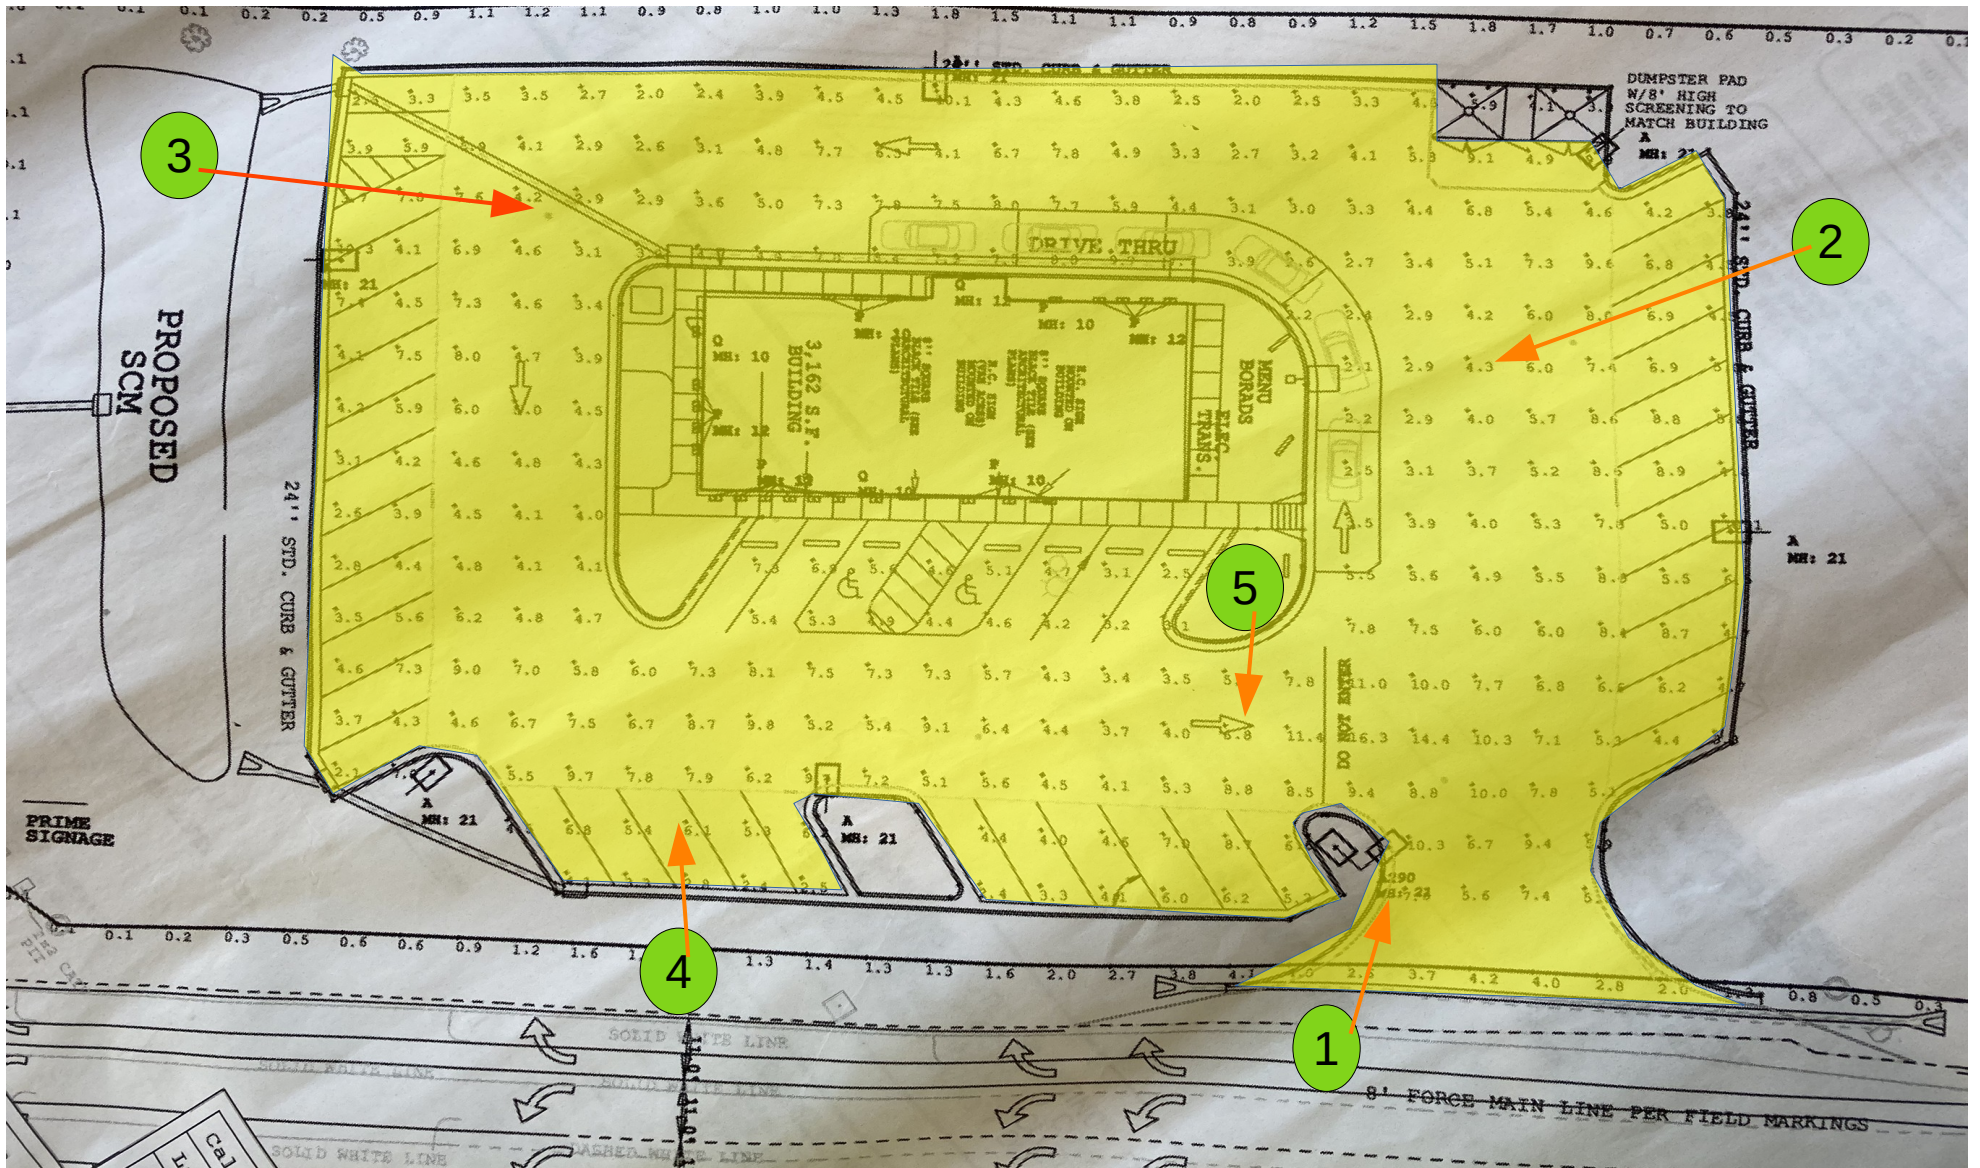

Gerald Bowling  
 6 NOV. 2020  
 Hardee's Cameron  
 Proj.#:5294  
 W/O#:59069

**Key:**

Parking lot asphalt coring



Core Locations

