




3d Community Church

659 Graham Rd Sanford, NC

9/3/25

Building Inspector
Harnett County

General contractor shall extend the one and two-hour fire rated wall framing and sheetrock tight to the roof insulation/tarp system. Apply fire caulk at the top of sheetrock. Allow deflection at the roof structure. — Follow UL Designs UL419 and V449. Provide top of wall condition at rated walls indicated in red and orange below.

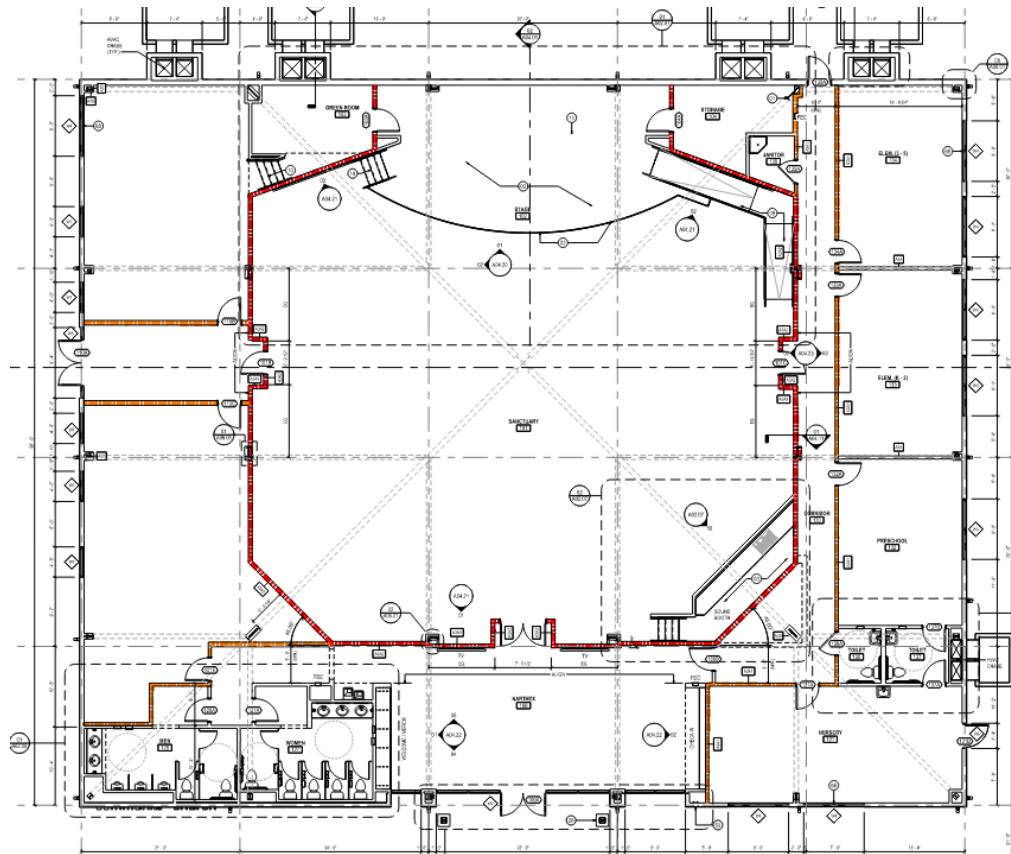

Jack Ossa, NCARB AIA LEED AP
Principal
9/3/25
