

Raleigh

5504 Commercial Avenue
Suite 102
Raleigh, NC 27612
Phone: 984.242.1950
Fax: 980.321.4099

Client:

RLC Construction Company, Inc.
414 E. Edgerton Street
Dunn, NC 28334

Project:

10727-1026045.000
192 Jarco Drive
192 Jarco Drive
Fuquay-Varina, NC

Activity Number: 6

Date: 08/03/2026

Weather: Cloudy

Temperature: 88

NOVA Representative: Randall Greer

General Contractor: RLC Construction Company, Inc.

NOVA representative arrived on site as requested to perform footing bearing capacity evaluations in the following locations:

- A.1/7.7

Footing evaluations consisted of visual observations, manual probing and Dynamic Cone Penetrometer (DCP) testing. Utilizing the DCP, testing was performed in the aforementioned locations at various depths below bearing elevation. Test results determined that material in the areas and at the elevations tested achieved the designed bearing pressure of 2000 psf.

Test locations and elevations are based on information provided by others.

Should the areas represented by passing tests this date be subject to rain, freezing, or other adverse conditions, prior to paving, concreting, placing additional lifts of fill, etc., NOVA recommends re-evaluation.

NOVA representative also observed concrete placement on the above noted date. The contractor placed 4 cubic yards of 4000 psi concrete Eastern Ready Mix for the following location(s):

- Column pedestals
- column footing A.1/7.7

One sample of the plastic concrete was/were obtained for field testing. The NOVA representative performed concrete temperature, air temperature, slump, air content and unit weight testing on the plastic concrete in accordance with ACI standards. Additionally, one set of 5 - 4" x 8" concrete test specimens (cylinders) were cast for compressive strength testing in accordance with ASTM C31. Concrete placement observed appeared to be performed in accordance with ACI standards and site specifications.

No observations, tests, inspections or approvals by NOVA shall relieve the Contractor from his obligation to perform the Work in strict conformity with the Contract Documents. NOVA's inspections and/or tests reported herein are in no way a guarantee of deficient-free construction. The information provided herein is intended for the sole and exclusive use of our Client unless other written agreement is entered into by NOVA and other parties. All other recipients are provided this document and any corresponding tests and/or inspection results for information purposes only, and any use of said information shall be at their sole risk.

Raleigh
5504 Commercial Avenue
Suite 102
Raleigh, NC 27612
Phone: 984.242.1950
Fax: 980.321.4099

Client:
RLC Construction Company, Inc.
414 E. Edgerton Street
Dunn, NC 28334

Project:
10727-1026045.000
192 Jarco Drive
192 Jarco Drive
Fuquay-Varina, NC

Picture	Caption
	C 9
	A.1/7.7

Additional Documents


Document(s):

Client:

RLC Construction Company, Inc.
414 E. Edgerton Street
Dunn, NC 28334

Project:

10727-1026045.000
192 Jarco Drive
192 Jarco Drive
Fuquay-Varina, NC

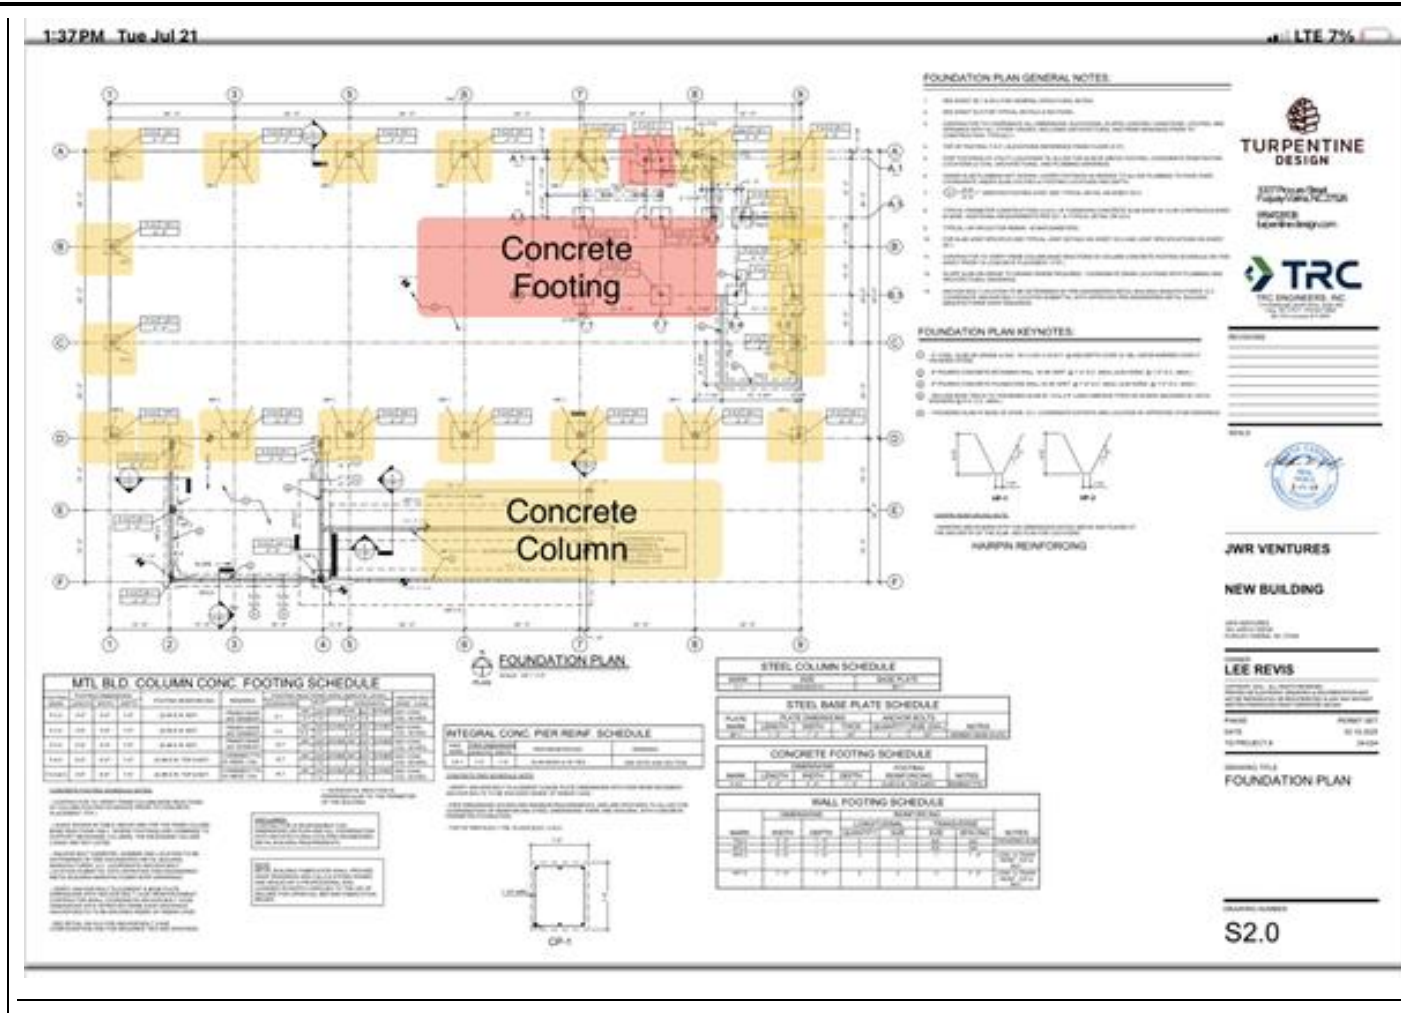

Shastin Jones

Electronically signed and sealed by
Glaston Jones, Business Unit Manager on
Aug 10, 2026 using a Digital Signature.
