

Certificate of Completion

Owner Matthew Burns Address _____
(MUST BE FILLED IN) (MAILING ADDRESS)

Contractor Jerry Pleasant Address _____
(MAILING ADDRESS)

Location of Premises off SR 1440 / Neill's Creek Farms
(SUBDIVISION, STREET OR ROAD NAME OR NUMBER, LOT NO.)
lot # 53

Details of Septic Tank System

Kind of Material for Tank: Concrete Other 1000 gal pump tank


Size of Tank: Capacity 1000 Gallons

Subsurface Drainage Field No. of Ditches 3 Exact Length of each Ditch 100 Ft. Width of Ditches 3 Ft. Depth of Ditches 20-22 18 Inches

Square Feet in Absorption Field _____

Inspected by Charles Wood Jr
(SANITARIAN)

Permit No. 4897 Date 04/02/91

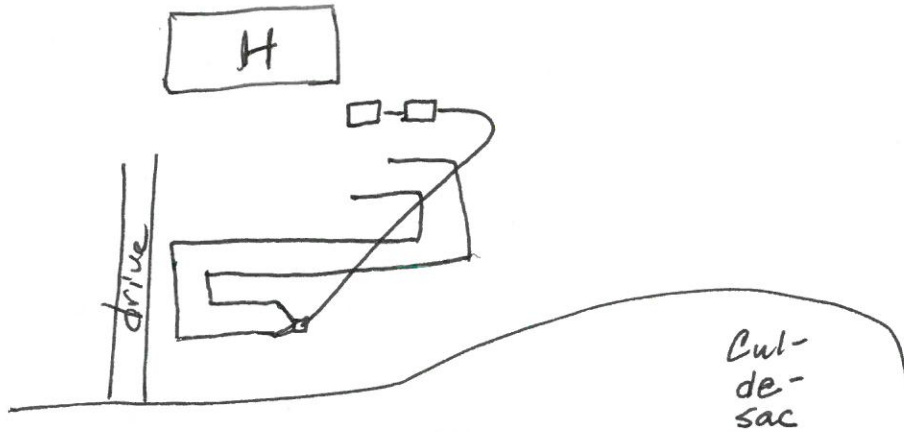

IMPROVEMENT PERMIT

Be it ordained by the Harnett County Board of Health as follows:
Section III, Item B. "No person shall begin construction of any building at which a septic tank system is to be used for disposal of sewage without first obtaining a written permit from the Harnett County Health Department."

Name: (owner) Matthew Burns New Installation Septic Tank
Property Location: Lot 53 Neills Creek Farms SF 1440 Repairs Nitrification Line

Number of Bedrooms Proposed: 3 Dish Washer Garbage Disposal
Lot Size: 2.04 ac Water Supply: Well City Community
Distance From Well?

Above information certified by: Application

Following is the minimum specifications for sewage disposal system on above captioned property. Subject to final approval.

Kind of Material for Tank: Concrete Other 1000 gal pump tank

Size of Tank: Capacity 1000 Gallons

Subsurface Drainage Field Ditches: No. of 3 Exact Length 100 Ft. of each Ditch Width of 3 Ft. Ditches Depth of 18 Ft. Ditches 18 Inches

Any Change in the layout of this system without prior approval of the issuing authority will result in this permit being void.


Date: 12/18/89

Signed: Mike Eake

(SANITARIAN)

Void After 5 Years

The permit is subject to revocation if site plans or the intended use change.

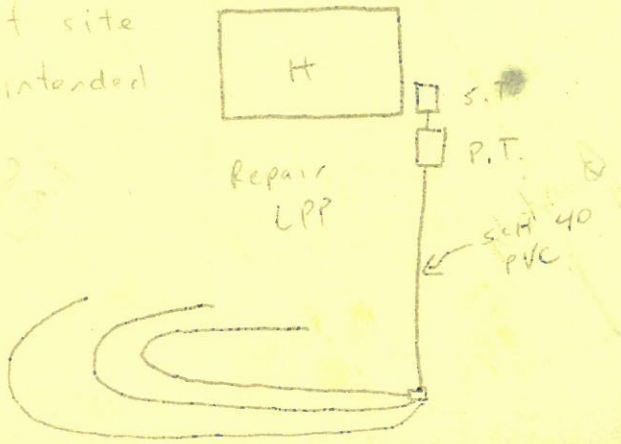

- ① High water alarm must be installed on separate circuit
- ② 18 inch depth must be maintained on ditches
- ③ Maintain 10 ft. off all property lines
