

HARNETT COUNTY HEALTH DEPARTMENT  
ENVIRONMENTAL HEALTH SECTION

N<sup>o</sup>07858

CERTIFICATE OF COMPLETION / OPERATIONAL PERMIT

Name: (owner) Staley Smith  New Installation  Septic Tank  
 Property Location: SR# 1542  Repairs  Nitrification Line  
 Subdivision Sandy Grove Lot # 14  
 TAX ID# \_\_\_\_\_ Quadrant # \_\_\_\_\_  
 Contractor: Gerald Temple Registration # 9  
 Basement with Plumbing:  Garage:   
 Water Supply:  Well  Public  Community  
 Distance From Well: 50+ ft.

Following are the specifications for the sewage disposal system on above captioned property.


Type of system:  Conventional  Other \_\_\_\_\_  
 Size of tank: Septic Tank: 1000 gallons Pump Tank: \_\_\_\_\_ gallons  
 Subsurface Drainage Field: No. of ditches 2 exact length of each ditch 100 ft. width of ditches 3 ft. depth of ditches 18-24 in.  
 French Drain: \_\_\_\_\_ Linear feet

PERMIT NO. 09408

Date: 9-21-94

Inspected by: James E. Manly

Environmental Health Specialist

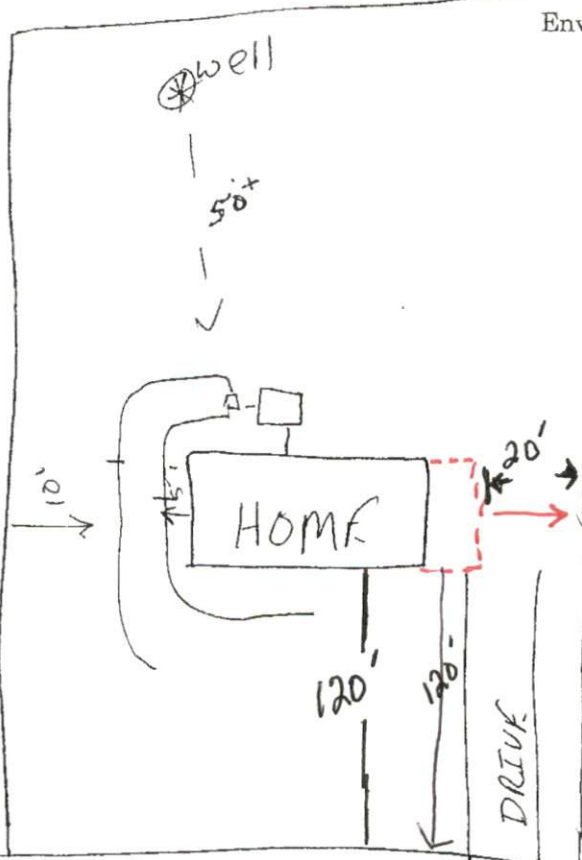

SMITH DRIVE
