

PREPARED 1/22/15, 14:23:19
Harnett County

INSPECTION TICKET
INSPECTOR: IVR

PAGE 1
DATE 1/23/15

ADDRESS : PEARIDG RD SUBDIV:
CONTRACTOR : L M LANGDON AND ASSOCIATES INC PHONE : (919) 422-6946
OWNER : DUPREE ROGER H & JANE A PHONE : (919) 639-2009
PARCEL : 04-0684- - -0050- - -
APPL NUMBER: 08-50021282 CP ADD & ALTER RESIDENTIAL

DIRECTIONS : 210 TOWARD ANGIER GO THUR ANGIER TURN
LEFT ON PEARIDGE RD JOB IS 1ST HOUSE ON
RIGHT 1/4 MILE FROM 210 ADDRESS IS 1307
JB

STRUCTURE: 000 000 36X40 SUNROOM / BDR / BATH

FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 4.00 SEPTIC - EXISTING? : EXS
WATER SUPPLY : EXS WELL

PERMIT: CPBP 00 CP BUILDING PERMIT

	REQUESTED	INSP	DESCRIPTION		
TYP/SQ	COMPLETED	RESULT	RESULTS/COMMENTS		
B101 01	1/22/15	TI	R*BLDG FOOTING / TEMP SVC POLE	TIME: 17:00	VRU #: 002619757
B101 02	1/23/15 <u>1/23/15</u>	TI <u>APD</u>	R*BLDG FOOTING / TEMP SVC POLE	TIME: 17:00	VRU #: 002620318

----- COMMENTS AND NOTES -----

Enoch Engineers, P.A.

Materials & Tests Division

1403 NC Highway 50 South

Benson, NC 27504

919-894-7765

Daily Report


Client: DUPREE FARMS Technician: BH
Project: ROGER DUPREE RESIDENCE Date: 1.22.15
Location: 1307 PEARIDGE RD ANGIER, NC Contractor: GO ROGER DUPREE

Services Performed:

- ☐ Soil Tests
- ☐ Concrete Tests
- ☐ Asphalt Tests
- ☐ Site Inspection
- ☒ Foundation Inspection
- ☐ Structural Inspection
- ☐ Proof-roll

- ☐ Steel Inspection
- ☐ Meeting
- ☐ Other

Remarks: PERFORMED FOOTING INSPECTION AT SITE REFERENCED ABOVE.
SOILS CONFIRMED A MINIMUM ALLOWABLE BEARING CAPACITY OF
2000 LB/FT². WE RECOMMEND BACKFILLING UNDERCUT AREA AT
STANDING WATER WITH #57 STONE TO DESIRED HEIGHT.

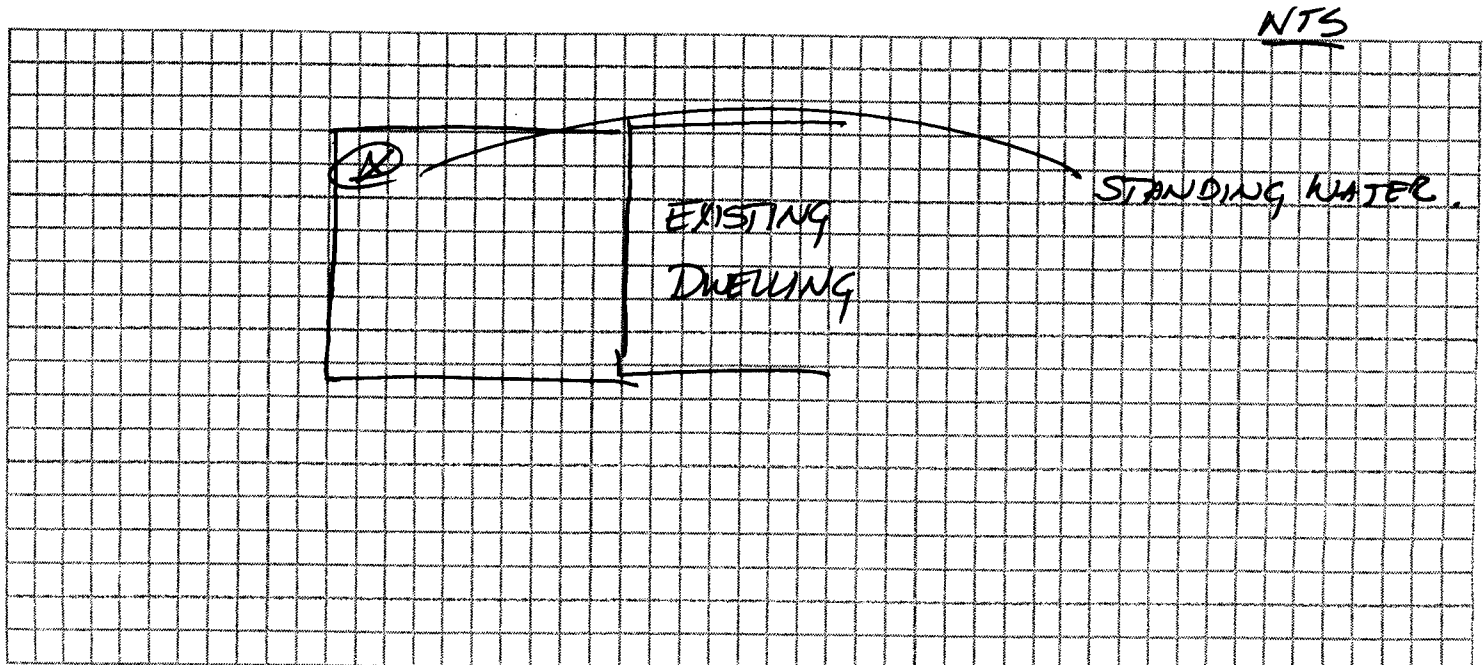

Technician: BH
