

PREPARED 3/24/15, 14:42:02
Harnett County

INSPECTION TICKET
INSPECTOR: IVR

PAGE 19
DATE 3/25/15

ADDRESS : 112 NEWBURY DR
CONTRACTOR : WELLONS ROBERT PAUL (REALTY)
OWNER : FOUR W'S INC
PARCEL : 04-0662- - -0002- -40-
APPL NUMBER: 15-50035326 CP NEW RESIDENTIAL (SFD)
DIRECTIONS : T/S: 01/14/2015 04:18 PM JBROCK ----
WATERFORD LOT 19

SUBDIV: WATERFORD
PHONE : (910) 892-3123
PHONE :

STRUCTURE: 000 000 41X50 3BDR CRAWL W/ GARAGE

FLOOD ZONE : FLOOD ZONE X
BEDROOMS : 3000000.00
SEPTIC - EXISTING? : SEWER

PROPOSED USE : SFD
WATER SUPPLY : COUNTY

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	1/30/15	MR	R*BLDG FOOTING / TEMP SVC POLE VRU #: 002622950 T/S: 01/30/2015 01:53 PM MREARIC
B101 02	1/30/15	CA	
B101 02	3/25/15	TI	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 002638138 premise # 06371242 T/S: 03/24/2015 01:36 PM LBENNETT

AP

----- COMMENTS AND NOTES -----

Enoch Engineers, P.A.

Materials & Tests Division

1403 NC Highway 50 South

Benson, NC 27504

919-894-7765

Daily Report

Client: WELLONS REALTY
Project: WATERFORD S/D
Location: 112 NEWBURY DR.
LOT 19

Technician: 13A
Date: 3.24.2015
Contractor: C/O BLAKE DENNING


Services Performed:

- Soil Tests
- Concrete Tests
- Asphalt Tests
- Site Inspection
- Foundation Inspection
- Structural Inspection
- Proof-roll

- Steel Inspection
- Meeting
- Other

Remarks: PERFORMED FOOTING INSPECTION FOR LOT NOTED ABOVE.
SOILS CONFIRMED A MINIMUM ALLOWABLE BEARING CAPACITY OF
2000 LBS PSF AT ALL LOCATIONS EXCEPT 8 PIER HOLES NOTED
BELOW. RECOMMEND UNDERCUTTING 8" OF EACH PIER HOLE AND
BACKFILL WITH WASHED # 57 STONE OR ADDITIONAL CONCRETE.

NTS

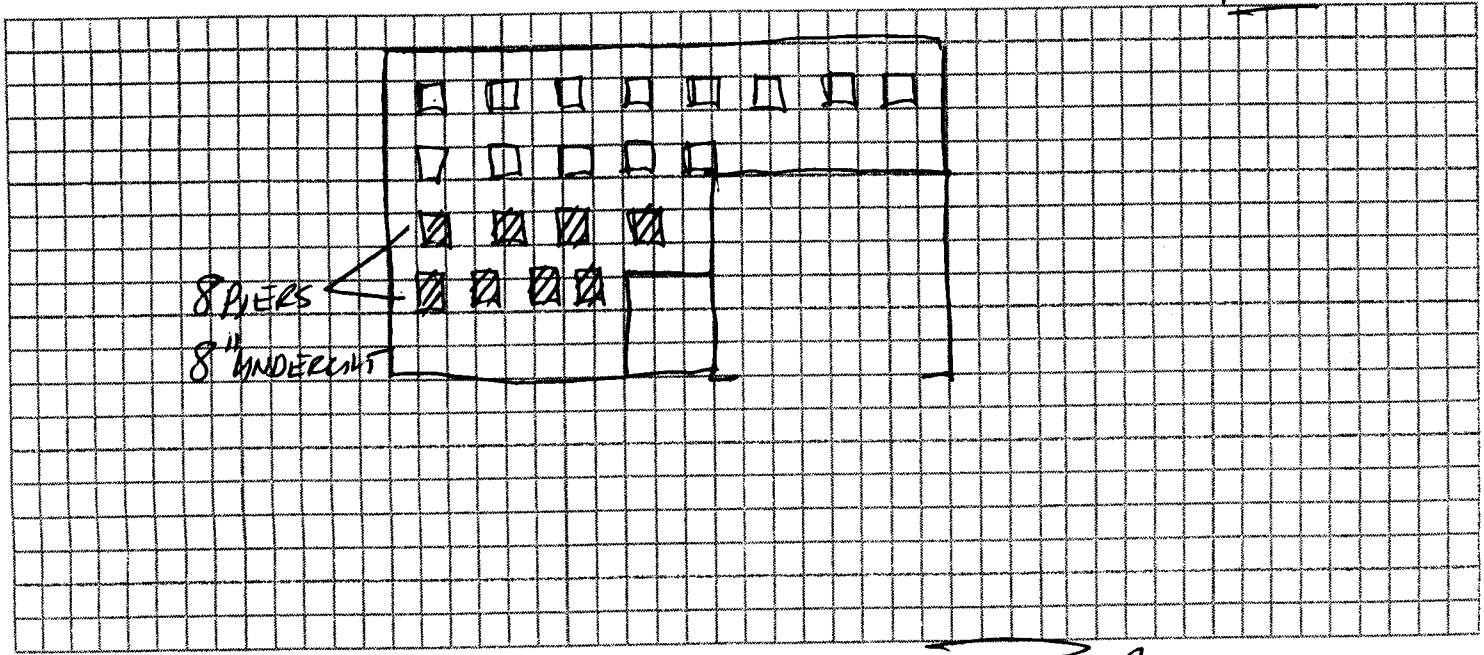

Technician: [Signature]
