

Certificate of Completion

No 4890

Owner 3rd Doppel Mission Address S.R. 2014
(MUST BE FILLED IN) (MAILING ADDRESS)
Contractor D. Temple Address Bunker
(MAILING ADDRESS)
Location of Premises Passiter Sub Post 4
(SUBDIVISION, STREET OR ROAD NAME OR NUMBER, LOT NO.)

Details of Septic Tank System

Kind of Material
for Tank:☒ Concrete☐ Other _____Size of
Tank:Capacity 1200 GallonsSubsurface
Drainage FieldNo. of
Ditches4 Exact Length
of each Ditch100Width of
Ft. Ditches3Depth of
Ft. Ditches22

Inches

Square Feet in Absorption Field

1200Surface Drainage
RequiredLinear
Ft.

Inspected by

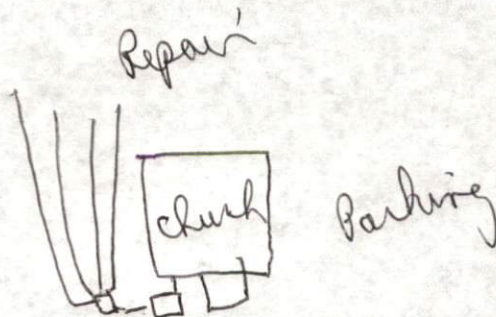
D. Temple

(SANITARIAN)

Permit No.

4569 # 7.000

Date

10.28.86

2014

IMPROVEMENT PERMIT

No 4596

Be it ordained by the Harnett County Board of Health as follows:
 Section III, Item B. "No person shall begin construction of any building at which a septic tank system is to be used for disposal of sewage without first obtaining a written permit from the Harnett County Health Department."

Name: (owner) Full Gospel Mission ☒ New Installation ☐ Septic Tank
 Property Location: SR 2014 ☐ Repairs ☒ Nitrification Line
Lawster Sub. lot 4
 Number of Bedrooms Proposed: 100 ☐ Dish Washer ☐ Garbage Disposal
 Lot Size: 2 acres Water Supply: ☒ Well ☐ City ☒ Community
 Distance From Well? ☐ At least 50'

Above information certified by: App.

Following is the minimum specifications for sewage disposal system on above captioned property. Subject to final approval.

Kind of Material for Tank: ☒ Concrete ☐ Other _____

Size of Tank: Capacity 1200 Gallons
 Subsurface No. of 4 Exact Length 100 Width of 3 Depth of 22
 Drainage Field Ditches of each Ditch Ft. Ditches Ft. Ditches Inches

Any Change in the layout of this system without prior approval of the issuing authority will result in this permit being void.

Date: 08/25/88

Signed: John Byrd
 (SANITARIAN)

Void After 3 Years



Parkies

- Keep line 10' from all property line
- Keep line 5' min. from Building
- Keep line 10' from all water lines
- Keep line 50' from all wells at least.
- Repair area in Rear of Church is at no time to be covered by any type of paving or concrete

Parkies

SR 2014

HARNETT COUNTY HEALTH DEPARTMENT

IMPROVEMENT PERMIT

No 4565

Be it ordained by the Harnett County Board of Health as follows:
on III, Item B. "No person shall begin construction of any building at which a septic tank system is to be used for disposal of sewage without first obtaining a written permit from the Harnett County Health Department."

Name: (owner) Full Gospel Mission ☒ New Installation ☐ Septic Tank
Property Location: SR 2014 Lassater Sub. lot 4 ☐ Repairs ☐ Nitrification Line

Number of Bedrooms Proposed: 150 members ☐ Dish Washer ☐ Garbage Disposal
Lot Size: 2 acres Water Supply: ☒ Well ☐ City ☐ Community
Distance From Well? ☐ 50' minimum

Above information certified by: APP.

Following is the minimum specifications for sewage disposal system on above captioned property. Subject to final approval.

Kind of Material for Tank: ☒ Concrete ☐ Other 2 A Boxes 1 Flow divider (V.C.)

Size of Tank: Capacity 1850 Gallons
Subsurface No. of 6 Exact Length 100 Width of 3 Depth of 22 Inches
Drainage Field Ditches of each Ditch Ft. Ditches

Any Change in the layout of this system without prior approval of the issuing authority will result in this permit being void.

Date: 07/28/88

Signed: [Signature] (SANITARIAN)

Void After 3 Years

07/28/88
- set Flow divider between Tank and A Boxes.
- Keep Line 10' off Property lines #215
- Keep Line at least 50' from all wells.

System Altered due to change in membership.
New Permit # 4596
08/25/88

