

HTE # 04-5-8802R

OPERATIONS PERMIT

Name: (owner) R.L Properties New Installation Septic Tank Repair

Property Location: SR# 1415 Bawls Church Rd Nitrification Line Expansion

Subdivision Wyndham Place Lot # 15 Tax ID # _____ Quadrant # _____

Contractor: Ricky Holland Registration # _____

Basement with Plumbing: Garage:

Water Supply: Well Public Community

Distance From Well: 100 ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system: Conventional Other 25% Reduction System Easyflow

Size of tank: Septic Tank: 1000 gallons Pump Tank: _____ gallons


Subsurface Drainage Field No. of ditches 2 exact length of each ditch 150 ft. width of ditches 3 ft. depth of ditches 20 in.

French Drain Required: _____ Linear feet

Date: 6-1-06

PERMIT NO. 20817

Inspected by: Jamie Tulington 

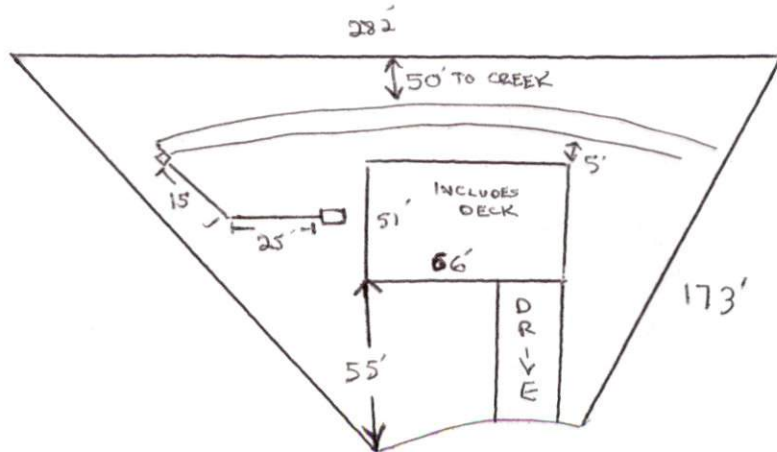

* HOUSE ON 1P 30' x 50'. ACTUAL HOUSE SIZE 51' x 66'

* FRONT SETBACK ON 1P 40'. ACTUAL SETBACK 55'

* REPAIR CHANGED TO PRETREATMENT LPP TO USE AREA BETWEEN SYSTEM & CREEK
