

HTE# 07-500-18810

# Harnett County Department of Public Health 23569

## Improvement Permit

A building permit cannot be issued with only an Improvement Permit

ISSUED TO: CAVINESS Land Dev. PROPERTY LOCATION: 1125  
NEW  REPAIR  EXPANSION  SUBDIVISION: FOREST OAKS LOT # 161

Type of Structure: SFD- 45x60 3BR  
Proposed Wastewater System Type: Pump to 25% Reduction System  
Projected Daily Flow: 360 GPD  
Number of bedrooms: 3 Number of Occupants: 6 max  
Basement  Yes  No

Pump Required:  Yes  No  May be required based on final location and elevations of facilities  
Type of Water Supply:  Community  Public  Well Distance from well 0 feet Permit valid for:  Five years  
Permit conditions: Meet on site maintain all set BACK  No expiration  
STUB OUT PLUMBING SHALLOW AT GROUND LEVEL OR HIGHER WHERE SHOWN  
AND PUMP MAY NOT BE REQUIRED

Authorized State Agent: Joe L. LAR Date: 11-30-07 SEE ATTACHED SITE SKETCH  
The issuance of this permit by the Health Department in no way guarantees the issuance of other permits. The permit holder is responsible for checking with appropriate governing bodies in meeting their requirements. This site is subject to revocation if the site plan, plat, or the intended use changes. The Improvement Permit shall not be affected by a change in ownership of the site. This permit is subject to compliance with the provisions of the Laws and Rules for Sewage Treatment and Disposal and to conditions of this permit.

## Construction Authorization

(Required for Building Permit)

The construction and installation requirements of Rules .1950, .1952, .1954, .1955, .1956, .1957, .1958, and .1959 are incorporated by references into this permit and shall be met. Systems shall be installed in accordance with the attached system layout.

ISSUED TO: CAVINESS Land Dev. PROPERTY LOCATION: 1125  
SUBDIVISION: FOREST OAKS LOT # 161

Facility Type: SFD- 45x60-3BR  New  Expansion  Repair  
Basement?  Yes  No Basement Fixtures?  Yes  No  
Type of Wastewater System\*\* Pump to 25% Red. System (Initial) Wastewater Flow: 360 GPD  
(See note below, if applicable)   
25% Reduction system (Repair)

### Installation Requirements/Conditions

Septic Tank Size 1000 gallons Exact length of each trench 1x150 feet Trench Spacing: 9 Feet on Center  
Pump Tank Size 1000 gallons Trenches shall be installed on contour at a Soil Cover: 6 inches  
Maximum Trench Depth of: 18.24 inches (Maximum soil cover shall not exceed 36" above the trench bottom)  
(Trench bottoms shall be level to +/-1/4" in all directions)  
Pump Requirements: \_\_\_\_\_ ft. TDH vs. \_\_\_\_\_ GPM \_\_\_\_\_ inches below pipe  
Aggregate Depth: \_\_\_\_\_ inches above pipe  
Conditions: \_\_\_\_\_ inches total

\*\*If applicable: *I understand the system type specified is different from the type specified on the application. I accept the specifications of this permit.*

Owner/Legal Representative Signature: \_\_\_\_\_ Date: \_\_\_\_\_

This Construction Authorization is subject to revocation if the site plan, plat, or the intended use changes. The Construction Authorization shall not be transferred when there is a change in ownership of the site. This Construction Authorization is subject to compliance with the provisions of the Laws and Rules for Sewage Treatment and Disposal and to the conditions of this permit.

Authorized State Agent: Joe L. LAR Date: 11-29-07 SEE ATTACHED SITE SKETCH  
Construction Authorization Expiration Date: 11-29-2012


HTE# 07-500 18880

Permit # 23569

# Harnett County Department of Public Health Site Sketch

ISSUED TO: Carroll Land Dev. PROPERTY LOCATOR: 1125  
SUBDIVISION: FOREST OAKS LOT # 161

Authorized State Agent: J. Williams Date: 11-28-07

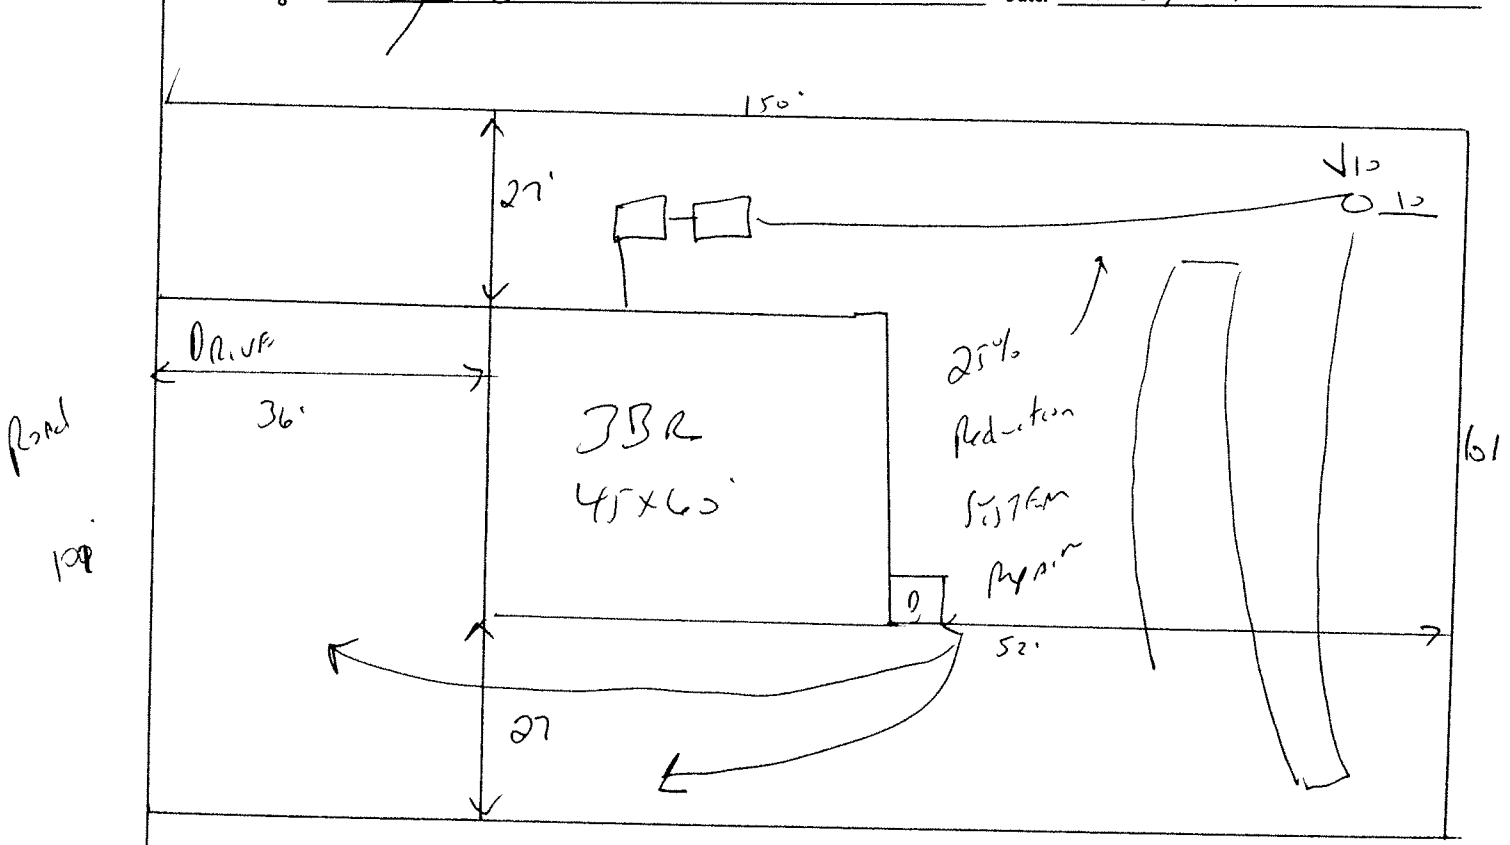

Meet onsite, maintain all set backs  
STUB out Plumbing shallow, at Ground level or higher  
where shown & pump may not be required  
 Install 1x150 of 25% Reduction system at 18"-24" Deep.
