

HTE# 10-5-25609R

Harnett County Department of Public Health

26318

Improvement Permit

A building permit cannot be issued with only an Improvement Permit

ISSUED TO: Stencil Builders PROPERTY LOCATION: Tingen Rd.
 SUBDIVISION: Patterson Point LOT # 173
 NEW REPAIR EXPANSION
 Type of Structure: 25% Red SFD 50x50'
 Proposed Wastewater System Type: 25% Reduction System
 Projected Daily Flow: 360 GPD
 Number of bedrooms: 3 Number of Occupants: 6 max
 Basement Yes No
 Pump Required: Yes No May be required based on final location and elevations of facilities
 Type of Water Supply: Community Public Well Distance from well _____ feet
 Permit conditions: _____ Permit valid for: Five years
 No expiration

Authorized State Agent: Bryan McLean, REHS Date: 1/31/2011 SEE ATTACHED SITE SKETCH

The issuance of this permit by the Health Department in no way guarantees the issuance of other permits. The permit holder is responsible for checking with appropriate governing bodies in meeting their requirements. This site is subject to revocation if the site plan, plat, or the intended use changes. The Improvement Permit shall not be affected by a change in ownership of the site. This permit is subject to compliance with the provisions of the Laws and Rules for Sewage Treatment and Disposal and to conditions of this permit.

Construction Authorization

(Required for Building Permit)

The construction and installation requirements of Rules .1950, .1952, .1954, .1955, .1956, .1957, .1958, and .1959 are incorporated by references into this permit and shall be met. Systems shall be installed in accordance with the attached system layout.

ISSUED TO: Stencil Builders PROPERTY LOCATION: Tingen Rd.
 SUBDIVISION: Patterson Point LOT # 173
 Facility Type: SFD New Expansion Repair
 Basement? Yes No Basement Fixtures? Yes No
 Type of Wastewater System** 25% Reduction System (Initial) Wastewater Flow: 360 GPD
 (See note below, if applicable)
25% Reduction System (Repair)

Installation Requirements/Conditions
 Septic Tank Size 1000 gallons
 Pump Tank Size _____ gallons
 Number of trenches 2
 Exact length of each trench 75 feet
 Trenches shall be installed on contour at a Maximum Trench Depth of: 36-18 inches
 (Trench bottoms shall be level to +/-1/4" in all directions)
 Trench Spacing: 9 Feet on Center
 Soil Cover: 18 inches
 (Maximum soil cover shall not exceed 36" above the trench bottom)
 Pump Requirements: _____ ft. TDH vs. _____ GPM
 Aggregate Depth: _____ inches below pipe
 _____ inches above pipe
 _____ inches total
 Conditions: Stepdowns will be needed

**WATER LINES (INCLUDING IRRIGATION) MUST BE 10FT. FROM ANY PART OF SEPTIC SYSTEM OR REPAIR AREA.
 NO UTILITIES ALLOWED IN INITIAL OR REPAIR DRAIN FIELD AREA.**

**If applicable: I understand the system type specified is different from the type specified on the application. I accept the specifications of this permit.
 Owner/Legal Representative Signature: _____ Date: _____

This Construction Authorization is subject to revocation if the site plan, plat, or the intended use changes. The Construction Authorization shall not be transferred when there is a change in ownership of the site. This Construction Authorization is subject to compliance with the provisions of the Laws and Rules for Sewage Treatment and Disposal and to the conditions of this permit. SEE ATTACHED SITE SKETCH


Authorized State Agent: Bryan McLean, REHS Date: 1/31/2011
 Construction Authorization Expiration Date: 1/31/2016

HTE# 10-5-25609R

Permit # 26318

Harnett County Department of Public Health Site Sketch

ISSUED TO: Stancil Builders PROPERTY LOCATOR: Tingencld.
SUBDIVISION: Pattur Point LOT # 173
Authorized State Agent: Bryan McJinn RTHS Date: 1/31/2011

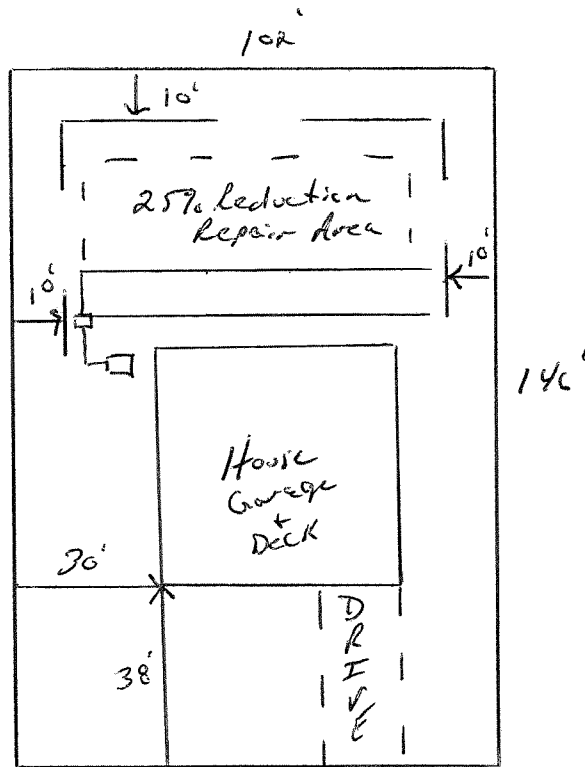

Abram Ct.
