

ADDRESS . . : 66 HARVEST CT SUBDIV: SWEETWATER 71LOTS
 CONTRACTOR : ATLANTIC CONSTRUCTION PHONE : (910) 938-9053
 OWNER . . : DIVERSIFIELD INVESTORS INC PHONE :
 PARCEL . . : 01-0544- - -0004- -51-
 APPL NUMBER: 15-50035902 CP NEW RESIDENTIAL (SFD)
 DIRECTIONS : T/S: 04/15/2015 08:42 AM JBROCK ----
 SWEETWATER #43

STRUCTURE: 000 000 45X42.6 3BDR SLAB W/ GARAGE

FLOOD ZONE : FLOOD ZONE X
 # BEDROOMS : 3000000.00 PROPOSED USE : SFD
 SEPTIC - EXISTING? : NEW TANK WATER SUPPLY : COUNTY

PERMIT: CPSF 00 CP * SFD

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
B101 01	5/04/15 5/04/15	JH AP	R*BLDG FOOTING / TEMP SVC POLE TIME: 17:00 VRU #: 002654374 T/S: 05/01/2015 02:20 PM LBENNETT -----
A814 01	5/07/15 5/08/15	TW AP	ADDRESS CONFIRMATION TIME: 17:00 VRU #: 002656874 66 Harvest Ct Linden 28356 # To be posted on home T/S: 05/08/2015 08:37 AM TWARD -----
B103 01	5/08/15 5/08/15	JH AP	R*BLDG FOUND & TEMP SVC POLE TIME: 17:00 VRU #: 002656858 T-POLE PASSED -----
P309 01	5/13/15 5/13/15	JH AP	R*PLUMB UNDER SLAB TIME: 17:00 VRU #: 002658201 T/S: 05/12/2015 11:20 AM DJOHNSON -----
B111 01	5/15/15 5/15/15	JH AP	R*BLDG SLAB INSP/TEMP SVC POLE TIME: 17:00 VRU #: 002659654 -----
B104 01	6/08/15 6/08/15	JB AP	R*FOUND & SETBACK VERIF SURVEY TIME: 17:00 VRU #: 002669786 T/S: 06/08/2015 09:14 AM JBROCK -----
R425 01	6/09/15 6/09/15	JH DP	FOUR TRADE ROUGH IN TIME: 17:00 VRU #: 002669794 1)Strap each side of garage door header from top plate to 1' below header.2)Need stud @ joint in osb over garage door.3)Missing structural nail guard over electrical panel in garage.4)Need more bracing under front porch.5)MISSING nails in floor truss hangers @ stairs.6)MISSING anchor bolt to left of back door7)Missing baffels in kitchen & upstairs in stairway, also HOW ARE YOU GOING TO INSTALL R38 IN KITCHEN AT BACK WALL WITH 6"?8)Fasten all interior load bearing walls with min fire powder fasteners.9)MISSING nails under stairs on garage wall.10)Nail osb to right of window in rec room & to right of window in back right bedroom.11)Frame chase & air barrier in right back bedroom closet.12)Strap trunk line upstairs every 64".13)Missing bra bracing on A2A trusses.14)Need truss papers for RFG1 2ply truss in kitchen.15)Missing flashing on all windows on top & bottom. DO NOT SIDE OR INSULATE
R425 02	6/11/15 6/11/15	KS AP	FOUR TRADE ROUGH IN TIME: 17:00 VRU #: 002671907 T/S: 06/11/2015 03:35 PM KSLATTUM -----
I129 01	6/15/15 6/15/15	JH AP	R*INSULATION INSPECTION TIME: 17:00 VRU #: 002673754 -----
H824 01	6/26/15	OT	ENVIR. OPERATIONS PERMIT TIME: 17:00 VRU #: 002680767


ADDRESS : 66 HARVEST CT
CONTRACTOR : ATLANTIC CONSTRUCTION
OWNER : DIVERSIFIELD INVESTORS INC
PARCEL : 01-0544- - -0004- -51-
APPL NUMBER: 15-50035902 CP NEW RESIDENTIAL (SFD)

SUBDIV: SWEETWATER 71LOTS
PHONE : (910) 938-9053
PHONE :

TYP/SQ	REQUESTED COMPLETED	INSP RESULT	DESCRIPTION RESULTS/COMMENTS
	6/26/15	AP	T/S: 06/29/2015 09:48 AM SSTEWARD ----- T/S: 06/29/2015 09:48 AM SSTEWARD -----
M305 01	7/09/15	MR	R*PLUMB SEWER CONNECTION TIME: 17:00 VRU #: 002685170
	7/09/15	CA	T/S: 07/09/2015 02:43 PM MREARIC -----
P307 01	7/09/15	MR	R*PLUMB WATER CONNECTION TIME: 17:00 VRU #: 002685188
	7/09/15	CA	T/S: 07/09/2015 02:43 PM MREARIC -----
M305 02	7/15/15	TI	R*PLUMB SEWER CONNECTION TIME: 17:00 VRU #: 002687887
	7-15-15	AP JH	
P307 02	7/15/15	TI	R*PLUMB WATER CONNECTION TIME: 17:00 VRU #: 002687903
	7-15-15	AP JH	
R125 01	7/15/15	TI	ONE TRADE ROUGH IN TIME: 17:00 VRU #: 002687911
	7-15-15	AP JH	track for the back screen porch - customer paid

----- COMMENTS AND NOTES -----

Rear Wall of House

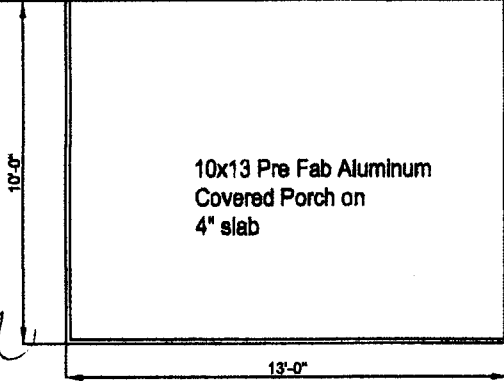

Bottom receiving track
fasten with 1/4x2 3/4 tapcons @ 24"

10x13 Pre Fab Aluminum
Covered Porch on
4" slab

13'-0"

*Screened porch
JUL*

PLAN VIEW

HARNETT COUNTY CENTRAL PERMITTING

APPLICATION # 1550035902.R


JOB NAME Atlantic Const.

DATE PLANS RECEIVED 7.9.15

SITE PLANS APPROVED 7.9.15

APPROVED BY Approved

per K.W.

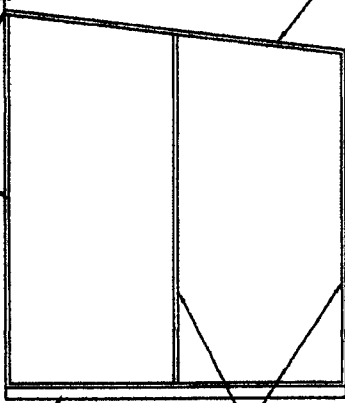

Fasten roof panels to top track
with 1/4x1 self tap screws @ 18"

Fasten well and roof track
to blocking on house with
1/4x3 lag screws @ 16"

*13x10
Screened
porch*

4" Concrete slab on grade
#3000 Concrete

Fasten screen frame
to bottom and top receiving track
with (2) 1/4x1 self tap screws (each location)
Frame spacing per manufacturer based on screen widths

SIDE VIEW



DESIGN MEETS 100 MPH WIND ZONE

DATE: 7/8/15	PROJECT NAME:	Eastern Engineering, P.C. 111 St. Charles Lane Jacksonville, NC 28546 (910) 934-3975 michael.elks@yahoo.com
SCALE:	Lot #43 Sweetwater Screened Porch	
DRAWN: MSE	PREPARED FOR:	Atlantic Construction, Inc Jacksonville, NC
FILE:		
Sign		
