

CERTIFICATE OF COMPLETION / OPERATIONAL PERMIT


Name: (owner) Rosa McLean New Installation Septic Tank
Property Location: SR# 2035 Repairs Nitrification Line
Subdivision _____ Lot # _____
TAX ID# _____ Quadrant # _____
Contractor: DC Carter Registration # _____
Basement with Plumbing: Garage:
Water Supply: Well Public Community
Distance From Well: 100 min ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system: Conventional Other _____
Size of tank: Septic Tank: 1000 gallons Pump Tank: _____ gallons
Subsurface No. of 3 exact length width of depth of
Drainage Field ditches of each ditch 155 ft. ditches 3 ft. ditches 18-24 in.
French Drain: _____ Linear feet

PERMIT NO. 09487

Date: 5/23/96
Inspected by: John A. Bube
Environmental Health Specialist

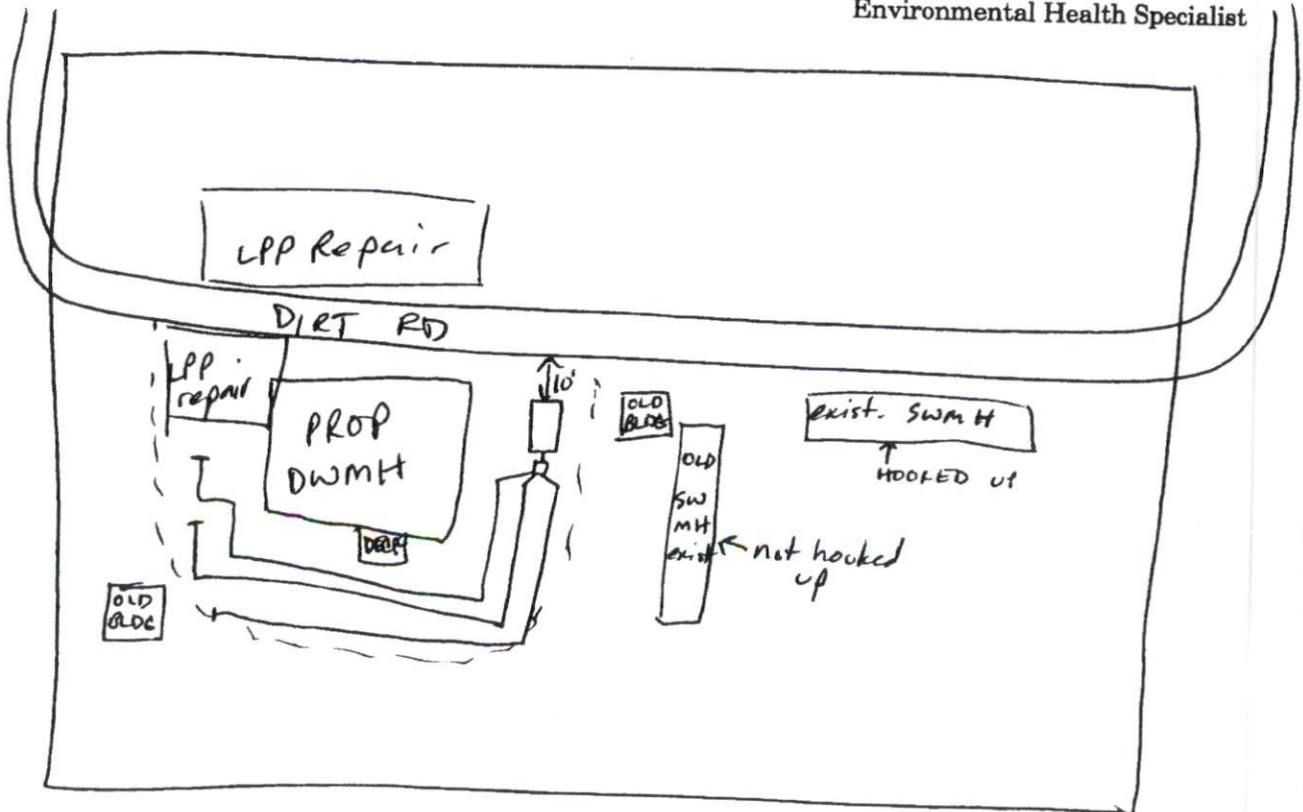

IMPROVEMENT PERMIT

Be it ordained by the Harnett County Board of Health as follows: Section III, Item B. "No person shall begin construction of any building at which a septic tank system is to be used for disposal of sewage without first obtaining a written permit from the Harnett County Health Department".

Name: (owner) Rosa McLean New Installation Septic Tank
 Property Location: SR# 2035 Repairs Nitrification Line

Subdivision _____ Lot # _____

Tax ID# _____ Quadrant # _____

Number of Bedrooms Proposed: 3 Lot Size: 4.01 ac.

Basement with Plumbing: Garage:

Water Supply: Well Public Community

Distance From Well: 100 min ft.

Following is the minimum specifications for sewage disposal system on above captioned property. Subject to final approval.

Type of system: Conventional Other _____

Size of tank: Septic Tank: 1000 gallons Pump Tank: _____ gallons

Subsurface Drainage Field No. of ditches 3 exact length of each ditch 155' width of ditches 3 ft. depth of ditches 18-30 in.

French Drain required: _____ Linear feet

This permit is subject to revocation if site plans or intended use change.


Date: 5/16/96

Signed: Pete A. Bube

NOT TO SCALE

Environmental Health Specialist

VOID AFTER 5 YEARS

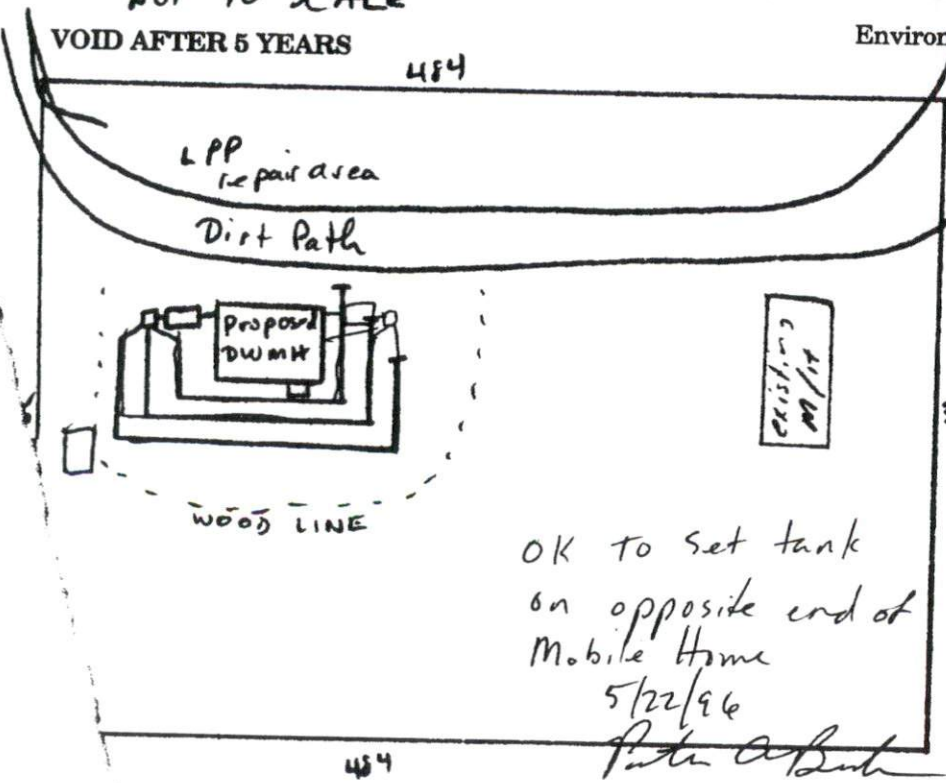

- 1) Maintain all required setbacks
- 2) Keep ditch bottoms level
- 3) Keep lines 5' min off deck location.
- 4) Application stubs 7 occupants. System designed for 420 gallon per day flow.

OK to set tank on opposite end of Mobile Home
 5/22/96
 Pete A. Bube
