

00-5-0688

No 13878

# OPERATIONS PERMIT

Name: (owner) HOLLOWAY CONSTRUCTION  New Installation  Septic Tank  
 Property Location: SR# 1120  Repairs  Nitrification Line  
 Subdivision STONE CROSS Lot # 65  
 TAX ID# \_\_\_\_\_ Quadrant # \_\_\_\_\_  
 Contractor: DC. CARTER Registration # \_\_\_\_\_

Basement with Plumbing:  Garage:   
 Water Supply:  Well  Public  Community  
 Distance From Well: 50 ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system:  Conventional  Other PUMP TO CONVENTIONAL

Size of tank: Septic Tank: 1000 gallons Pump Tank: 1000 gallons


Subsurface Drainage Field No. of ditches 2 exact length of each ditch 75 ft. width of ditches 3 ft. depth of ditches 24-30 in.

French Drain: \_\_\_\_\_ Linear feet

Date: 12-10-01

PERMIT NO. 16818

Inspected by: [Signature]  
Environmental Health Specialist

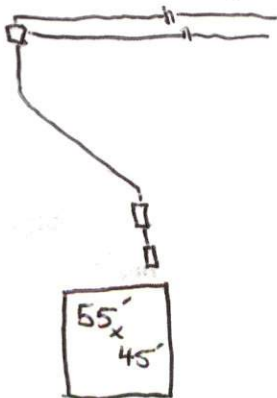

- SYSTEM CHECKED ON 9/11/01
- PUMPS + ALARMS NEED TO BE CHECKED
- CHECKED ON 11/30/01
- ADDITIONAL RISER TO BE PLACED ON TOP OF PUMP TANK DUE TO LANDSCAPING NEEDS TO BE CHECKED

Riser ok by JOE WEST  
on 12-10-01
