

HTE 03-5-7455

OPERATIONS PERMIT

Name: (owner) JN WESCO, INC New Installation Septic Tank
 Property Location: SR# 1125 LEMUEL BLACK RD Repairs Nitrification Line
 Subdivision CARLIE HILLS Lot # 20
 Tax ID # _____ Quadrant # _____
 Contractor: OTIS STRICKLAND Registration # _____

Basement with Plumbing: Garage:

Water Supply: Well Public Community

Distance From Well: 100 ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system: Conventional Other _____

Size of tank: Septic Tank: 1000 gallons ⁸¹³ Pump Tank: _____ gallons
₅₇₈₋₁₀₉

Subsurface Drainage Field No. of ditches 5 exact length of each ditch 80 ft. width of ditches 3 ft. depth of ditches 18-20 in.


French Drain Required: _____ Linear feet

Date: 12/16/03

Inspected by: [Signature] Environmental Health Specialist

PERMIT NO. 20214

97'

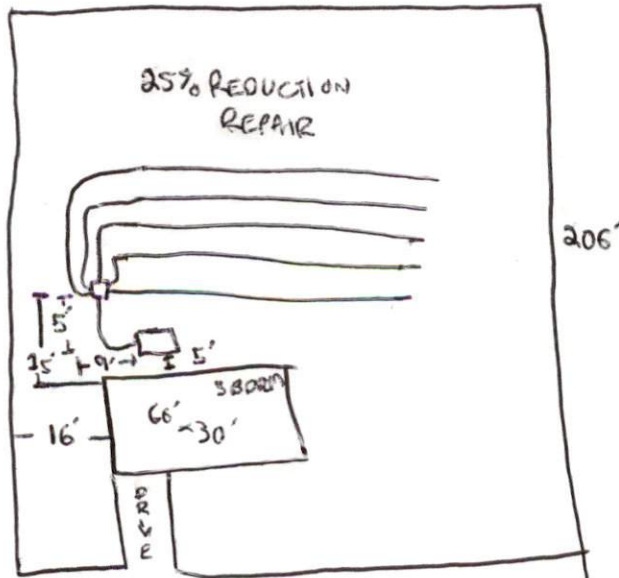

- * DISTRIBUTION BOX IS 15' FROM REAR HOUSE CORNER
- * PLUMBING NEEDS TO BE RAISED TO ACHIEVE FALL INTO TANK. PLUMBING NEEDS TO ENTER TANK AT REQUIRED AREA IN TANK
