## Harnett County Department of Public Health


## Improvement Permit

A building permit cannot be issued with only an Improvement Permit PROPERTY LOCATION: 155 Roping Ln, Cameron (SR1106) ISSUED TO: Celia Arroyo SUBDIVISION Site Improvements required prior to Construction Authorization Issuance: EXPANSION NEW 🗀 REPAIR 🗌 Type of Structure: Proposed Wastewater System Type: Projected Daily Flow: Number of Occupants: \_\_\_\_\_max Number of bedrooms: ☐ No Basement Yes | May be required based on final location and elevations of facilities ☐ No Pump Required: Yes Type of Water Supply: Community Public Well Distance from well \_\_\_\_\_\_feet Permit valid for: Five years No expiration Permit conditions: Pump may be avoided if plumbing can be re-routed so system can meet proper trench depth of 18" - 20" with a new septic tank placement. Date: 01-21-21 The issuance of this permit by the Health Department in no way guarantees the issuance of other permits. The permit holder is responsible for checking with appropriate governing bodies in meeting their requirements. This site is subject to revocation if the site plan, plat, or the intended use changes. The Improvement Permit shall not be affected by a change in ownership of the site. This permit is subject to compliance with the provisions of the Laws and Rules for Sewage Treatment and Disposal and to conditions of this permit. Construction Authorization (Required for Building Permit) The construction and installation requirements of Rules .1950, .1952, .1954, .1955, .1956, .1957, .1958, and .1959 are incorporated by references into this permit and shall be met. Systems shall be installed in accordance with the attached system layout. PROPERTY LOCATION: 155 Roping Ln. Cameron (SR1106) ISSUED TO: Celia Arroyo SUBDIVISION . Expansion Facility Type: DWMH Basement Fixtures? Yes ⊠ No Basement? Yes (Initial) Wastewater Flow: \_\_\_\_\_ Type of Wastewater System\*\* (See note below, if applicable ) 25% reduction Number of trenches 5 Installation Requirements/Conditions Trench Spacing: 9 Feet on Center Exact length of each trench 40 \_gallons Septic Tank Size Trenches shall be installed on contour at a Soil Cover: 6 \_gallons Pump Tank Size \_\_\_\_\_ (Maximum soil cover shall not exceed Maximum Trench Depth of: 18" - 20" inches (Trench bottoms shall be level to +/-1/4" 36" above the trench bottom) in all directions) inches below pipe Pump Requirements: \_\_\_\_\_\_ft. TDH vs. \_ Aggregate Depth: \_\_\_\_\_\_ inches above pipe Conditions: May want to reroute plumbing to front of house to avoid a pump WATER LINES (INCLUDING IRRIGATION) MUST BE 10FT. FROM ANY PART OF SEPTIC SYSTEM OR REPAIR AREA. NO UTILITIES ALLOWED IN INITIAL OR REPAIR DRAIN FIELD AREA. \*\*If applicable: I understand the system type specified is different from the type specified on the application. I accept the specifications of this permit. Owner/Legal Representative Signature: This Construction Authorization is subject to revocation if the site plan, plat, or the intended use changes. The Construction Authorization shall not be transferred when there is a change in ownership of the site. This SEE ATTACHED SITE SKETCH Construction Authorization is subject to compliance with the provisions of the Laws and Rules for Sewage Treatment and Disposal and to the conditions of this permit. Date: 01-21-21 Construction Authorization Expiration Date: 01-21-26

Application # EH210	1-0025
---------------------	--------

## Harnett County Department of Public Health Site Sketch

Property Location: 155	Roping Ln, Cameron (SR1106)	
Issued To: Celia Arroyo		Lot #
Authorized State Agen	hall the	Date: 01-21-21

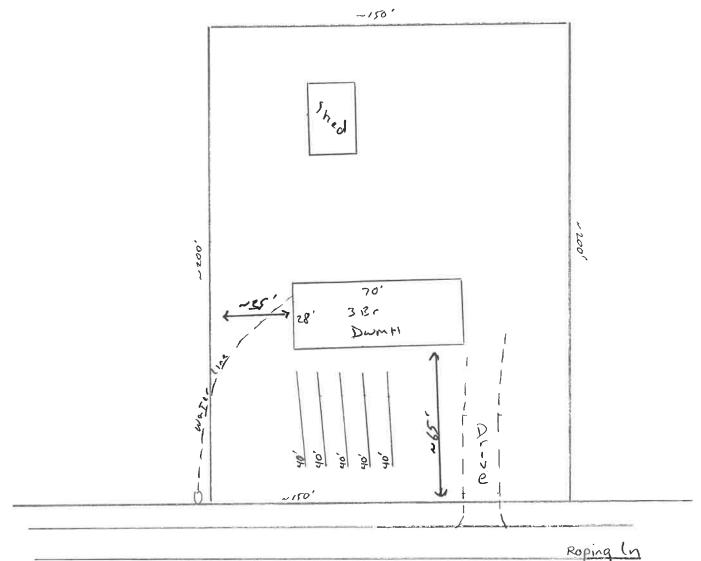

This drawing is for illustrative purposes only. System installation must meet all pertinent laws, rules, and regulations.
