

# OPERATIONS PERMIT

Name: (owner) MAK Dev. Co.  New Installation  Septic Tank  
 Property Location: SR# 27  Repairs  Nitrification Line  
 Subdivision Airbor crest Lot # 33  
 TAX ID# \_\_\_\_\_ Quadrant # \_\_\_\_\_  
 Contractor: Mike Ray Registration # \_\_\_\_\_

Basement with Plumbing:  Garage:

Water Supply:  Well  Public  Community

Distance From Well: 50+ ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system:  Conventional  Other Pump to conv. lines

Size of tank: Septic Tank: 1000 gallons Pump Tank: 1000 gallons


Subsurface Drainage Field No. of ditches 4 exact length of each ditch 75 ft. width of ditches 3 ft. depth of ditches 16 in.

French Drain: \_\_\_\_\_ Linear feet

Date: 11-20-98

PERMIT NO. 15489

Inspected by: Thomas J. Boyce R.S.  
Environmental Health Specialist

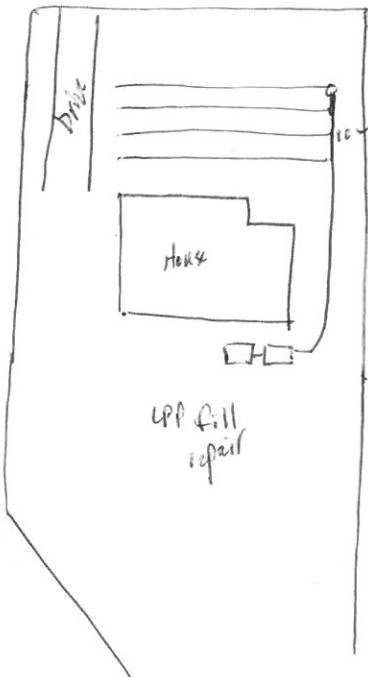

Lines installed  
Tanks installed 11-19-98  
TJB
