

CERTIFICATE OF COMPLETION / OPERATIONAL PERMIT

Name: (owner) DANNY NORRIS New Installation Septic Tank
 Property Location: SR# 27 Repairs Nitrification Line
 Subdivision MIRE BRANCH Lot # 68
 Contractor: Ted Brown Registration # _____
 Basement with Plumbing: Garage:
 Water Supply: Well Public Community
 Distance From Well: _____ ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system: Conventional Other CJ-1000 STB 939
 Size of tank: Septic Tank: 1000 gallons Pump Tank: _____ gallons
 Subsurface Drainage Field: No. of ditches 2 exact length of each ditch 80 ft. width of ditches 3 ft. depth of ditches 20-48 in.
 French Drain: _____ Linear feet


PERMIT NO. 6531

Date: 9/8/92

Inspected by: Mike Eake

Environmental Health Specialist

Area installed deep (soil OK 18" under)
PUMP TO CONVI. REPAIR

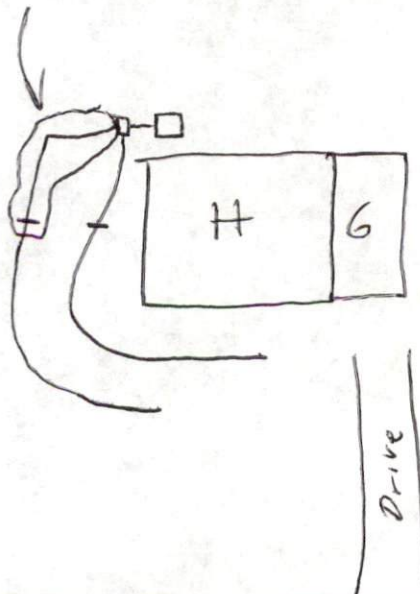

To 27 ← Rd
