

CERTIFICATE OF COMPLETION / OPERATIONAL PERMIT


Name: (owner) Steven Brian Johnson New Installation Septic Tank
 Property Location: SR# 1440 Repairs Nitrification Line
 Subdivision Twin Oaks Lot # 5
 Contractor: Jerry Stewart Registration # 10
 Basement with Plumbing: Garage:
 Water Supply: Well Public Community
 Distance From Well: 50 ft. min

Following are the specifications for the sewage disposal system on above captioned property.

Type of system: Conventional Other _____
 Size of tank: Septic Tank: 1000 gallons Pump Tank: _____ gallons
 Subsurface Drainage Field No. of ditches 3 exact length of each ditch 100 ft. width of ditches 3 ft. depth of ditches 18-24 in.
 French Drain: _____ Linear feet

PERMIT NO. 6925

Date: 04-15-93
 Inspected by: Jack H. Boyd R-5
 Environmental Health Specialist

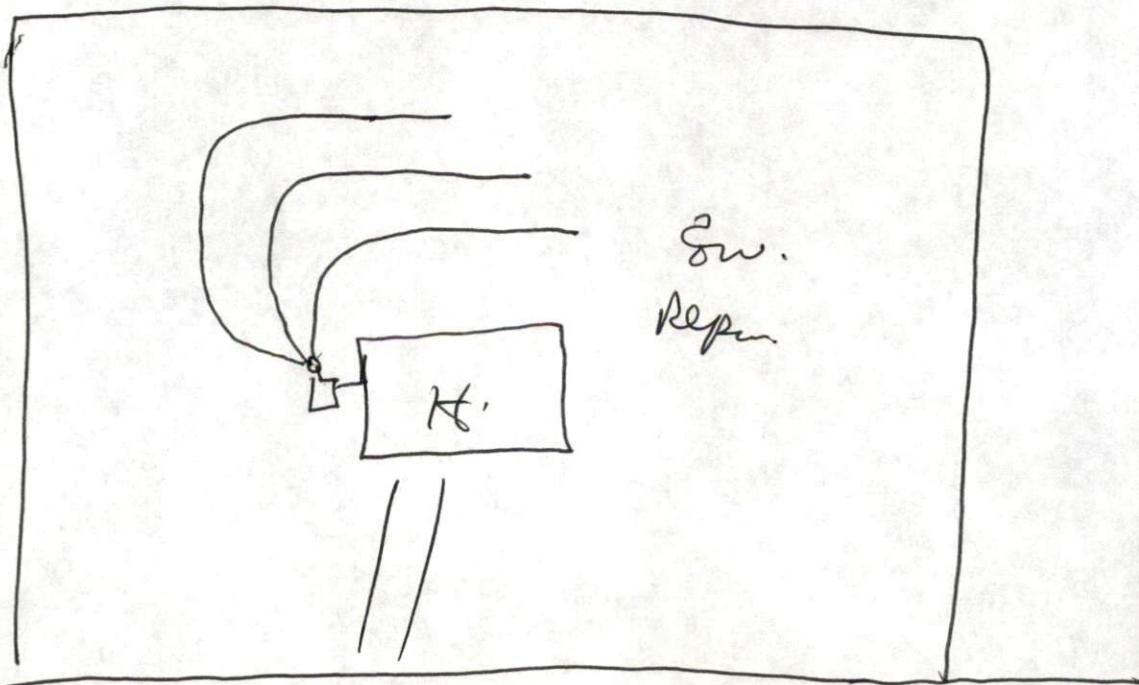

T> SR 1440 →
