


# CERTIFICATE OF COMPLETION / OPERATIONAL PERMIT

Name: (owner) Benson Building Supply     New Installation     Septic Tank  
Property Location: SR# 301     Repairs     Nitrification Line  
Subdivision \_\_\_\_\_ Lot # \_\_\_\_\_  
TAX ID# \_\_\_\_\_ Quadrant # \_\_\_\_\_  
Contractor: Larry Sharpe    Registration # 29  
Basement with Plumbing:     Garage:   
Water Supply:  Well     Public     Community  
Distance From Well: 100 ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system:  Conventional     Other pump to cond lines  
Size of tank: Septic Tank: 2 1000 gallons    Pump Tank: 1000 gallons  
Subsurface Drainage Field    No. of ditches 2    exact length of each ditch 250 ft.    width of ditches 3 ft.    depth of ditches 24 in.  
French Drain: \_\_\_\_\_ Linear feet

PERMIT NO. 7947    Date: 4-13-94  
Inspected by: Thomas J. Boye  
Environmental Health Specialist

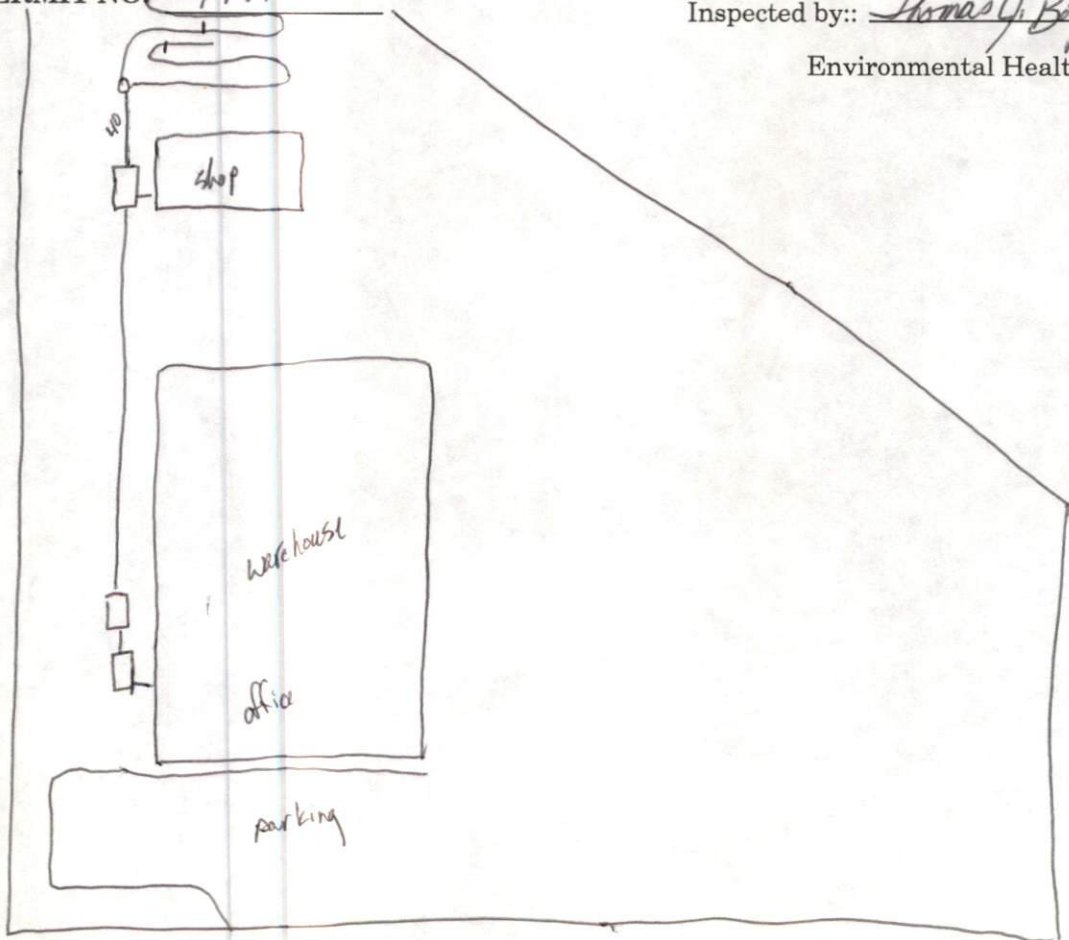

301 N → Benson
