

SOIL/SITE EVALUATION

for -SITE WASTEWATER SYSTEMOWNER: Stan + Ruby LyonAPPLICANT: Stan + Ruby LyonADDRESS: DwmlAPPLICATION DATE: 5-12-97DATE EVALUATED: 7-19-97PROPOSED FACILITY: Dwml PROPOSED DESIGN FLOW (.1949): SR 1131PROPERTY SIZE: 180 x 210LOCATION OF SITE: SR 1131PROPERTY RECORDED: WATER SUPPLY: ☐ Private ☒ Public ☐ Well ☐ Spring ☐ OtherEVALUATION METHOD: ☒ Auger Boring ☐ Pit ☐ CutTYPE OF WASTEWATER: ☒ Sewage ☐ Industrial Process ☐ Mixed

P R O F I L E #	.1940 LAND- SCAPE POSITION/ SLOPE %	HORI- ZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941)		OTHER PROFILE FACTORS				PROFILE CLASS & LTAR
			.1941 STRUCTURE/ TEXTURE	.1941 CONSISTENCE/ MINERALOGY	.1942 SOIL WETNESS/ COLOR	.1943 SOIL DEPTH	.1956 SAPRO CLASS	.1944 RESTR HORIZ	
1	0-1% L	0-16	SL to LS gr	VFR	Start 24" Heavy at 30"				PS
		16-30	SC sbk	F ₁					
2	0-1%	0-13	LS gr	VFR	20"				
		13-24	SC sbk	F ₁ to F ₂					
3	0-1%	0-16	LS gr	VFR	30"				
		16-30	SC sbk	F ₁					
4	0-1%	0-16	LS gr	VFR	24"				
		16-30	SC sbk	F ₁					

Soil wetness at 24 to 30"

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM	OTHER FACTORS (.1946):
Available Space (.1945)			SITE CLASSIFICATION (.1948): <u>PS</u>
System Type(s)			EVALUATED BY: <u>Jeff Endy</u>
Site LTAR	<u>.3</u>	<u>.4 to .3</u>	OTHER(S) PRESENT: <u>Sam</u>


12" deep ditches - EE-22 Lay System


$$\frac{10}{85} \frac{1}{5}$$



1.

$$\frac{75}{15} \frac{90}{10}$$

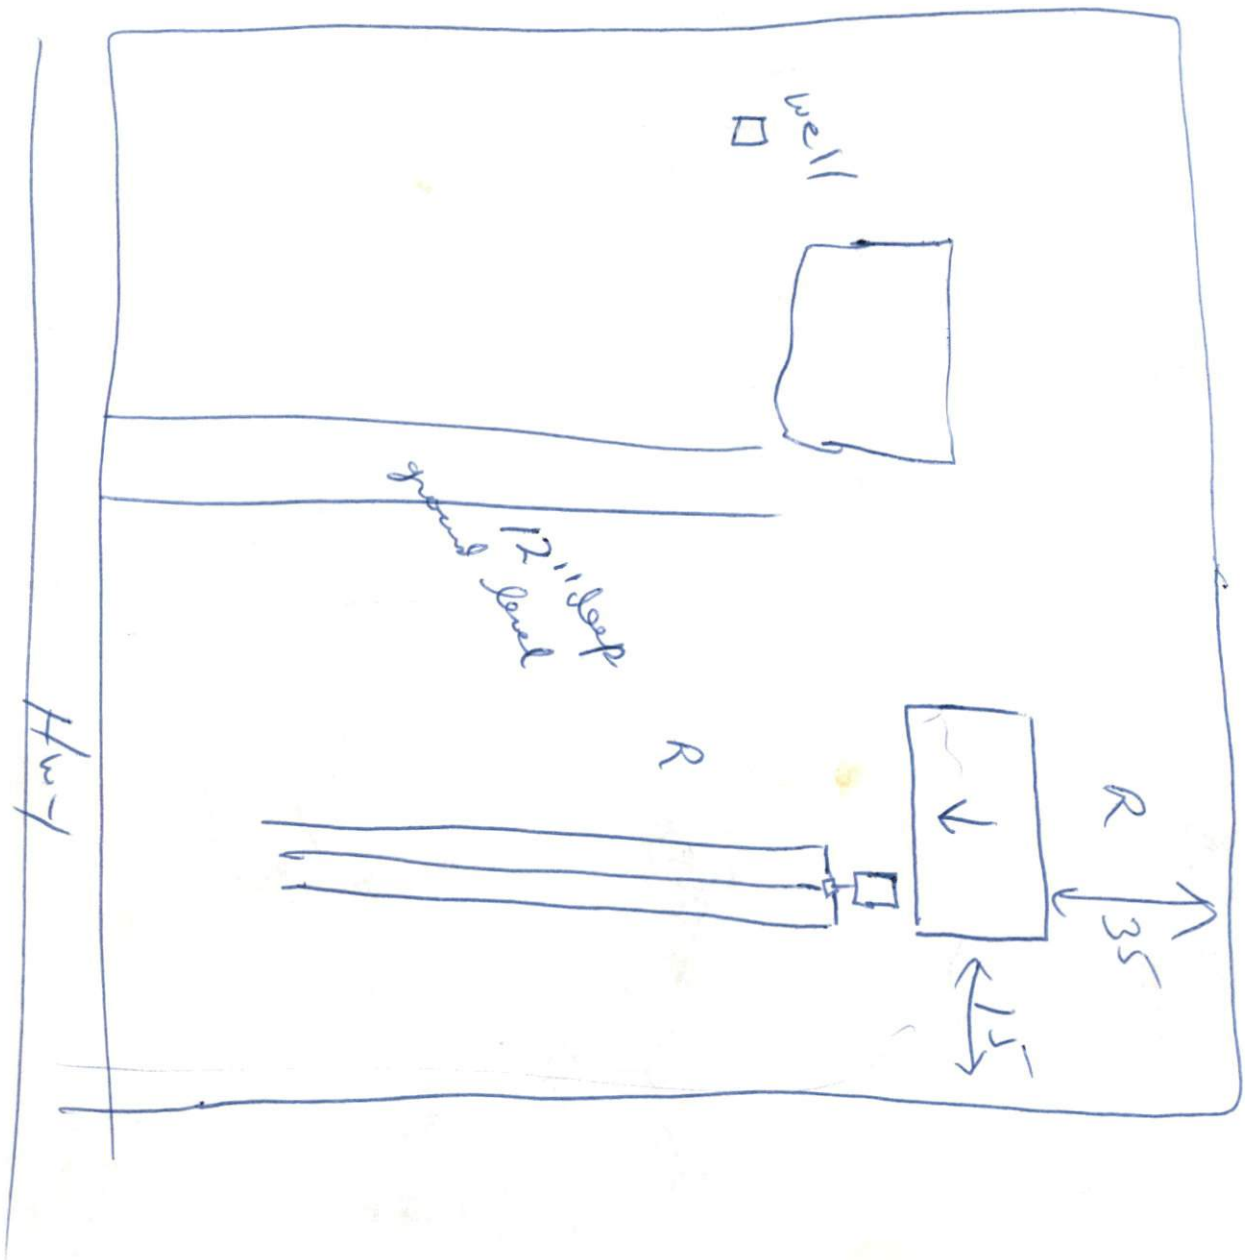

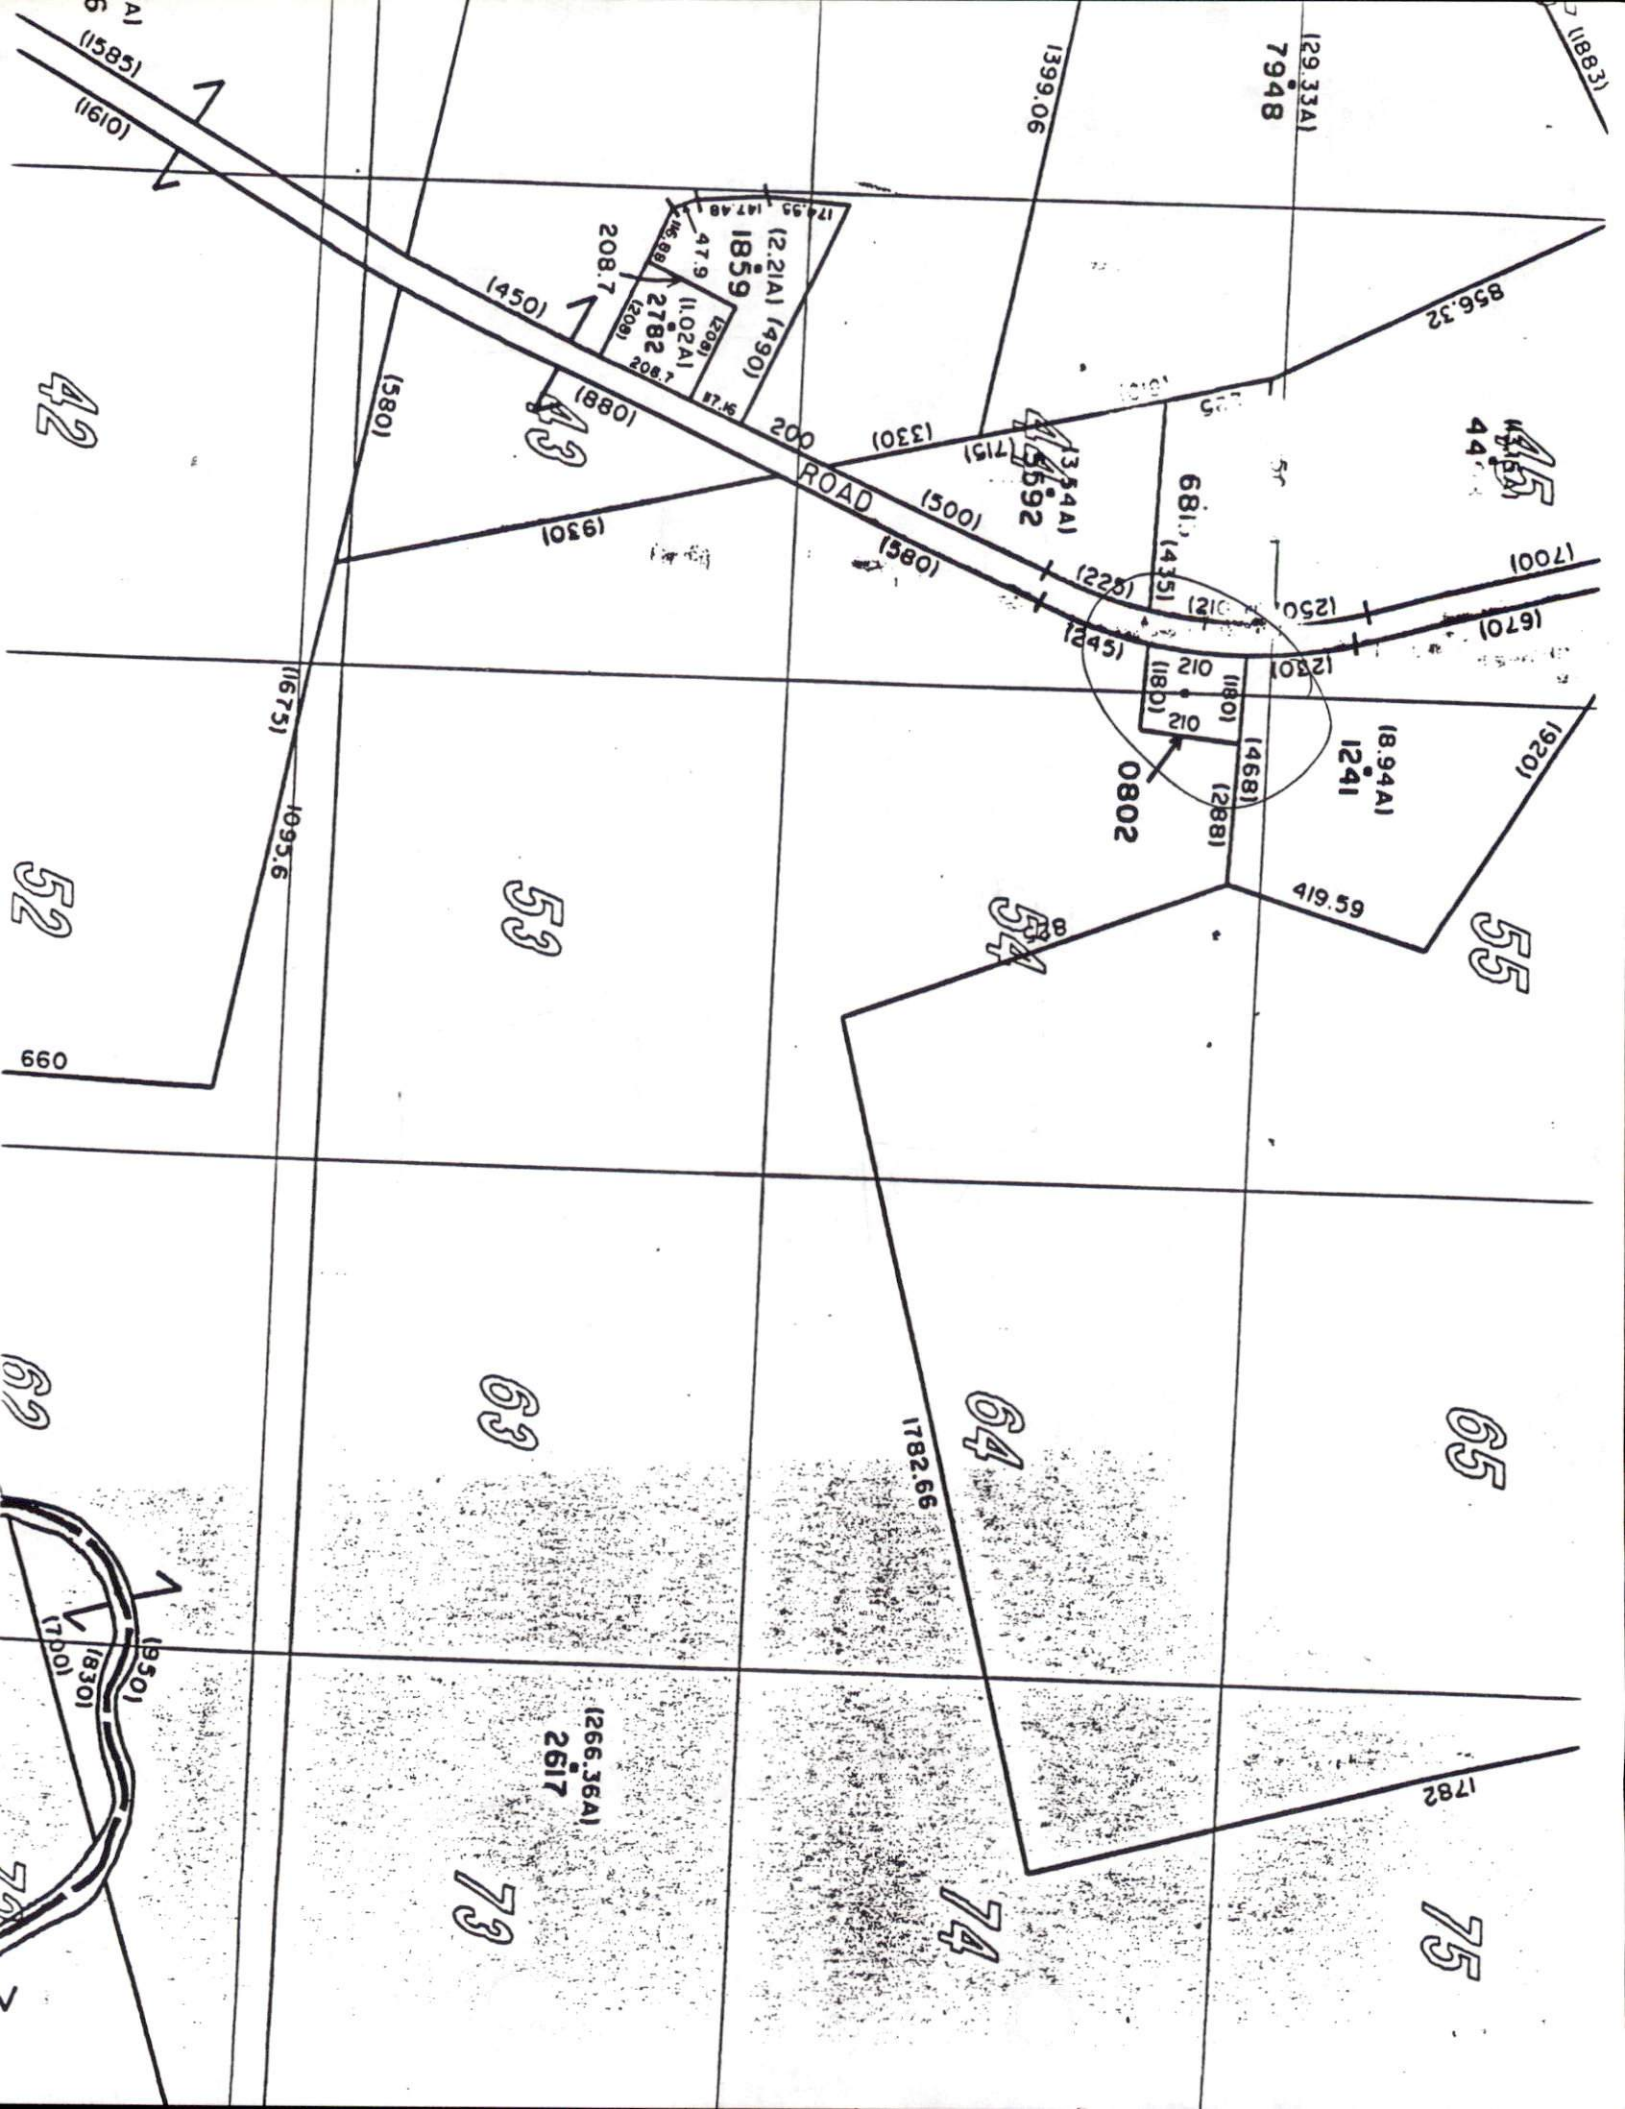


SITE PLAN APPROVAL

DISTRICT NA USE MH (28 x 40)

#BEDROOMS 3

Date 5-12-97 [Signature]
Zoning Administrator

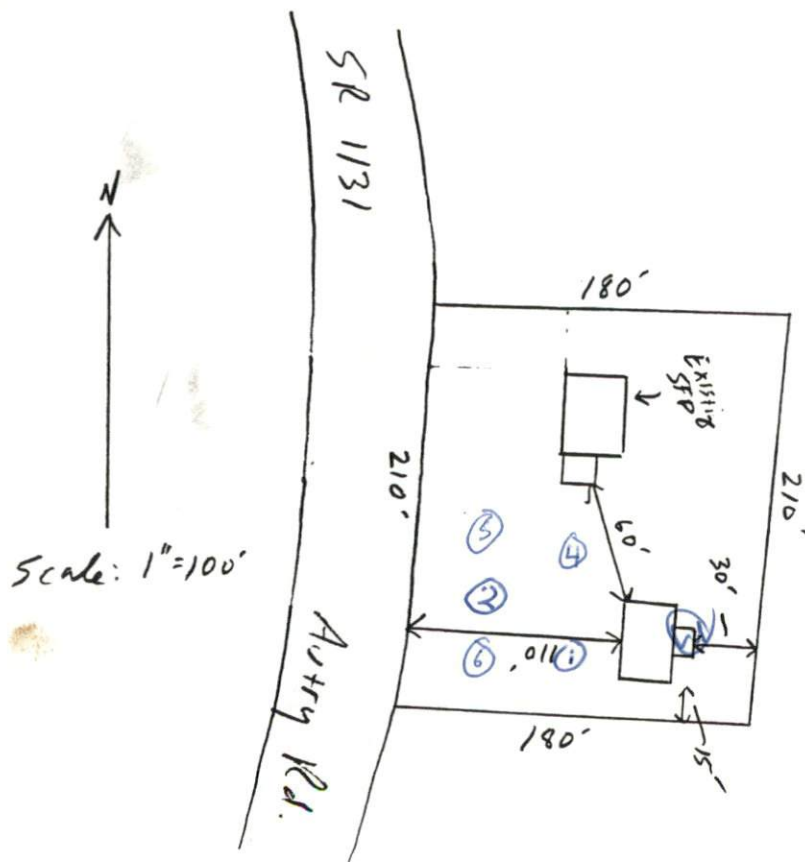

② 0-13LS
13-24 SC
mottles starting
at 20"

① 0-16 SK to LS
16-30 SC
mottles start at 24"
heavy at 30"

③ 0-16LS
16-30 SC
mottles at 30"
