

# OPERATIONS PERMIT

00-40000714


Name: (owner) Johnny Farcloth  New Installation  Septic Tank  
 Property Location: SR# 1270  Repairs  Nitrification Line  
 Subdivision Hollis Pines Lot # 2  
 TAX ID# \_\_\_\_\_ Quadrant # \_\_\_\_\_  
 Contractor: Johnny Farcloth Registration # \_\_\_\_\_

Basement with Plumbing:  Garage:   
 Water Supply:  Well  Public  Community  
 Distance From Well: 50 ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system:  Conventional  Other \_\_\_\_\_  
 Size of tank: Septic Tank: 1000 gallons Pump Tank: \_\_\_\_\_ gallons  
 Subsurface Drainage Field: No. of ditches 1 exact length of each ditch 500 ft. width of ditches 3 ft. depth of ditches 18 in.  
 French Drain: \_\_\_\_\_ Linear feet

PERMIT NO. 17924 Date: 11-9-2000  
 Inspected by: G. L. [Signature]  
 Environmental Health Specialist

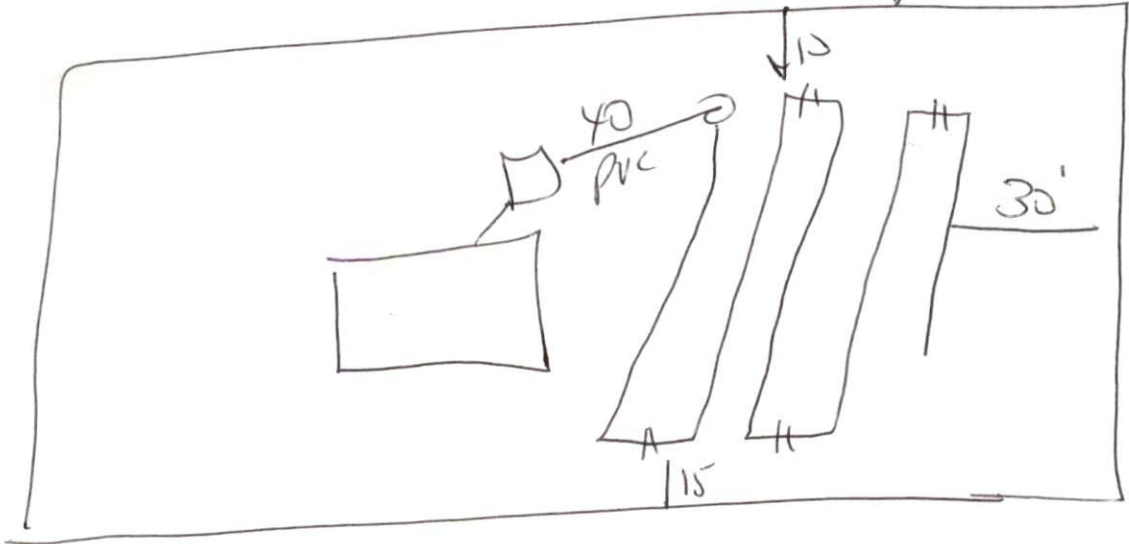

RL
