

HTE # 05-50011544

OPERATIONS PERMIT

Name: (owner) Pine Grove Dev. New Installation Septic Tank Repair

Property Location: SR# 1141 Nitrification Line Expansion
Subdivision Cherokee Ridge Lot # 13 Tax ID # _____ Quadrant # _____

Contractor: Ted Brown Registration # _____

Basement with Plumbing: Garage:

Water Supply: Well Public Community
Distance From Well: 50 ft.

Following are the specifications for the sewage disposal system on above captioned property.

Type of system: Conventional Other 25% Reduction System *Infiltrator 2nd ch chamber*
Size of tank: Septic Tank: 1000 gallons Pump Tank: _____ gallons


Subsurface Drainage Field No. of ditches 1 exact length of each ditch 200 ft. width of ditches 3 ft. depth of ditches 18-24 in.

French Drain Required: _____ Linear feet *1 chamber* Date: 6-3-05

PERMIT NO. 21921 Inspected by: Joe Wall

~~Proposed~~ *open ditch / Beam for diversion*

*57x1000
57D-103
24-05*

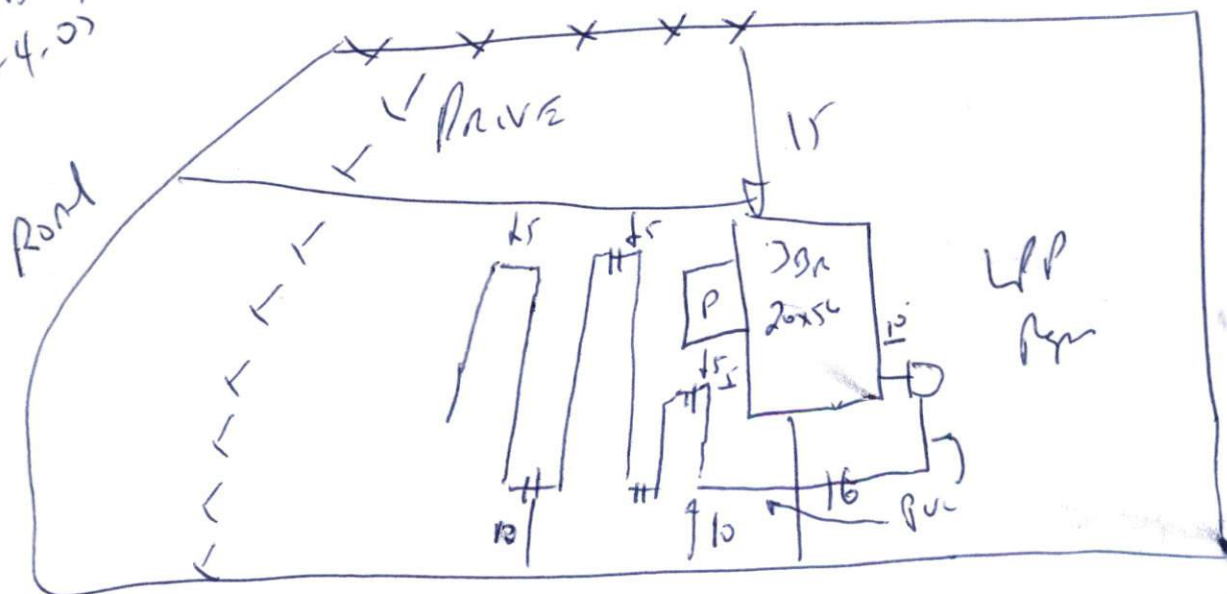

Needs - Beam & open Ditch checked
