

FIELD REPORT

Piedmont Geotechnical, Inc.
 1869 Jimmie Kerr Road
 Haw River, NC 27258
 Phone 336-578-8884
 Fax 336-578-8848
 336-516-8634



PROJECT LOT 23 CAMERON WOODS SUB	
LOCATION NWS W/ Box	
PERMIT #	JOB # 23PG-0203D
DATE 2-3-23	OWNER
WEATHER Wet Windy	TEMP 50°
CONTRACTOR ADAMS HOMES	
PRESENT AT SITE	

ADAMS HOMES


PRELIMINARY REPORT HARD COPY TO FOLLOW

A REPRESENTATIVE OF PIEDMONT GEOTECHNICAL ARRIVED ON-SITE 2-3-23 TO OBSERVE AND TEST THE FOLLOWING FOR THE ABOVE REFERENCED SITE. THE SUBGRADE SOILS WERE OBSERVED, PROBED AND TESTED USING A DCP. BASED ON THE OBSERVATIONS, PROBING AND TESTING THE SOILS IN THE UPPER 3 FT WERE ADEQUATELY COMPACT FOR 2000 PSF.

2 TAN CLAYSANDS TO SAND CLAYS

WITH AREAS OF THE LEFT, FRONT & REAR (LEFT FROM FRONT TO REAR) OF THE RT WALL AND APPROX 1/2 FT OR TWO REAR WALL @ LEFT REAR CORNER. THE SO AREAS WERE OVER EXCAVATED

2 TO 1.5 FT WITH CLEAN WASHES STOVE OVER FABRIC FROM BELOW

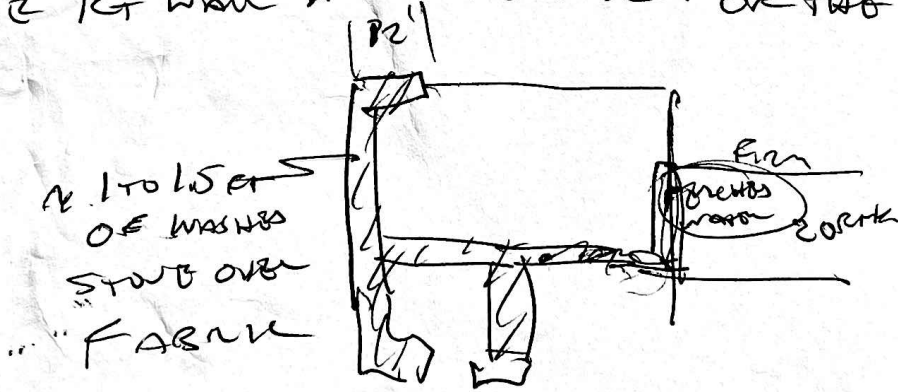

FRONT
