
Harnett County Department of Public Health

Improvement Permit

PROPERTY LOCATION: SN 1412 Christian (Ight RD)
ISSUED TO: DONALD + Kelle STEPHENS SUBDIVISION LOT #
NEW REPAIR EXPANSION Site Improvements required prior to Construction Authorization Issuance:
Type of Structure: SFD
Proposed Wastewater System Type: 25% DEDUCTION
Projected Daily Flow: 360 GPD
Number of bedrooms: Number of Occupants: max
Basement Yes Y No
Pump Required: No May be required based on final location and elevations of facilities
Type of Water Supply: Community Public Well Distance from wellfeet Permit valid for: Five years
Permit conditions: No expiration
2 11 1 LAT 178 HS
Authorized State Agent: Date: 4-21-23 SEE ATTACHED SITE SKETCH
The issuance of this permit by the Health Department in no way guarantees the issuance of other permits. The permit holder is responsible for checking with appropriate governing bodies in meeting their requirements.
site is subject to revocation of the site plan, plat, or the intended use changes. The Improvement Permit shall not be affected by a change in ownership of the site. This permit is subject to compliance with the provision the Laws and Rules for Sewage Treatment and Disposal and to conditions of this permit.
the cams and holes for semage realiment and disposal and to conditions of this perinte.
Construction Authorization
(Required for Building Permit)
The construction and installation requirements of Rules .1950, .1952, .1954, .1955, .1956, .1957, .1958, and .1959 are incorporated by references into this permit and shall be met. Systems shall be installed in accordance
with the attached system layout.
HOUSE TO DISCOLATE STRUCTS MODERNING # 1417 Christia 15-At R
ISSUED TO: DONALD + Keller STEPHENS PROPERTY LOCATION: SC 1412 Christian Land For the Subdivision LOT #
Basement? Yes No Basement Fixtures? Yes No
Type of Wastewater System** 1572 NETWOTON System (Initial) Wastewater Flow: 360 GPD
(See note below, if applicable)
Installation Requirements/Conditions Number of trenches
Septic Tank Size 1000 gallons Exact length of each trench 255' feet Trench Spacing: Feet on Center
Pump Tank Size / Doo gallons Trenches shall be installed on contour at a Soil Cover:inches
Maximum Trench Depth of:
(Trench bottoms shall be level to $\pm 1/4$ " 36" above the trench bottom)
in all directions)
Pump Requirements:ft. TDH vsGPMinches below p
Aggregate Depth: inches above
Conditions: Follow Consultants Cagost Aggregate Depth: 2 inches to
WATER LINES (INCLUDING IRRIGATION) MUST BE 10FT. FROM ANY PART OF SEPTIC SYSTEM OR REPAIR AREA.
NO UTILITIES ALLOWED IN INITIAL OR REPAIR DRAIN FIELD AREA.
**If applicable: I understand the system type specified is different from the type specified on the application. I accept the specifications of this permit.
Owner/Legal Representative Signature: Date:
This Construction Authorization is subject to revocation if the site plan, plat, or the intended use changes. The Construction Authorization shall not be transferred when there is a change in ownership of the site. This
Construction Authorization is subject to compliance with the provisions of the Laws and Rules for Sewage Treatment and Disposal and to the conditions of this permit.
2 11 / ATD RENS
Authorized State Agent: Date: 4-21-23
Authorized State Agent: Date: 4-21-23 Construction Authorization Expiration Date: 4-21-28

Harnett County Department of Public Health Site Sketch

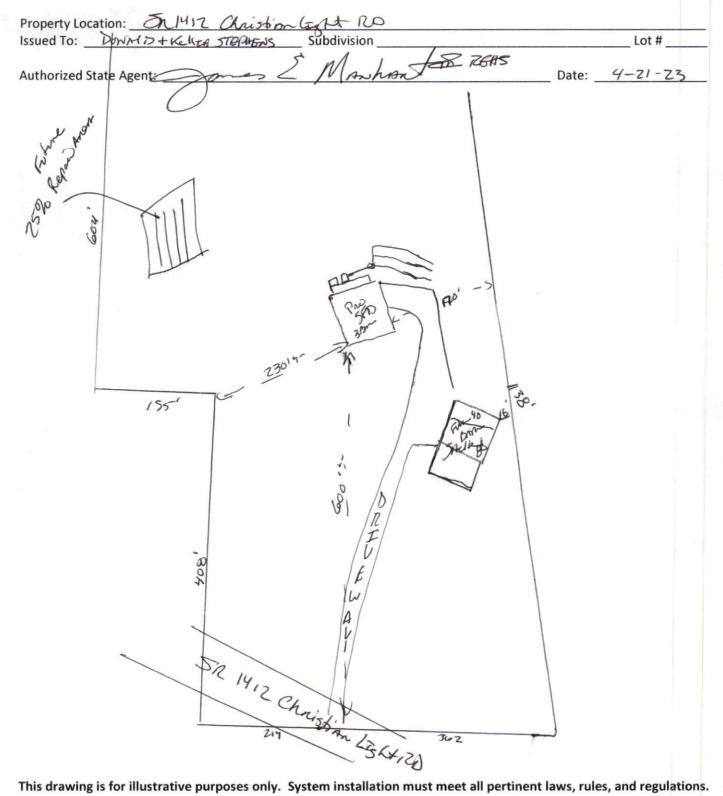

This drawing is for illustrative purposes only. System installation must meet all pertinent laws, rules, and regulations.
