



HAYES STRUCTURAL

Consulting & Design, PLLC

1501 Lakestone Village Ln. #103
Fuquay-Varina, NC 27526
NC Firm License No.: P-2854

Date: October 31, 2025

To: Cameron Hill
Hill Backhoe Service Inc.
3309 Roxbury Drive
Wake Forest, NC 27587

Re: 25-FTG-167
Footing Inspection
122 Gates Way
Sanford, NC 27332
Permit No.: SFD2503-0043

Mr. Hill:

At your request, a site visit was made to the above referenced single family residence under construction to inspect the footings prior to concrete placement.

The bottom of the footings was inspected and a mixture of firm residual sandy silt and sandy clay was encountered at depths ranging from one to five feet below grade. The over-excavated sections where soft soil and/or stumps were removed may have concrete placed at an increased thickness in lieu of washed stone replacement. The soil at the bottom of the footings will provide the minimum required bearing capacity of two thousand pounds per square foot.

Third party inspection revealed the footings for the single family residence were excavated per the approved plans with all concrete depths and step downs set correctly. The footings are in conformance with Chapter 4 of the 2018 North Carolina Residential Code and are suitable for concrete placement. The interior lug footing was not excavated at the time of our inspection and is to be incorporated into the slab. A 24"x24"x8" lug footing was excavated at each end of the garage door opening per our direction in lieu of a continuous footing through the opening per plan.

Please contact us if you have any questions.

Respectfully submitted,
Hayes Structural Consulting & Design, PLLC



Digitally signed by
Zachary H. Hayes,
PE

Date: 2025.10.31
12:33:29 -04'00'

Garrett Scott
Structural Engineering Technician
(919) 980-2756
garrett@hayesstructural.com

Zachary H. Hayes, PE
President & Principal Engineer
(919) 210-3480
zach@hayesstructural.com

Harnett COUNTY INSPECTIONS DEPARTMENT

3RD PARTY INSPECTION FORM

RECORD OF THE INSPECTION OF A COMPONENT OR ELEMENT BY A NC LICENSED ARCHITECT OR ENGINEER

Project Information:

Residential Single Family Project: ☒ Y ☐ N

Commercial Project: ☐ Y ☒ N

Code Enforcement Project No.:

Permit No.: SFD2503-0043

Project Name: 122 Gates Way

Owner: Lamco Custom Builders, LLC

Project Address: 122 Gates Way Sanford, NC 27332

Suite No.:

Date Inspected: 10/30/2025

Contractor Name: Lamco Custom Builders, LLC

Component Inspected: Footings for stem wall foundation

Responsible Licensed NC Architect or NC Engineer

Name: Zachary H. Hayes, PE

Firm Name: Hayes Structural Consulting & Design, PLLC

Phone No.: Office N/A

Mobile

Email Address: zach@hayesstructural.com

Mailing Address: 1501 Lakestone Village Ln. Ste. 103 Fuquay-Varina, NC 27526

APPLICABLE CODE SECTION: 2018 NCRC

2018 NCBC = 2018 NC Building Code; 2018 NCRC = 2018 NC Residential Code

Describe Element/Component/Type of Inspection: *


Inspection of footings prior to concrete placement to verify excavation per approved plans and in conformance with Chapter 4 of the 2018 NCRC. See sealed letter for additional information.

*(subgrade form/letter may also be required) Attestation/Signature:

By signing below, I certify that the component and/or element of the building as identified on this form has been inspected by me or someone under my direct supervision per subsection (b2) of NC G.S. 153A-352 and is in compliance with the Code or other proposal of the architect or engineer for the project. This inspection is in compliance with all of the requirements of the above referenced Code. Attach any additional documents if needed.

LICENSED ARCHITECT OR ENGINEER

Digitally signed by
Zachary H. Hayes, PE
Date: 2025.10.31
12:33:41 -04'00'

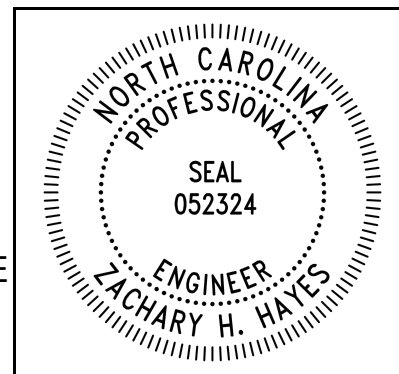

Inspection Department disclaimer:

Upon the receipt of a signed written document as required under subsection (a) of Article 160A-413.5., Code Enforcement shall be discharged and released from any liabilities, duties and responsibilities imposed by this article or in common law from any claim arising out of or attributed to the component or element in the construction of the building for which the signed written document was submitted. Be aware that this inspection will be noted in all inspection records including the Certificate of Occupancy or Certificate of Compliance. This inspection does not address any local ordinances or zoning requirements.
