

Load Calculation


Sq'	3012 x 3 VA = 9036
Small circuit	4500
HW	4500
Dryer	4000
DW	1500
Range	14,000

total kVA	37536
-	10000
<hr/>	
	27536
x	.40
	11014.4
+	10000
<hr/>	
	21014.4
+	9200
<hr/>	
	30214.40
	125.89
	126 A

Heat

Harold H Co Inspection

Thomas Galloway
576 Tiszah Dr
910-261-0269

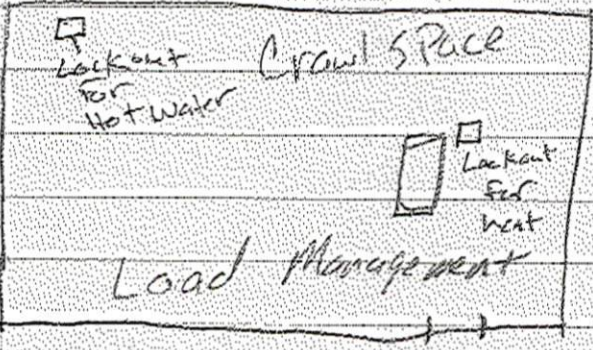

Harmon's Electric & Home Improvement Inc.
800 Vernon Street, Broadway NC 27505
919-353-8982 | [REDACTED]

fax

TO:	INSPECTOR GUY	FROM:	Frank Harmon
<hr/>			
FAX:	910-893-2793	PAGES:	2
<hr/>			
PHONE:	910-893-7525	DATE:	4/2/2020
<hr/>			
RE:	LOAD CALCAULATION FOR THOMAS GALLOWAY ,576 TIRZAH DR. 910-261-0269	CC:	[Names]
<hr/>			

- Urgent
- For Review
- Please Comment
- Please Reply
- Please Recycle

Comments: Please contact me at 919-498-4321 if you have any questions.

Thank You,

Frank Harmon
