

SOUTHEASTERN SOIL & ENVIRONMENTAL ASSOC., INC.

PROPOSED SUBSURFACE WASTE DISPOSAL SYSTEM DETAIL SHEET

SUBDIVISION: Liberty Meadow  
pump to

INITIAL SYSTEM: APPROVED 25% REDUCTION

DISTRIBUTION: SERIAL OR P-Box  
OR BENCH

BENCHMARK: 100.0

NO. BEDROOMS: 3

LOT 32 → 32

REPAIR Approved 25% Reduction  
pump to

DISTRIBUTION SERIAL OR D-Box

LOCATION No Bench

LTAR 0.4 gpd/ft<sup>2</sup>

LINE	FLAG COLOR	ELEVATION	LENGTH
1	0	100.17	90
2	W	100.00	90
3	R	100.00	90
			270 AVAIL

4	Y	99.17	90
5	B	98.75	90
6	0	98.33	90
			270 AVAIL

BY B.C. Raynor

TYPICAL PROFILE

0-13 LS vfr gran  
13-36 SCL firm SBK  
Pm CA2 233"

DATE 01/14/2022


THERE SHALL BE NO GRADING,  
CUTTING, LOGGING OR OTHER SOIL  
DISTURBANCE IN SEPTIC AREA

HEALTH DEPARTMENT USE ONLY.

DESIGNS DO NOT GUARANTEE FUNCTIONALITY

32  
 Liberty Meadow  
 Lot 30 & 31 → 33

Pump PERSIA TO  
 0 space (seems for 42/43)  
 Behind 42/43

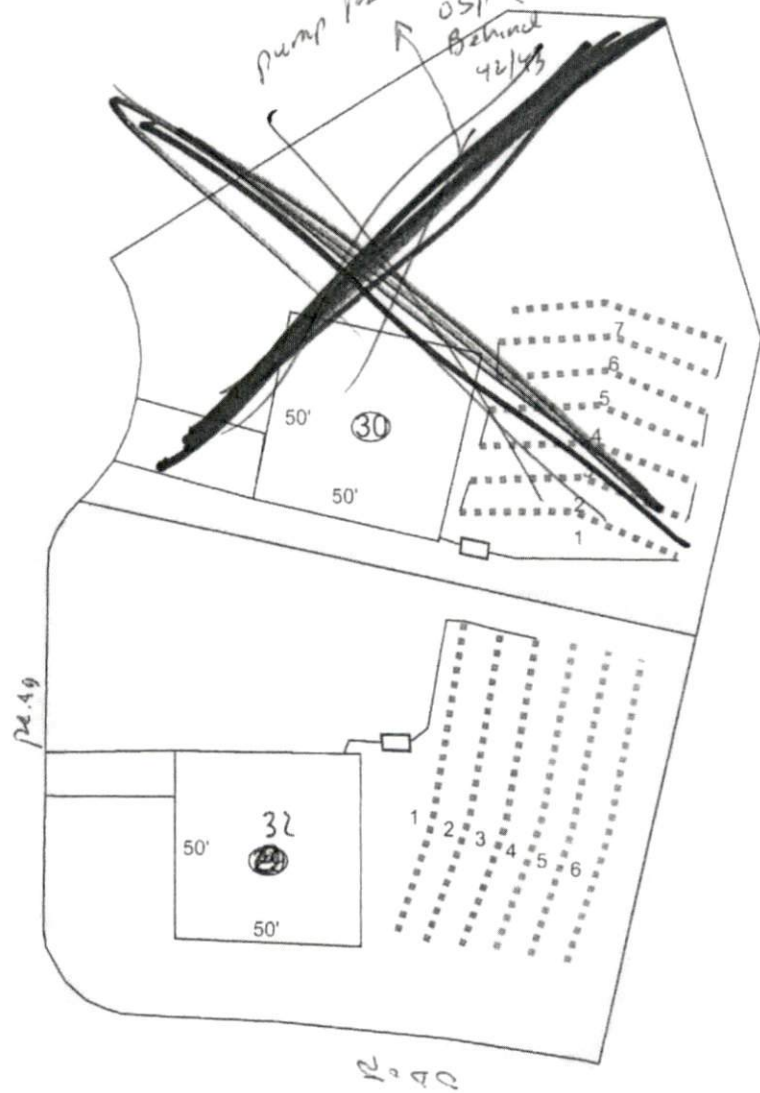

33 = need  
 new lawn!

32 : 50' deep  
 @ unlimited width
