HTE# 12-5-28585

Harnett County Department of Public Health

PERMIT # 26837

Operation Permit

22289

☑ New Installation ☑ Septic Tank ☑ Nitrification Line ☐ Repair ☐ Expansion

PROPERTY LOCATION: 321429 Chalybeate Rd

Name: (owner) STEPHENSON Builders SUBDIVISION Deerfield LOT # 34

System Installer: Adcock Excavation Registration # _____

Basement with plumbing: ☐ Garage ☑ Number of Bedrooms 3

Type of Water Supply: ☐ Community ☑ Public ☐ Well Distance from well _____ feet

System Type: Manufactured 25% Reduction system Type III B Types V and VI Systems expire in 5 years.

(In accordance with Table V a) Owner must contact Health Department 6 months prior to expiration for permit renewal.

This system has been installed in compliance with applicable North Carolina General Statutes, Rules for Sewage Treatment and Disposal, and all conditions of the Improvement Permit and Construction Authorization.

System installed as permitted.

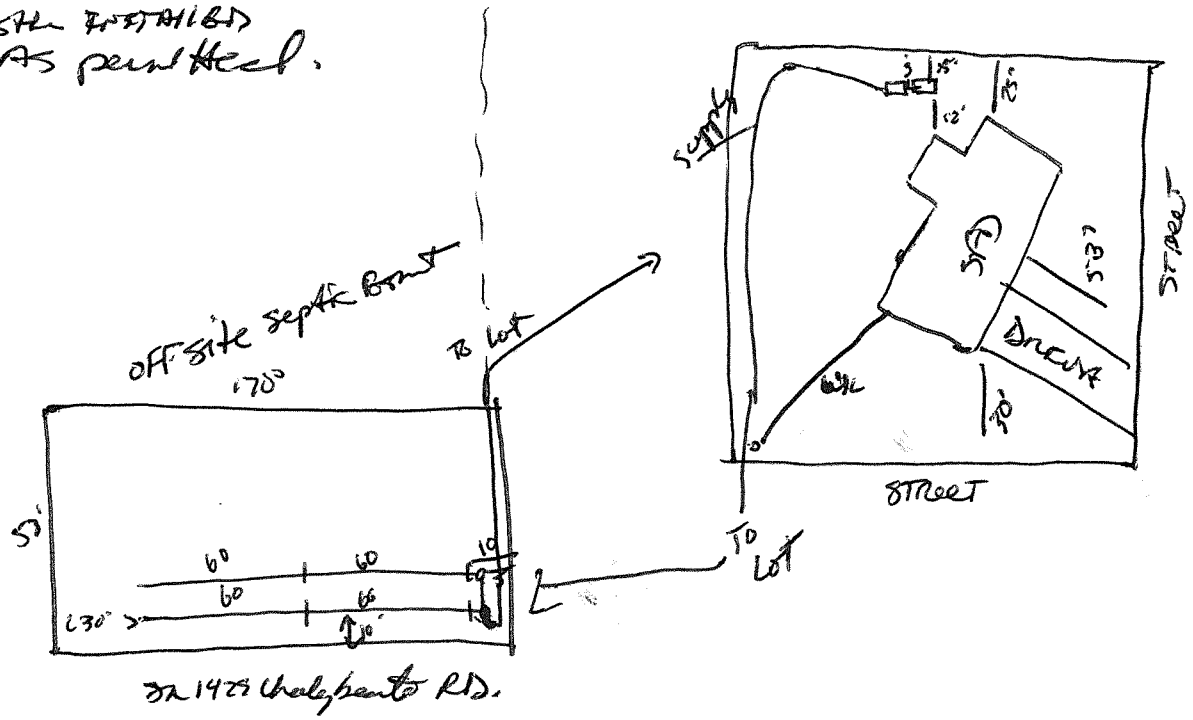

PERMIT CONDITIONS:

I. Performance: System shall perform in accordance with Rule .1961.

II. Monitoring: As required by Rule .1961.

III. Maintenance: As required by Rule .1961. Other: _____

Subsurface system operator required? Yes ☐ No ☐

If yes, see attached sheet for additional operation conditions, maintenance and reporting.

IV. Operation: _____

V. Other: _____

☐ _____ D-Box ☐ _____ Pump ☐ _____ Alarm ☐ _____ H2OLine ☐ _____ PWR Line

Following are the specifications for the sewage disposal system on the above captioned property.

Type of system: ☐ Conventional ☐ Other 25% Reduction System Type III B Septic Tank: 1000 gallons Pump Tank: 1000 gallons

Subsurface Drainage Field: No. of ditches 2; exact length of each ditch 120 feet; width of ditches 3 feet; depth of ditches 24 inches

French Drain Required: _____ Linear feet

Authorized State Agent James E Mann III REHS Date 8-3-12
