SOUTHEASTERN SOIL & ENVIRONMENTAL ASSOC., INC.

PROPOSED SUBSURFACE WASTE DISPOSAL SYSTEM DETAIL SHEET

SUBDIVISION: Summerlin

LOT 37

INITIAL SYSTEM: Gravity APPROVED 25% RECUCTION

REPAIR Gravity Approved 25% Reduction

DISTRIBUTION: D-Box

DISTRIBUTION D-Box

BENCHMARK: 100.0

LOCATION BC Lot Iron 36/37

NO. BEDROOMS: 4

LTAR 0.4 gpd/Ft²

	LINE	FLAG COLOR	ELEVATION	LENGTH
I	1	W	105.00	60
	2	P	104.50	60
	3	W	104.08	60
	4	P	103.67	60
	5	W	103.00	60
				300
R	6	P	102.50	60
	7	W	101.83	60
	8	P	101.17	60
	9	W	100.91	60
	10	P	100.50	60
				300

BY B.C. Raynor

DATE 07/09/2018

TYPICAL PROFILE

0-12 LS vfri gran

12-36 SCL firm SBK

CR2 >32"

THERE SHALL BE NO GRADING, CUTTING, LOGGING OR OTHER SOIL DISTURBANCE IN SEPTIC AREA

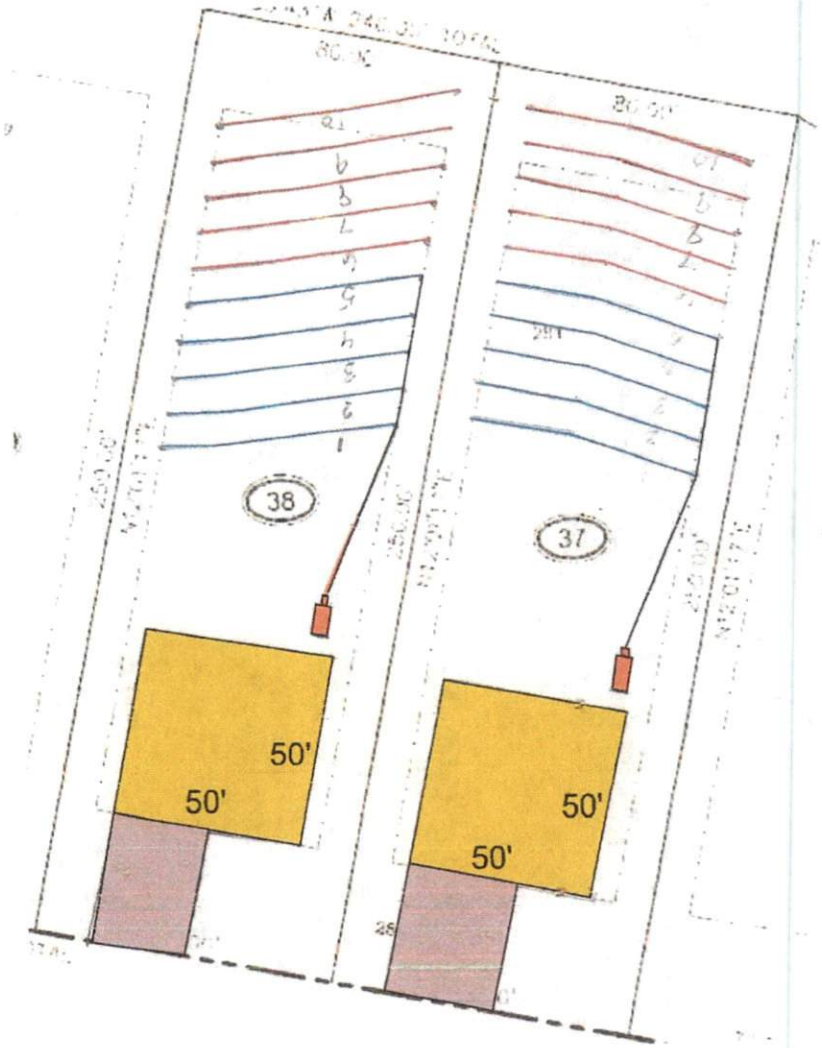
38
37
50'
50'
50'
50'
