Harnett County Department of Public Health

PERMIT # SFD2103-0029

Operation Permit

☒ New Installation ☒ Septic Tank ☒ Nitrification Line ☐ Repair ☐ Expansion

PROPERTY LOCATION: 228 NEGAL CREST DR. (RIVER RD.)

Name: (owner) ~~NC CUSTOM HOMES~~ NC CUSTOM HOMES SUBDIVISION NEGAL CREST LOT # 9

System Installer: JASON MATTHEWS

Basement with plumbing: ☐ Garage ☒ Number of Bedrooms 4

Type of Water Supply: ☐ Community ☒ Public ☐ Well Distance from well NA feet

System Type: 25% REDUCTION SYSTEM IIIB Types V and VI Systems expire in 5 years.

(In accordance with Table V a) Owner must contact Health Department 6 months prior to expiration for permit renewal

This system has been installed in compliance with applicable North Carolina General Statutes, Rules for Sewage Treatment and Disposal, and all conditions of the Improvement Permit and Construction Authorization.

* PUMP TO MEDIUM D-BOX EQUAL DISTRIBUTION
* SYSTEM SHIFTED TO PUMP DUE TO PLUMBING LOCATION

INSTALL BY [signature]

* INSTALL: 09/13/2021

Pump + Alarm By JM 12-16-21

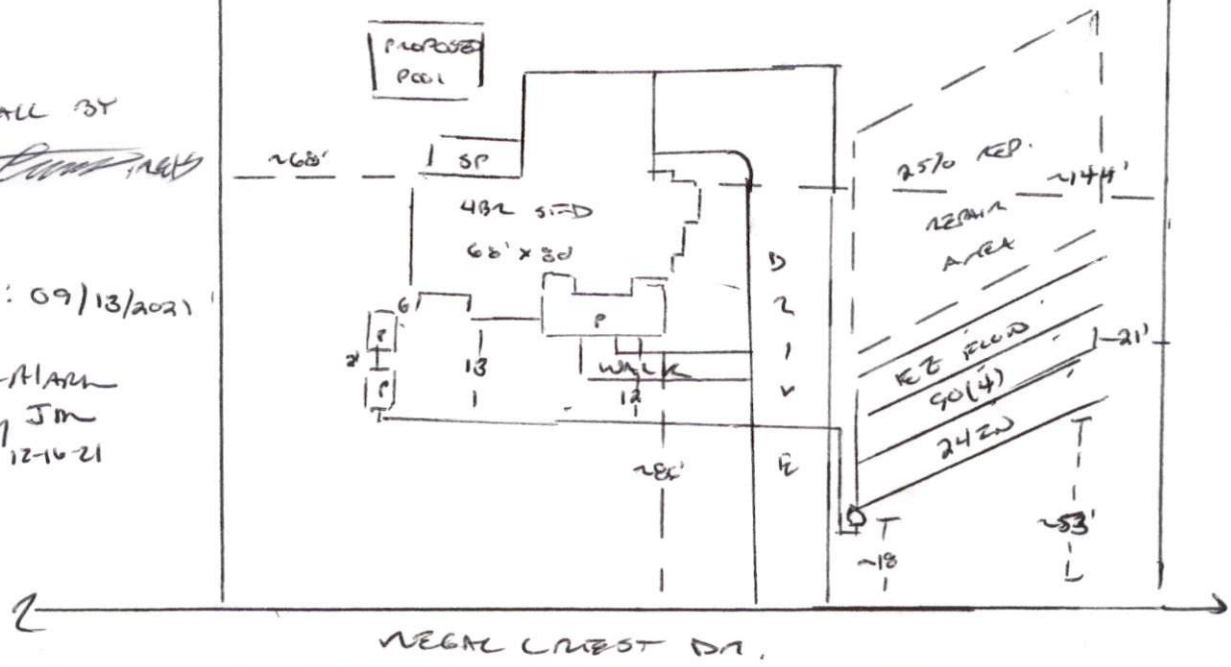

PERMIT CONDITIONS:

I. Performance: System shall perform in accordance with Rule .1961.

II. Monitoring: As required by Rule .1961.

III. Maintenance: As required by Rule .1961. Other: _____

Subsurface system operator required? Yes ☐ No ☐

If yes, see attached sheet for additional operation conditions, maintenance and reporting.

IV. Operation: _____

V. Other: _____

☐ _____ D-Box ☐ _____ Pump ☐ _____ Alarm ☐ _____ H2OLine ☐ _____ PWR Line

Following are the specifications for the sewage disposal system on the above captioned property.

Type of system: ☐ Conventional ☒ Other EZ FLOW IIIB Septic Tank: 1250 gallons Pump Tank: 1250 gallons

Subsurface Drainage Field: No. of ditches 4 exact length of each ditch 90 feet width of ditches 3 feet depth of ditches 24 inches

French Drain Required: _____ Linear feet

Authorized State Agent [signature] Date 12-16-21
