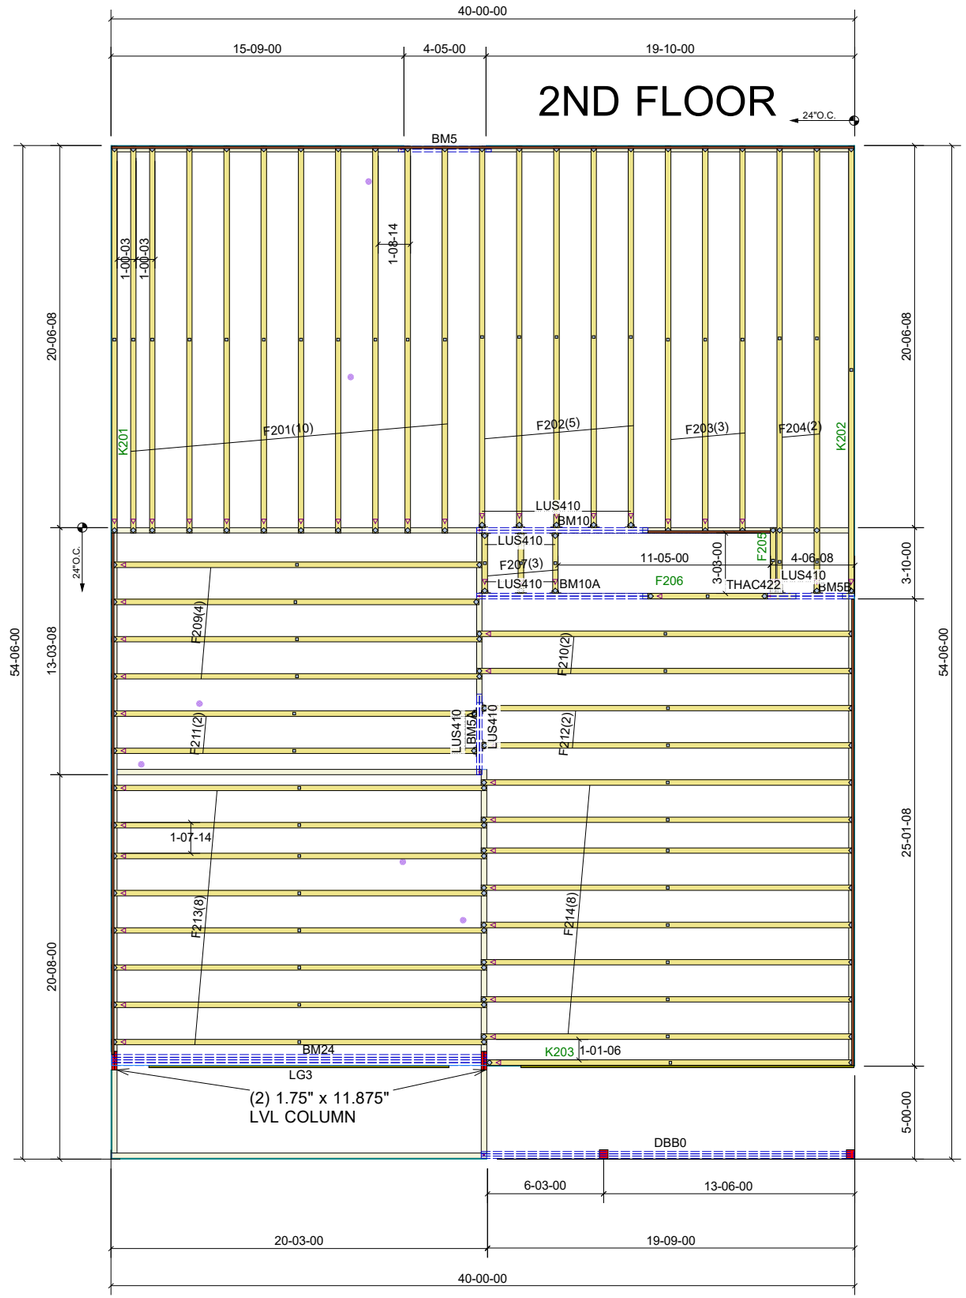

Truss Connector Total List		
Manuf	Product	Qty
Simpson	LUS410	17
Simpson	THAC422	1

Products				
PlotID	Length	Product	Plies	Net Qty
BM5	5-00-00	1 3/4" x 9 1/4" 2.0E LVL	2	2
BM10	10-00-00	1 3/4" x 14" 2.0E LVL	2	2
BM10A	10-00-00	1 3/4" x 14" 2.0E LVL	2	2
BM5A	5-00-00	1 3/4" x 14" 2.0E LVL	2	2
BM5B	5-00-00	1 3/4" x 14" 2.0E LVL	2	2
BM24	24-00-00	1 3/4" x 24" 2.0E LVL	4	4
COL LVL	10-00-00	1 3/4" X 11 7/8" LVL	2	2

SHOP DRAWING APPROVAL

THIS LAYOUT IS THE SOLE SOURCE FOR FABRICATION OF TRUSSES AND VOIDS ALL PREVIOUS ARCHITECTURAL OR OTHER TRUSS LAYOUTS. REVIEW AND APPROVAL OF THIS LAYOUT MUST BE RECEIVED BEFORE ANY TRUSSES WILL BE BUILT. VERIFY ALL CONDITIONS TO INSURE AGAINST CHANGES THAT WILL RESULT IN EXTRA CHARGES TO YOU.

REVIEWED BY: APPROVED BY: DATE:

THIS IS A TRUSS PLACEMENT DIAGRAM ONLY

These trusses are designed as individual building components to be incorporated into the building design at the specification of the building designer. See individual design sheets for each truss design identified on the placement drawing. The building designer is responsible for temporary and permanent bracing of the roof and floor system and for the overall structure. The design of the truss support structure including headers, beams, walls, and columns is the responsibility of the building designer. For general guidance regarding bracing, consult "Bracing of Wood Trusses" available from the Truss Plate Institute, 583 D'Onifrio Drive; Madison, WI 53179.

Carolina Structural Systems
Roof Trusses • Floor Trusses • EWP
Carolina Structural Systems
P.O. Box 157, Ether, NC 27247
225 Frame Shop Rd., Star, NC 27356
910-491-9004

Job #: Q2201201 NEALY 23-17-09

Customer: Value Build Homes

Site Address: 754 BENHAVEN SCHOOL RD.

City, ST, ZIP: SANFORD, NC, 27332

Plan: GREEN-A

Date: 04/08/2022

Sales Rep:SL

Designer: JSP
